


Gateway to Excellence

# St. Louis Oversight Committee Meeting Corps Update

14 JULY 2006



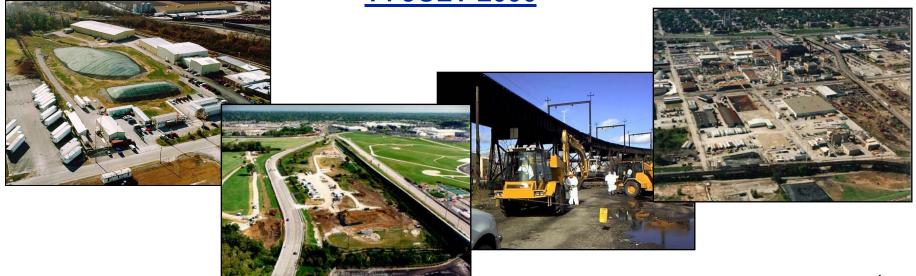

# **Agenda**



- Mississippi Valley Division
- Progress Report
- North County ROD
- Community Interactions
- Taskers
- Questions



# Mississippi Valley Division



Gateway to Excellence





### St. Louis Downtown Site (SLDS)



Gateway to Excellence

#### Remedial Actions

- Gunther Salt (South): COMPLETED 6 JUNE. (690 cy remediated) Asphalt work remains.
- MI Plant 6W Railspur:
  - RA COMPLETED 5,000 cy excavated.
  - Installation of rail line scheduled for later in July.
- MI Plant 7 N/S:
  - 7S: COMPLETED
  - 7N; COMPLETED 31 MARCH. Haz.Mat. Handling Bldg. Perimeter Remediation In-Progress.
- MI West (3, 8, 9, 11 and MI Parking Lot):
  - Plant 9 remediation initiated.
  - MI Security Gate remediation initiated.

#### Releases Pending

- Properties West of Broadway.
- Thomas & Proetz.

#### Remedial Designs and Investigations

- PSC Metals (DT-8) RAWD; e/o July.
- Properties South of Anglerodt; Complete
- 2 properties require clean-up (Christiana and Norfolk)
- Others to be released. Documents are being prepared.
- SLDS Rail Shipments in FY05: 7,700 cy shipped this FY (FY06 milestone 3,500 cy)<sub>4</sub>
  - +8,000 cy Stockpiled onsite





# St. Louis Airport Site (SLAPS)

- Shipping: On temporary hold May resume pending availability of funds
- Phase 6 Work In-Progress
  - ☐ Excavating in PUs (Progress Units) 57-58 [as-scheduled]
  - ☐ Final Status Survey Confirmation in SU (Survey Unit) 71 [on schedule]
  - ☐ Stockpiling as planned
  - ☐ Water Management / Dust Control; routine, as required
  - ☐ MSD Discharge Permit; 2-year extension granted (for both SLAPS/SLDS)
- SLAPS Activities Completed
  - McDonnell/Banshee RR Signal Upgrade Support
     [@ East End of SLAPS]; 390 cy of contaminated material removed
  - SLAPS Rail Shipments in FY06: +68,400 cy shipped.



# Latty Avenue Properties and SLAPS VPS



North County USACE prioritization in-progress

#### Latty Avenue Properties

- HISS/Futura; Pre-Design Investigation [PDI] Summary Report- USACE review.
- VPs 1L, 8C and 40a Parcel; PDI Report pending.
- VP-2L; PDI Work Plan being prepared.
- GIFREHC (VP-2L); Responding to claims for reimbursement.


#### SLAPS VP's

- VPs 17, 18, 19, 20, 20A and 25; PDIR /Final Status Survey Evaluation being prepared.
- VP-26; Replying to Landowner's request for information.
- IAs 12 + 13 (southside of SLAPS along Banshee Rd.); Preparing PDIR.
- Property along Coldwater Creek; Responding to Request for Information (no rad. problems anticipated).



# Volume Removed Using Environmental Documents



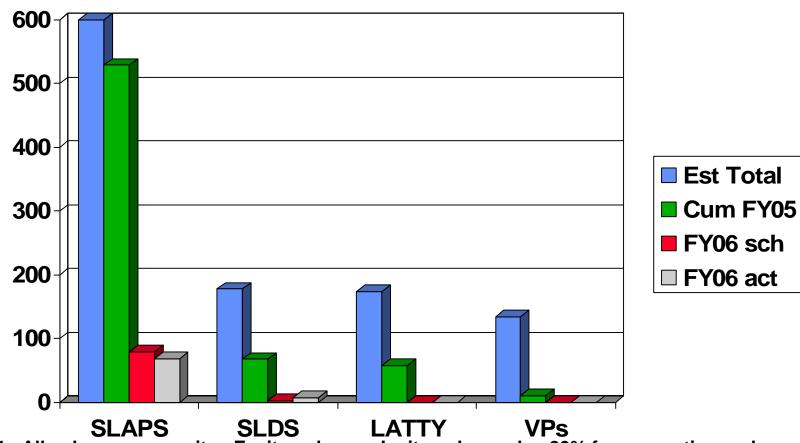

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles



# **Community Interactions**



Gateway to Excellence

#### Recent Events

- □ Presentation for N/S Railway Workers 5 May.
- □ Annual Utility Support meeting held 11 July.
- □ NEWSLETTER (Spring 2006) Issued.



### **Taskers**




#### Old Taskers

✓ USACE to schedule a time w/DOE Office of Legacy Mgmt. to brief on Long-Term Stewardship; 11 MAY.

#### New Taskers



## **Questions**



Gateway to Excellence

Questions?

Questions? Questions?

Questions?

Questions?

Questions? Questions?

Questions?

Questions?
ons?

**Questions?** 

10
