


# **FUSRAP**



# St. Louis Oversight Committee Meeting Corps Update

8 JANUARY 04

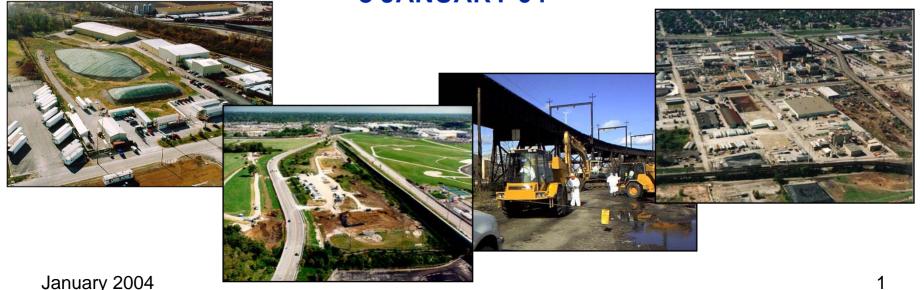



### **Agenda**




- Mississippi Valley Division
- Progress Report
- North County ROD
- Community Interactions
- Taskers
- Questions



### **Mississippi Valley Division**



Gateway to Excellence

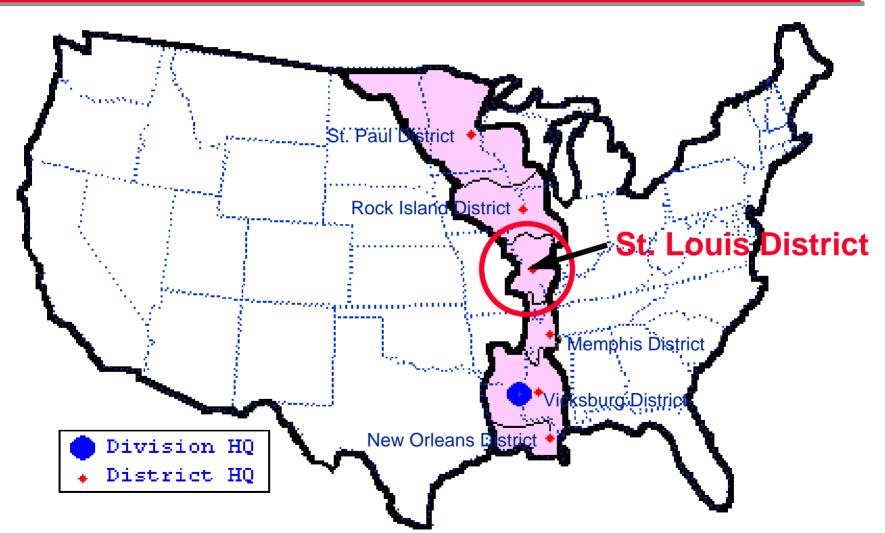



# Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- Pre-Remedial Investigation: Walkovers of west of Broadway nearly complete. 3 remain
- Remedial Design
  - Pre Design Investigation Conducting historical reviews at VP's and completed sampling a
    portion of Plant 6W. We are currently working on MI Plant 7 N/S. Additional samples have been
    collected from Thomas and Proetz property and will be incorporated into the report.

#### Remedial Action

- **Plant 1 3,724 cyds remediated -** Post Remedial Action Report internal review comments are being addressed. Next step will be regulator review.
- VP's
  - Midwest Waste The RAS (Remedial Action Summary Report) is complete will be grouped in a PRAR with Heintz Steel
  - **Heintz Steel** Remediation was completed in SEP, 1,663 cyds removed. The RAS is under internal review.
  - McKinley Bridge RA is currently ongoing 1,375 cyds expected, 1,961 cyds removed to date. Last area (south of bridge) in final status survey.
- Plant 6E / 6E1/2 22,958 cyds remediated
  - The RAS is complete and the contractor is working on the PRAR. Internal review is next.
- MI Plant 7E RA was completed in SEP, 1,319 cyds removed. Area is backfilled, RAS under internal review of RAS complete. Contractor working on the PRAR.
- Rail Shipments off SLDS
  - 2,052 cyds shipped / 10,000 planned



### Progress Report



## Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS

#### HISS / Latty Avenue

- Support for FUTURA asset purchase (Scanning equipment for transfer) completed.
  - · Report to be issued
- Rail Shipments off HISS
  - 0 cyds planned in FY04

#### SLAPS VP's

- Data Evaluation
  - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
- Characterization
  - Ongoing for VP's
- Designs are on hold and expected to be completed in FY04
  - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
- MSD support in FY04 Sewer line project along Eva and Frost next FY
- Property Owner Support Support for VP 4C / 5C likely in MAR 04
- Rail Shipments from VP's
  - 0 cyds planned in FY04, 35 cyds shipped to date



# Progress Report St. Louis Airport Site (SLAPS)



- Remedial Design Complete for SLAPS
  - Work Descriptions for Phases 4 / 5 and Phase 6 Errata sheets for Designs forwarded to regulators
- Removal Actions
  - Phase II/III (IA-2/3) excavation Continues. 75,000 cyds expected
    - Approximately 60,000 cyds have been excavated to date
    - This Phase consists of 10 Survey Units 6 complete to date.
  - Status of Corps Proposal to MDNR for Selenium (Se) discharge limits
    - Developed and sent responses to MDNR Water Pollution Control Program. Draft responses have been prepared and are being reviewed at MDNR.
    - In the interim we continue to treat water to MSD standards and use Best Management Practices (dust suppression, lined excavations, etc..)
  - Rail Shipments off SLAPS
    - 25,500 cyds shipped to date / 85,000 planned.



# Progress Report Other Issues



#### Bi-Annual Utility Meeting

Next meeting scheduled for 13 JAN

#### Long Term Stewardship -

- Meeting was held 6 November
  - Currently reviewing draft Overlay Ordnance proposal (Not been through internal USACE review).
  - Next meeting to be scheduled for late-February.
- North County Haul Road information will be issued for regulator review.


#### DoE Program POC's interactions -

- None during this timeframe
- CERCLA 5 year Review for all St. Louis FUSRAP Sites
  - USACE is working on the response to regulator comments
- E&W Bill -
  - Expect all remaining site funding to be received by mid to late JAN



# Volume Removed Using Environmental Documents



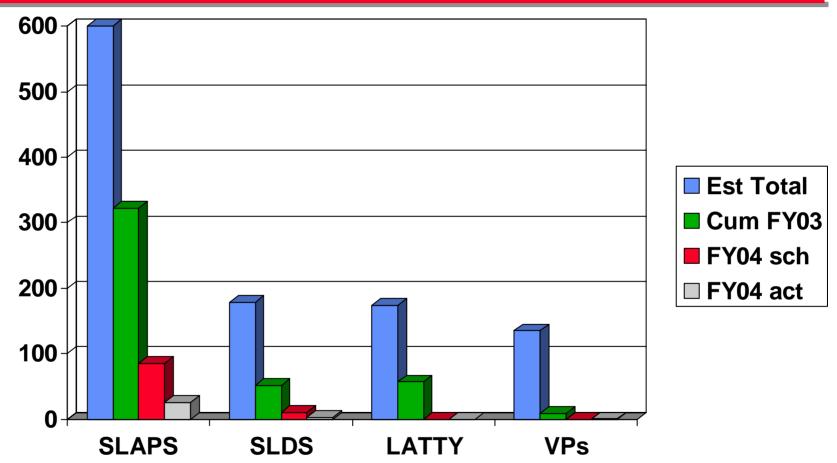

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles



### **North County ROD Status**



- The North County Record of Decision
  - Draft ROD and Responsiveness Summary is currently under internal USACE review.
    - Comments received from HQUSACE, MVD and the HTRW-CX. Responses being developed.
  - Derivation of Site-Specific DCGLs for North County Structures
    - Comments were due 1 DEC from the USEPA and MDNR.
      - MDNR requested an extension to 15 DEC for their comments and 31 DEC for MDOH comments.
      - USACE working responses to comments.



### **Community Interactions**




Recent Events

- St. Louis Post Dispatch article appeared in 8 Jan paper
- Upcoming Events
  - Publish Winter newsletter



### **Taskers**



#### Old Taskers

 USACE will schedule a time with the DOE Office of Legacy Management to brief the Oversight Committee on Long Term Stewardship (Date / Time TBD)

#### New Taskers

January 2004 11



### **Questions**



Gateway to Excellence

Questions?

Questions? Questions?

Questions?

Questions?

Questions? Questions?

Questions?

Questions?

**Questions?**
