



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

10 SEP 04

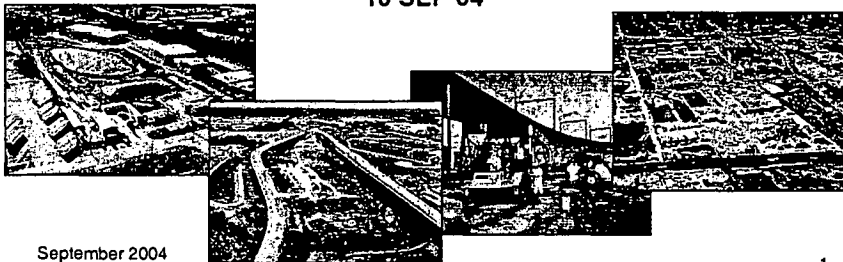

September 2004

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **North County ROD**
- **Community Interactions**
- **Taskers**
- **Questions**

September 2004

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

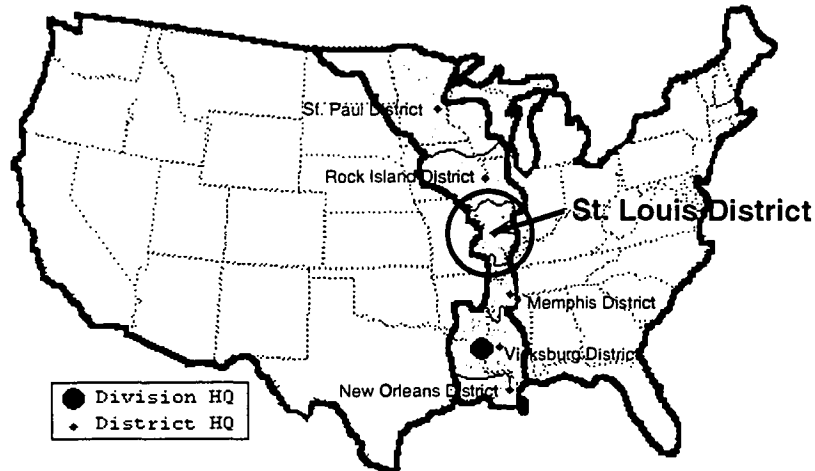

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
 - MI - Plant 7N/S PDIR regulator review complete. Design in progress. Plant 7W sampling complete. PDIR in progress.
 - **South of Anglerodt VPs** –
Thomas & Proetz PDIR finalized. Design out for regulator review.
Gunther- Sampling complete. PDIR in progress.
 - **West of Broadway VPs** – Sampling complete.
- **Remedial Action**
 - **MI Plant 6W South of Bldg 101** – Excavation 90% complete. Areas 2 & 3 in verification. 3,036 cy excavated. (appx. 500 cy to be reused).
 - **Post Remedial Action Reports (PRARs)** – 4 in progress, Plant 1, Plant 7E, City of Venice (McKinley Bridge) and DT 6/7 (Heintz Steel / Midwest Waste).
 - **Rail Shipments** – 5,460 cy shipped. (5,000 cy planned for FY04).

September 2004

4



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design** – Phase 6 Sheetpile wall design being coordinated w/ NS-RR.
- **Removal Actions**
 - **Phase 2/3** - 85,000+ cy total shipped to date (43,000+ cy this FY).
 - No activities currently.
 - SU-35 being utilized for one water storage basin.
 - **Phase 4/5** – ~45,000 cy shipped to date; SU-41 in-progress.
 - **Coldwater Creek COMPLETE**
 - **Phase 6** – RR signal line relocation complete.
 - **Water Storage / Water Treatment**
 - Minimum water being retained on site, currently.
 - 25th batch recently discharged.
 - **Rail Shipments off SLAPS this FY**
 - 101,000 cy shipped to date / 85,000 cy planned.

September 2004

5



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Group 1 VPs (2L, 3L, 4L, 5L) PreDesign Investigation (PDI) – Draft work plan .
 - VPs 1L, 8C and 40a Parcel – preparing Draft Summary Report
 - Rail Shipments off HISS – No shipments planned for FY04
- **SLAPS VP's**
 - **Assessment of the 30 DoE remediated properties.** Complete; issue after ROD.
 - **Characterizations** – On-going.
 - **Designs are on hold in FY04**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Utility Support** – 19 this FY in N. Cty; mostly along haul road ROW.
 - **Rail Shipments from VP's** – No shipments planned for FY04, however...
 - ~1,800 cy shipped from VPs – 10, 13 and 4C/5C.

September 2004

6




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

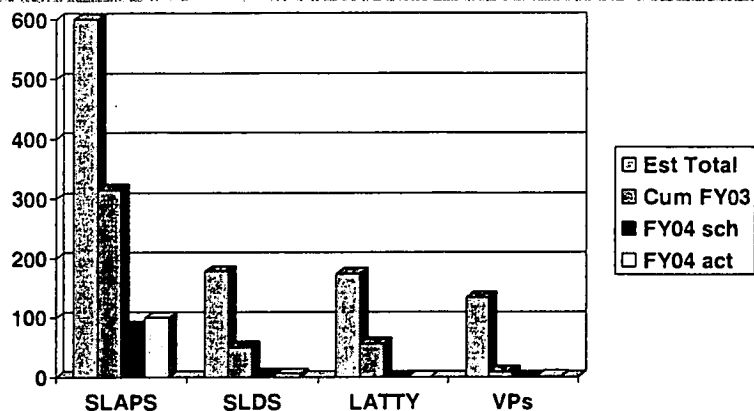

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles

September 2004

7



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **New Transportation Regulations**
 - Request made for DOT exemption, to transport material via gondola cars, as currently done.
 - Still awaiting response
- **Long Term Stewardship** - Next Meeting in December.
- **North County Haul Road Study** - Draft for Regulator review pending.
- **DoE Program POC (Jeff Short)** - No interactions during this timeframe.
- **CERCLA 5 year Review** - Finalization of document pending.

September 2004

8



US Army
Corps of Engineers
St. Louis District

North County ROD Status



Gateway to Excellence

- **Current Status / Recent Events**

- MVS revised responses and draft ROD (per 22-23 June discussion with EPA and MDNR) and issued to CX, MVD and HQ for concurrence.
- Minor comments received. Document being revised.
- Draft Final expected to be issued today.

September 2004

9



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**

- **Derivation of Site Specific DCGLs for N. County Structures** (DCGL doc) and memorandum explaining rationale.
 - Public notice published in Post Dispatch – 7 July. Letters issued to mailing list. Document available electronically via website, or paper copies w/ Admin Records.
 - Request for extension received. Review period extended initially to 18 Aug and then again to 23 Aug.
 - Response to comments expected next week.

September 2004

- **Upcoming Events**

10



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - USACE to provide a summary briefing on the North County ROD – TBD.
 - USACE to schedule a time w/DOE Office of Legacy Management to brief Oversight Committee on Long-Term Stewardship – TBD.
- **New Taskers**

September 2004

11



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

September 2004

12

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

*c/o 430 Adams St.
St. Louis, MO 63135
314-313-2959*

rcavanagh@ltcop-stl.org

MEMORANDUM

TO: FUSRAP Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, October 8, 2004, 11:30am, in the trailers on Latty Ave.

Members of the Committee who cannot attend should contact the chairperson at the above numbers to be excused.

Please allow sufficient time for Committee members to participate in a brief site tour following the meeting.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 430 Adams St.

St. Louis, MO 63135

314-313-2959

rcavanagh@ltcop-stl.org

Summary of September 10, 2004 Meeting

Committee Members Present: Jack Fraenhoffer, Ric Cavanagh, Sally Price, Michelle Morgenstern, Tom Manning, Jan Titus

Committee Members Excused: Jim Grant, Bill Brandes, Tom Binz

Other Interested Parties: Jacque Mattingly, Sharon Cotner, Larry Erickson

The following comments are in addition to the handouts provided by USACE at the meeting.

Page 4 – PDIR is the Pre Design Investigation Report

Page 5 – 11,000 cy in situ taken out of Coldwater Creek. The site is in very good shape regarding status of water.

Page 6 – Lots of economic development. Therefore there have been 19 utility support requests at the site

Page 8 – New regulations have been received, our site should be granted an exemption to the regs. An additional \$13,000 has been sent to the state for the Cooperative Agreement. That brings the total for this agreement to about \$373,000 for the year. Funding will likely be under Continuing Resolutions (CRA's) for the near term, possibly until April.

Page 9 – Re:ROD – Financial projections needed to be redone since they had been based on 2001 numbers. All parties have seen the Draft-Final. However, the Army has not signed off on it. Once signed, EPA has 30 days to give final approval. Larry Erickson indicated that the State may still have some issues with the ROD. There will be no further public review on the ROD. Hopefully, the Oversight Committee will get a briefing on the ROD at the October meeting.

Other General Business - The visit by the Assistant Secretary of the Army went well. Sharon reported that it is not likely that St. Louis will receive any new money in the remainder of the fiscal year.

NEXT MEETING

Friday, October 8, 11:30 am
