ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec Clayton, Missouri 63105 314.854.6635

MEMORANDUM

TO:

FUSRAP Oversight Committee

Other Interested Parties

FROM:

Richard R. Cavanagh, CHE

Chairpeerson

RE:

Next Meeting

The next monthly meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, April 9, 11:30 am, at the Latty Avenue trailers.

Committee members who cannot attend should call me at 854-6635.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE Summary of Meeting March 12, 1999

Members Present: Tom Manning, Tom Binz, Jan Titus, Bill Brandes, Jack Frauenhoffer, Donovan Larson, Sally Price, Ric Cavanagh

Members Excused: Eileen Davis-Young, Krista Durlas

Other Interested Parties: Tom Horgan, Dave Wagoner, Eric Gilstrap

The following notes are in addition to the handouts (see attached).

Page 4 - Cost of water treatment is 5 cents per gallon. Map at the end of packet details the sections of SLAPS. East end is almost complete. Project will proceed in the following order:

- Radium Pits
- Northwest Central
- Southwest Central
- West End
- Rail Loadout
- Railroad Right of Way

This basically reflects an upstream to downstream pattern.

- Page 5 Futura still very concerned about expanding into HISS area. Wants the work speeded up if possible.
- Page 6 There may not even be enough to do design work on VP's in FY 99. Better use of contractors is to do SLAPS and SLDS.
- Page 7 Plant 2 to be completed by end of summer. "8500" refers to the total cyds.
- Page 8 ARAR's being reviewed by Omaha. PCOC (risk assessment) being reviewed, anticipate some modifications. ECO means ecological.

March 11, the draft MOU between DOE and USACE is being reviewed. (DOE to assume management two years after final USACE close out. The first five year review is to be done by USACE). The Committee requested that it have input into this process. Sharon to supply Committee with names to write to.

Disposal cost is approximately 33% of project cost. (Hopefully, this cost will go down over time).

Page 9 - SLDS open house had approximately 35040 people.

Page 10 - Old Taskers:

- 1) Cost for water treatment is 5 cents per gallon.
- 2) NRC can regulate 11 E2 waste generated from 1978 on. Therefore NRC cannot regulate our project. EPA agrees that is doesn't make good policy sense.

New Taskers:

- 1) MOU DOE contact address
- 2) Move trailers to Super Valu lots??
- 3) Who were bidders for disposal contract?

Appropriations: Tom Horgan from Congressman Talent's office raised the issue of current and future appropriations. St. Louis has 50% of the FUSRAP waste but gets only 33% of the money. Rep. Talent to request more dollars from the Energy and Water Subcommittee. Will also seek bi-partisan support from other Missouri Congressmen, Senators.

NEXT MEETING:

FRIDAY, APRIL 9, 1999 11:30 AM LATTY AVE. TRAILERS








Gateway to Excellence

St. Louis Oversight Committee Meeting Corps Update



Notes




Agenda



- Mississippi Valley Division
- Progress Report
- Community Interactions
- Capability
- Taskers
- Questions

March 1999 2

-	Notes							
			•					
•								



Notes			



Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- EE/CA Action Memo/Responsiveness Summary Received
 - Distribution of Final EE/CA within 2 weeks
- · North Ditch / Sedimentation Basin Construction ongoing
 - North Ditch (including Sediment Trap) 16,148 cyds 63%
 - Sedimentation Basin 13,978 cyds 90%
 - Placing liner week of 22 March (weather permitting)
 - Treated and released 650,000 gallons of water S Ditch
- SLAPS East End Construction ongoing
 - 8,588 cy by PRAC (Radian) -95%
 - · Prepared 800 cyds of asbestos for shipment
 - 20,000 cy by TERC (Stone & Webster) starting 1 MAY 99
 - Negotiating Task Order RD (Complete) / RA (MAR 99)
- · Rail Shipments off SLAPS and Eva
 - 457 gondola railcars shipped to date (32,447 cyds)
- · Site Remediation Plans

March 1999 4

Notes				
			·····	
	· · · · · · · · · · · · · · · · · · ·			



Progress Report

Hazelwood Interim Storage Site (HISS)/Latty Avenue



- Railspur construction underway 75% complete
 - Placing rail now
 - Current completion date is mid-April (weather permitting)
- Plans & Specifications for HISS and Eastern Pile Removal (40,000 cy total) completed.
 - Finalizing Plans and Specifications
 - RFP to contractor in early April
 - Estimated FY99 removal is 4,000 cy (constrained by funds)
 - Initial start date is July 99

Notes				



Progress Report SLAPS Vicinity Properties



- Negotiating Right-of-Way with several Vicinity Property owners.
- · No remediation currently scheduled this fiscal year
- Developing remediation strategy
 - Risk based priorities list by end of FY99.
- Finalizing release letter for remediated properties.

Notes			



Progress Report Other Issues



- North County Feasibility Study/ROD & ARARs
 - First pass of ARAR's completed sent to HTRW-CX
 - PCOC memo sent to HTRW-CX -comments received
 - To regulators by end of March
 - ECO risk sampling ongoing
 - Land use designation under CoE review
- COE/DOE Memorandum of Understanding
 - Draft under CoE review as of 11 March
 - Topic at USACE Environmental Conference in March
- Nationwide Disposal Contract
 - Award in May

Notes					
	···				



Progress Report St. Louis Downtown Site (SLDS)



• IT Corp. continues Planning & Design activities

- Plant 1 Remedial Design underway
- · IT Corp remediation efforts
 - Remediation of City Properties is approximately 95% complete backfill ongoing. (4,500 cy)
 - Plant 2 began on 6 JAN with slab break up. Subsurface excavation ongoing (8,500) 10% complete.
- Seventy-two gondola cars shipped to date. (5,353 cy)

Notes				



Taskers



Gateway to Excellence

- Old Taskers
 - Cost for treatment of SLAPS Water to Ms. Price (complete)
 - NRC authority/new position to Mr. Larson (complete)
 - HQ POC for SLAPS EE/CA to Mr. Cavanagh & Mr. Horgan (complete)
 - HQ POC for DOE MOU to Mr. Cavanagh & Mr. Horgan (complete)
 - Filtration residue disposal information to Mr. Larson (complete)
 - Participation at Corps Environmental Conference to Mr. Cavanagh (complete)
- New Taskers

Notes				
	,			
	<u>-</u>			



Community Interactions



Recent Events

- FUSRAP Brief to Kentucky Society of Professional Engineers -18 & 19 FEB
- FUSRAP St. Louis Sites Newsletter -19 FEB 99
- St. Louis District briefed on status in Lunch and Learn -23 FEB
- SLDS Open House 25 FEB 99
- Upcoming Events
 - FUSRAP Model on Display at Clay School (15 Mar-19 Apr)
 - Hazelwood High School Physics Class Presentation (19 Mar)
 - Community Relations Presentation at Env Technical Conference

Notes		




Questions



Gateway to Excellence

Gnear	uestions?	Questions?
Questions	? Question	c2
Question	ns? Que	stions?
Question Questions?		Questions?
Questions?		estions?
11-Mar-99March 1999	Qu	11

Notes					
		·			
-					

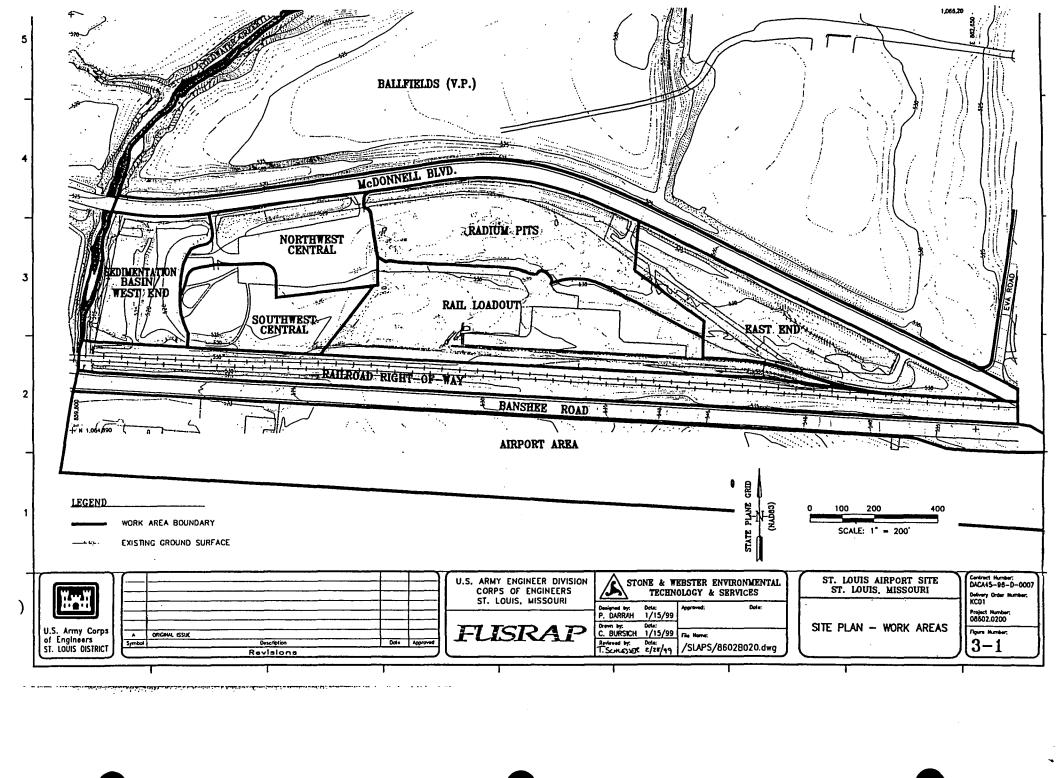

Data Entry Form

{Technical Managers fill in C through G. Document Managers fill in the rest}

A. Document ID Number: Will be assigned by database OD -142 B. Further Information Required?:
C. Primary Category: (Choose One): USACE St. Louis Sites Downtown North County Madison Site Inaccessible Areas PRP Oversight Committee D. Site (Optional): SLDS VP Mallinckrodt SLAPS CWC HISS PRP Madison D. Site (Optional): SLAPS UP CWC CWC CWC CWC CWC CWC CWC CWC CWC CW
E. Area (Optional):
F. Primary Document Type (Choose One): Site Management Records Removal Response Remedial Investigation Feasibility Study Record of Decision Program Management Remedial Design Remedial Action Public Affairs/Community Relations Congressional Relations Freedom of Information Act Requests Real Estate
G. Secondary Document Type (see back of form):
H. Bechtel Number: I. SAIC Number: J. MARKS Number(Choose One): FN: 1110-1-8100e FN: 1110-1-8100g FN: 1110-1-8100g
K. Subject: 1 Meeting Menutes from 12 mas 99 2
L. Title:
M. Author: Richard Caronagh N. Author's Company: Stor Oversight Commit
O. Recipient: Destrubrition P. Recipient's Company:
Q. Version (Choose One): Draft Final R. Date: 4/9/00
S. Include in the ARF? T. Include in the AR? U. Filed as Confidential/Privileged? V. To Be Microfilmed?
W. Document Format (Choose one): Paper Photographic Cartographic/Oversize Electronic Audio-visual Microform
X. Physical Location (Choose One): Central Files Records Holding Area Department of Energy In AR
Y. Filed in AR Volume Number: Z. Associated with Document(s):

Secondary Document Types

Amendments to Record of Decision (ROD)		П.
Anomaly Review Board Documents (Management Plan, Correspondence,		٠٠ لـنـا
Standard Operating Procedures, Findings)		
Applicable or Relevant and Appropriate Requirements (ARAR) Determinations		H
Archives Search Reports (ASR)		님
	٠.	H
Briefing Papers		닏
Chain of Custody Forms		Щ
Community Relations Plan		Ц
Correspondence	Ĵ •	Ш
Daily Operations Summary/Situation Reports		Ш
Engineering Evaluation and Cost Analysis (EE/CA) Action Memo	.*:	
Engineering Evaluation and Cost Analysis (EE/CA) Approval Memorandum	•	
Engineering Evaluation and Cost Analysis (EE/CA)		
Explanation of Significant Differences	•	
Fact Sheets/Newsletters		
Feasibility Study (FS) Reports	,	
Federal, State, Local Tech. Records	İ	同
Final Approved Findings and Determinations		\sqcap
Final Remedial Design Documents		Ħ
Freedom of Information (FOIA) Requests		Ħ
Freedom of Information (FOIA Responses)		Ħ
Health and Endangerment Assessments		뻐
Interagency Agreements/Memoranda	1	H
Interim Deliverables		님
Inventory Project Report (INPR) Risk Assessment Code (RAC)		버
Invoices/Contractor Payments/Cost Reports		님
Land Grants/Deeds		片
Mailing Lists	İ	H
News Clippings and Press Releases		님
No Further Action Docs (NOFA)	. 1	뭐
	į	님
On-Scene Coordinator Reports	i	닏
Proposed Plans for Remedial Action		님
Public Meeting Minutes/Transcripts	1	닖
Public Notices		닏
Public notices, Comments Received, Responses to the Comments		닏
Published Hearings		Ц
Record of Decision (ROD)		Щ
Reference Documents		Ш
Remedial Action Documents		
Remedial Investigation (RI) Reports		
Removal Response Reports (Emergency Evacuation Orders)		
Rights of Entry Documents		
Sampling/Analysis Data and Plans	Į.	
Scopes of Work/Contractual Documents	-	
Site Descriptions and Chronologies	Ī	
Site Inspection Documents	Ì	Ī.
Site Photographs and Maps	į	Ħ.
Testimonies	j	Ħ
Title Search Documents	. i	Ħ
Work Logs	,	Ħ
Work Plans and Progress Reports	i	Ħ
Work Plans/Site Safety and Health Plans and Progress Reports	Ī	H
Work Register and Logs	1	H
··	1	
