

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**  
*c/o 111 So. Meramec*  
*Clayton, MO 63105*  
*314-854-6635*

**OCT - 5**

September 30, 1998

**MEMORANDUM**

TO: Oversight Committee Members  
Other interested parties

FROM: Richard Cavanagh, CHE *RC*  
Chairperson

SUBJECT: **October 9 Meeting**

The next meeting of the St. Louis FUSRAP Oversight Committee will be Friday, October 9, 1998, 11:30 a.m. at the Latty Avenue trailers.

Please bring your own lunch.

Committee members who cannot attend should contact Ric Cavanagh at 854-6635.

Thank you.

:cr

Enclosure

**ST. LOUIS FUSRAP OVER SITE COMMITTEE**

*c/o 111 So. Meramec*

*Clayton, MO 63105*

*314.854.6635*

Highlights of September 11, 1998 Meeting

Committee Members Present: Sally Price, Jack Frauenhoffer, Bill Brandes, Donovan Larson, Jan Titus, Richard Cavanagh

Other Interested Parties: David Wagoner, Bob Boland, Bob Geller, Tom Binz, Michael Zlatic, Darrell Woolery, Laurie Peterfreund, Tom Horgan

**Please see the attached copies of handouts provided by USACE for the meeting.** The following are additional comments from the meeting. Page numbers reference the page of the handout.

Pg. 4 - SLAPS east end construction to start 9/21, not 9/24. The rail spur stock pile is being shipped to Envirocare immediately.

Pg. 5 - Rail spur location may need to be changed due to unwillingness of land owner to allow access without significant financial payment. The HISS pile will be shipped in FY 99 after the rail spur is completed.

Pg. 6 - the Florissant work entails removal of sediment by the bridge. Two questions were raised and will be addressed at next meeting: **1) What is the degree of contamination of the sediment? 2) When were field characterizations done most recently?**

Pg. 7 - ROD for SLDS is awaiting the General's signature. City properties will be done first in October, 1998.

Pg. 8 - a total of an additional \$4 million was available from other sites. However, St. Louis was only able to justify spending \$1.5 million since it had to be spent by the end of FY 98. USACE will attempt to establish arrangements and have contracts in place for the end of FY 99 so that St. Louis can get more money at the end of FY 99 (if available).

GAO visited USACE staff as a follow up of initial audit done in June at the request of the House Commerce Committee with the knowledge of the Water and Energy Committee. Questions focused on the budget, clean up standards, justification of the use of rail versus truck, etc.

The Memorandum of Agreement (MOA) with DOE deals with long term monitoring, land ownership, etc.

Pg. 9 - again it was stressed that HISS/Latty Ave work is dependent on the construction of the rail spur. It was also clarified that N/A for SLDS does not mean that there would be no additional funds to be utilized for SLDS. (FY 99 Capability column refers to amount above budget).

Pg. 10 - meeting with Coalition of Black Trade Unionists was the result of a NIOSH study on employees of Mallincrodt. NIOSH mistakenly thought that Mallincrodt was no longer in business and wanted to discuss potential effects on employees of Mallincrodt between 1942-1966. Since Mallincrodt is still in business, NIOSH needs to talk directly with those employees who are still alive.

Pg. 11 - There has been no meeting with Anna Ginsberg as of the date of the meeting.

***New Taskers:***

- get dollar amounts to be spent on VP's
- what was the level of contamination at St. Denis bridge
- provide NIOSH report to committee when available
- inform Jan Titus as to how much longer to complete the characterization of the ballfields
- State wants to know when wells are being drilled so that they can have a geologist on site

***Final Comments***

No digging is expected in January and February due to weather. Hope to have stockpiled dirt so that shipping can continue year round.

***Next Meeting:***

***Friday, October 9, 1998, 11:30 am  
Latty Avenue Trailer  
(Bring your own lunch)***



US Army  
Corps of Engineers  
St. Louis District


# ***FUSRAP***



Gateway to Excellence

## St. Louis Oversight Committee Meeting *Corps Update*

11 SEP 98



September 1998

1

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Agenda



Gateway to Excellence

- Mississippi Valley Division
- Progress Report
- Issues
- FY 99 Budget
- Community Interactions
- Taskers
- Questions

September 1998

2

## Notes

---

---

---

---

---

---

---




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

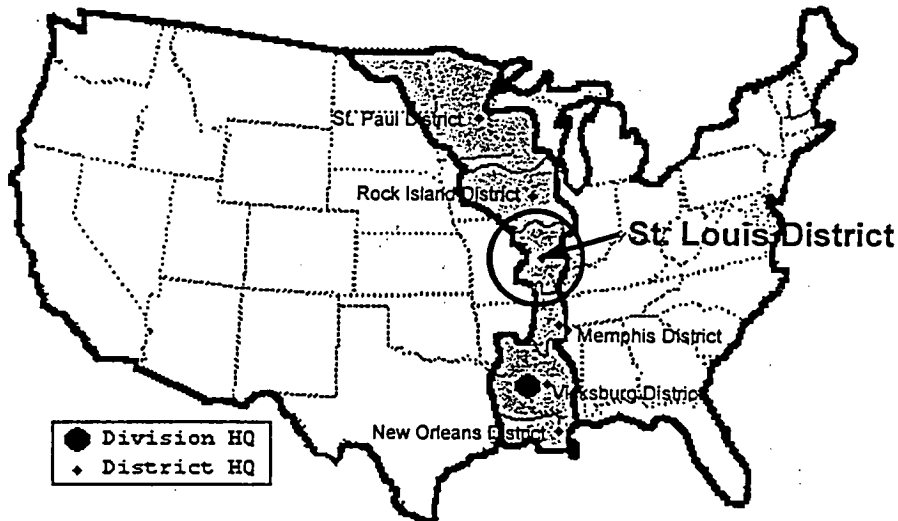

3

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **EE/CA Action Memo/Responsiveness Summary signed by ASA(CW) 25 Jun 98**
- **Railspur Construction completed 27 Aug 98**
- **North Ditch / Sedimentation Basin Construction ongoing**
  - North Ditch - 12,500 cyds (FY98/FY99)
  - Sedimentation Basin - 6,600 cyds (FY98)
- **SLAPS East End**
  - Design 100%- 40,000 cyds (FY98/FY99)
  - Construction starts ~~24~~<sup>27</sup> Sep 98
- **Characterization sampling ongoing**
- **First rail shipment completed 9 September from SLAPS**
  - Currently shipping RR spur stockpile (3,000 cyds)
  - Shipping from Eva and SLAPS concurrently

September 1998

4

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **EE/CA Action Memo/Responsiveness Summary signed by ASA(CW) 25 Jun 98**
- **Railspur construction to begin 16 Sep 98**
  - Pending Right of Way from GIFREHC
- **Plans & Specifications for HISS Pile Removal (40,000 cy) completed in two Phases**
  - Phase I (Supplementary Pile) completed 15 Jun 98
  - Phase II (Main Pile/Eastern Pile) completed 10 Sep 98

September 1998

5

### Notes

---

---

---

---

---

---

---





US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- Received \$1 million in capability funding from HQUSACE on 11 Aug 98
  - BNI will remediate VP 56, along Pershall road, Sep 98 (850 cyds)
- BNI will support City of Florissant work at St. Denis Bridge in Oct 98 (250 cyds)

September 1998

6

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- EPA signed ROD 27 Aug 98
- Completed Right-of-Entry requests to perform initial ROD work.
- IT Corp. began Planning / Design / Mobilization activities
- Final Groundwater Report issued 29 Jul 98
- IT Corp to begin remediation of City Properties (2,900 cyds) and Plant 2 (29,200 cyds) in Oct 98.
  - Submitted contractor work plans to regulators
- Conducted TERC Training within the District and in Jefferson City for MDNR.

September 1998

7

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ROD**
  - Met with Regulators, Center of Expertise (CX) and HQUSACE to determine timeline, issues, etc...
- **Additional funds became available this year**
- **4th Quarter construction execution - ongoing**
- **GAO visited site 8 Sep 98**
- **Located "free backfill" stockpile, looking for more**
  - 30,000 cyds, first come, first serve
- **Cooperative Agreement signed 28 Aug 98**
  - Payment for invoiced amount being processed as of 8 Sep 98.
- **MOA with DoE at HQUSACE level**

September 1998

8

## Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## FY 99 Budget and Capability



Gateway to Excellence

Site	FY99 Budget	FY99 Capability	Scheduled Work
SLAPS	21.2 million	20.0 million	<ul style="list-style-type: none"><li>• Continue East End</li><li>• Transition from PRAC to TERC</li><li>• Radium Pits</li><li>• Complete N. Ditch</li><li>• North County ROD</li></ul>
SLDS	15.0 million	N/A	<ul style="list-style-type: none"><li>• Remediate City Properties</li><li>• Begin remediation of Plant 2</li></ul>
Latty / HISS	5.6 million	16.4 million	<ul style="list-style-type: none"><li>• Complete RR Spur</li><li>• Begin Pile Removal (Eastern Pile Field)</li><li>• North County ROD</li></ul>
SLAPS VP's	.5 million	3.25 million	<ul style="list-style-type: none"><li>• Boundary delineation</li><li>• North County ROD</li></ul>
Totals	42.3 million	39.65 million	

September 1998

9

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- Internal Working Draft Community Relations Plan working, expected completion date is 30 Sep 98
- Participated, along with MDNR and USEPA, at the Coalition of Black Trade Unionists Conference on 15 Aug 98
- Awaiting NIOSH report on Mallinckrodt
  - Expect release in late September

September 1998

10

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- **Old Taskers**

- Keep Oversight Committee Chairman informed on Cooperative Agreement (complete)
- Add Mr. Larson to Oversight Committee mailing list (complete)
- Public Affairs to meet with Ms. Ginsburg's staff on Community Relations Plan (pending release of Community Relations Plan from USACE)

- **New Taskers**

September 1998

11

## Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

9-Sep-98September 1998

12

## Notes

---

---

---

---

---

---

---

Cataloging Form  
{Technical/Project Managers fill in C through G, K through Q. RM completes other fields}

A. Document ID Number: Assigned by database 838

B. Further Information Required? ☐

C. Operable Unit (Choose One):

USACE	<input type="checkbox"/>
St. Louis Sites	<input type="checkbox"/>
Downtown	<input type="checkbox"/>
North County	<input type="checkbox"/>
Madison Sites	<input type="checkbox"/>
Inaccessible Areas	<input type="checkbox"/>
PRP	<input type="checkbox"/>
Oversight Committee	<input checked="" type="checkbox"/>

D. Site (Optional):

SLDS VPs	<input type="checkbox"/>
Mallinckrodt	<input type="checkbox"/>
SLAPS	<input type="checkbox"/>
SLAPS VPs	<input type="checkbox"/>
CWC	<input type="checkbox"/>
HISS	<input type="checkbox"/>
Madison	<input type="checkbox"/>

E. Area (Optional): \_\_\_\_\_

F. Primary Document Type (Choose One):

Site Management Records	<input type="checkbox"/>
Removal Response	<input type="checkbox"/>
Remedial Investigation	<input type="checkbox"/>
Feasibility Study	<input type="checkbox"/>
Record of Decision	<input type="checkbox"/>
Remedial Design	<input type="checkbox"/>

Remedial Action	<input type="checkbox"/>
Public Affairs/Community Relations	<input checked="" type="checkbox"/>
Congressional Relations	<input type="checkbox"/>
Freedom of Information Act	<input type="checkbox"/>
Real Estate	<input type="checkbox"/>
Project Management	<input type="checkbox"/>

G. Secondary Document Type (see back of form):

Correspondence

H. Bechtel Number: \_\_\_\_\_

I. SAIC Number: \_\_\_\_\_

J. MARKS Number(Choose One): FN: 1110-1-8100e ☐ FN: 1110-1-8100f ☐ FN: 1110-1-8100g ☐

K. Subject/Title:

Oversight Committee Meeting Minutes from the September 11, 1998 Meeting

L. Author:

Richard Cavanagh

M. Author's Company:

Oversight Committee

N. Recipient(s): \_\_\_\_\_

O. Recipient(s) Company:

Distribution

P. Version (Choose One): Draft ☐

Final ☒

Q. Date:

9/30/98

R. Include in the ARF? ☒

S. Include in the AR? ☐

T. Filed as Confidential/Privileged? ☐

U. Document Format (Choose one):

Paper	<input checked="" type="checkbox"/>
Electronic	<input type="checkbox"/>

Photographic	<input type="checkbox"/>
Audio-visual	<input type="checkbox"/>

Cartographic/Oversize	<input type="checkbox"/>
Microform	<input type="checkbox"/>

V. Filed in AR Volume Number: \_\_\_\_\_

W. Physical Location (Choose One):

Central Files	<input checked="" type="checkbox"/>
Records Holding Area	<input type="checkbox"/>

Microfilm Vendor	<input type="checkbox"/>
Department of Energy	<input type="checkbox"/>

In ARF	<input type="checkbox"/>
In AR	<input type="checkbox"/>

X. Associated with Document(s): \_\_\_\_\_



## *Secondary Document Types*

- ☐ Amendments to Record of Decision (ROD)
- ☐ Anomaly Review Board Documents (Management Plan, Correspondence, Standard Operating Procedures, Findings)
- ☐ Applicable or Relevant and Appropriate Requirements (ARAR) Determinations
- ☐ Archives Search Reports (ASR)
- ☐ Briefing Papers
- ☐ Chain of Custody Forms
- ☐ Community Relations Plan
- ☐ Correspondence
- ☐ Daily Operations Summary/Situation Reports
- ☐ Engineering Evaluation and Cost Analysis (EE/CA) Action Memo
- ☐ Engineering Evaluation and Cost Analysis (EE/CA) Approval Memorandum
- ☐ Engineering Evaluation and Cost Analysis (EE/CA)
- ☐ Explanation of Significant Differences
- ☐ Fact Sheets/Newsletters
- ☐ Feasibility Study (FS) Reports
- ☐ Federal, State, Local Tech. Records
- ☐ Final Approved Findings and Determinations
- ☐ Final Remedial Design Documents
- ☐ Freedom of Information (FOIA) Requests
- ☐ Freedom of Information (FOIA Responses)
- ☐ Health and Endangerment Assessments
- ☐ Interagency Agreements/Memoranda
- ☐ Interim Deliverables
- ☐ Inventory Project Report (INPR) Risk Assessment Code (RAC)
- ☐ Invoices/Contractor Payments/Cost Reports
- ☐ Land Grants/Deeds
- ☐ Mailing Lists
- ☐ News Clippings and Press Releases
- ☐ No Further Action Docs (NOFA)
- ☐ On-Scene Coordinator Reports
- ☐ Proposed Plans for Remedial Action
- ☐ Public Meeting Minutes/Transcripts
- ☐ Public Notices
- ☐ Public notices, Comments Received, Responses to the Comments
- ☐ Published Hearings
- ☐ Record of Decision (ROD)
- ☐ Reference Documents
- ☐ Remedial Action Documents
- ☐ Remedial Investigation (RI) Reports
- ☐ Removal Response Reports (Emergency Evacuation Orders)
- ☐ Rights of Entry Documents
- ☐ Sampling/Analysis Data and Plans
- ☐ Scopes of Work/Contractual Documents
- ☐ Site Descriptions and Chronologies
- ☐ Site Inspection Documents
- ☐ Site Photographs and Maps
- ☐ Testimonies
- ☐ Title Search Documents
- ☐ Work Logs
- ☐ Work Plans and Progress Reports
- ☐ Work Plans/Site Safety and Health Plans and Progress Reports
- ☐ Work Register and Logs
