

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

*c/o 111 So. Meramec
Clayton, Missouri 63105
314.615.1635
Ric_Cavanagh@Stlouisco.com*

July 3, 2001

MEMORANDUM

TO: FUSRAP Oversight Committee
Other Interested Parties

FROM: Richard R. Cavanagh, CHE
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, July 13, 2001, 11:30 am, at the trailers on Latty Ave.

Oversight Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

I will provide copies of the Congressional Delegation letter at the meeting. If you need copies of the handouts provided by USACE at the June meeting, please contact me.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

*c/o 111 So. Meramec
Clayton, Missouri 63105
314.615.1635*

Ric_Cavanagh@Stlouisco.com

Summary of June 8, 2001 Meeting

Committee Members Present: Jim Grant, Bill Brandes, Tom Binz, Ric Cavanagh, Jon Langerak, Jan Titus, Sally Price

Committee Members Excused: Tom Manning

Other Interested Parties: Jack Fraenhoffer, Larry Erickson, Eric Gilstrap, Tom Horgan, Bob Marchant, Sharon Cotner, Lou Dell'Orco

The following comments are in addition to the handouts provided by USACE at the meeting.

Page 4 - Will continue to stockpile soil at the east end. It will be moved if extra money is available at the end of the year.

Page 5 - Contractor has had more efficiency; therefore, more has been shipped than planned.

Page 6 - Tenants, landowners, and governments will receive the "Friendly Letter." Jack Fraenhoffer suggested that a press release also go out "to reduce the grief, avoid confusion."

Page 7 - the actual acreage of VP's is not increasing. However, staff is learning that more parties actually own the land, therefore there are more VP's. Soil is also be stockpiled at SLDS and Midwest Waste. Larry Erickson asked if there is any security on the stockpiled soil at night. It is a concern since it is an open property. Lou will check this out and report back.

Page 11 - no impacted areas with MDOT construction on the I-270/I-170 construction.

Tom Horgan of Congressman Aiken's office reported that a five member Congressional Delegation letter is being signed and will be sent to appropriate Congressional leaders endorsing continued funding for St. Louis FUSRAP sites. Many thanks to Tom and Washington lobbyist Laurie Madden for getting this done.

Chairperson's comments on Congressional changes: The change in the political balance in the Senate may actually help our project. With redistricting, all of the FUSRAP sites will be in Congressman Clay's district after the 2002 election. Next meeting: Friday, July 13, 2001, at the trailers on Latty Ave.



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

8 JUNE 01



June 2001

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

June 2001

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

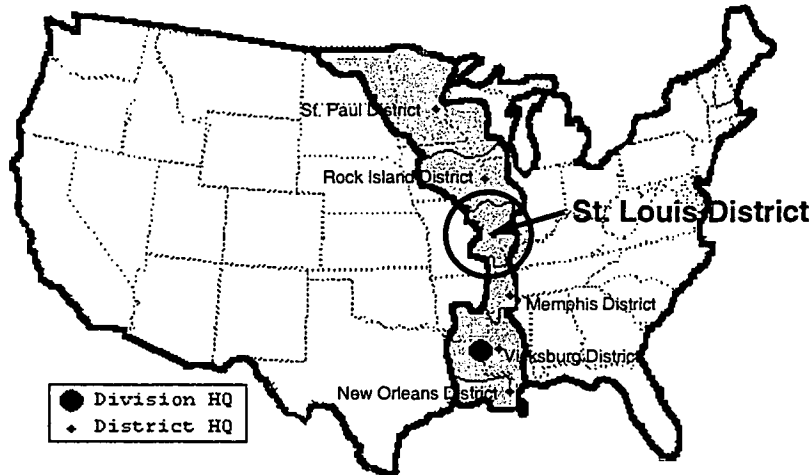

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - Site Wide Preliminary Design Investigation Report completed.
 - Work Description for Phase I (IA5) - REV 0 published 4 JUN 01.
 - Work Description for Phases 2 / 3 (IA2 / 3) - W and SW of the Radium Pits - 60% due 28 JUN
- **Removal Actions**
 - **East End - Excavation ongoing in the Eastern End Right of Way**
 - The contractor is currently excavating at SU14 & SU7, adjacent to McDonnell Boulevard.
 - A portion of the SU is in Final Status Survey
 - 45,000 cyds expected, 27,258 cyds excavated to date
 - Soil is being sent to both EnviroSafe and Envirocare (Avg concentration is 578 pCi/g)
 - **Status of treatment of selenium (Se) in water**
 - Currently in the process of awarding RFP for treatment
 - Plant may be operational by end of FY. (USACE will know more after JUL bench test)
 - Currently answering MSD questions for discharge application
 - **Rail Shipments off SLAPS**
 - 28,247 cyds shipped to date / 60,000 planned
 - **Modular office building move in is complete minus some data lines**
 - Stone and Webster has relocated from NW Plaza to the SLAPS.

June 2001

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Remedial Design**
 - **Main Pile North Half - 9,500 cyds**
 - Contract is complete. Request for Proposal (RFP) on hold due to funding
 - Target start date is late in the FY
- **Remedial Action**
 - **Main Pile South Half (12,500 cyds on the South Half)**
 - Contractor is decontaminating last piece of equipment.
 - **GIFREHC - No new Information**
 - MVS is awaiting the latest proposal from GIFREHC on roof replacement costs / schedule
 - It is expected that MVS will support GIFREHC contract with radiological operations only. Transportation and disposal may be done by USACE pending agreement. Some asbestos, not related to FUSRAP, is on the roof
 - GIFREHC would like to start in the JUL - OCT timeframe
 - **Rail Shipments off HISS**
 - 25,694 cyds shipped to date / 20,000 cyds planned

June 2001

5



US Army
Corps of Engineers
St. Louis District

Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Data Evaluation**
 - VP removal action assessments on hold for 30 DoE remediated properties.
 - Document is pending regulator review
 - 12 - Expect No Further Action
 - 12 - Need Additional Investigation to determine status
 - 6 - Need Additional Investigation and Probable Remedial Action
- **Characterization Surveys / Remedial Design**
 - **Continue to gain real estate access to properties to obtain walkover and sampling data for Plans and Specifications in FY01**
 - 56/57/58/59/1C & Pershall & I-270 ROW (@2,000 cyds) - DBM due mid JUN
 - 9/10/11/12 & Hotspots in the ballfields and IA 10 - 60% design submitted
 - Coordinating design with Laclede Gas on VP 12
 - One design will be completed this year by SAIC (One delayed due to funding)
- **"Friendly Neighbor" letter to VP owners - Due 15 JUN**
 - Being sent to owners, tenants and affected state / city organizations.
- **Remedial Action - None scheduled for this FY**
 - **Rail Shipments of VP soils (Shipped from HISS)**
 - 0 cyds planned; however, based on funding / utility work, the number could increase

June 2001

6



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **VP designations:** Three properties on existing parcels, added for investigation
 - Star Bedding, Christiana and Collins
 - **Remedial Design**
 - **Pre Design Investigation** - Plant 7N/7S, McKinley Bridge and Thomas / Proetz Lumber are currently pending or under review
 - **Work Description for Small Area Remediation - REV 0 published 4 MAY**
 - Helntz Steel & Gunther Salt are complete. PSC Metals is working
 - **Remedial Action**
 - Plant 2 PRAR is pending regulator review.
 - **Plant 1 continues (@2,750 cyds) - 2,545 cyds remediated to date**
 - Current completion date is 30 JUN 01. 7 small areas remain.
 - **Plant 6E / 6E1/2 (15,000 cyds) began 3 DEC - 7,625 cyds remediated to date**
 - Phase I excavation continues. New completion date is end of JUL
 - Soils are going to Envirocare.
 - **VP's - Midwest Waste (900 cyds) - 842 cyd removed to date. 1 JUL completion**
 - Final Status Survey for MSD Lift Station is under regulator review
 - **Rail Shipments off SLDS**
 - 7,297 cyds shipped / 7,500 planned
- June 2001 • Soil is currently being stockpiled at the SLDS and Midwest Waste - 1,000 cyds 7



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - FS/PP regulator review is the next step
 - USACE has finalized and is now incorporating updated cost data
 - USACE continues to develop the Administrative Record - JUL completion
- **Stockpiling of soils will occur at SLDS and SLAPS due to funding constraints.**
- **Long Term Stewardship**
 - Long Term Stewardship Workshop 30 JUL - 2 AUG in Grand Junction
- **MDNR requested an additional funding for the Cooperative Agreement.**
 - \$437,000 - Split between the remainder of 2001 and 2002
- **DoE Program POC's interactions - A new Acting Director and staff is in the process of being hired (Director of Long term Stewardship Office)**
 - HQUSACE and the DoE continue to talk.
- **The Army Audit Agency continues their audit of our FUSRAP - Draft pending in JUL**

June 2001

8




US Army
Corps of Engineers
St. Louis District

Volume Shipped Using Environmental Documents



Gateway to Excellence

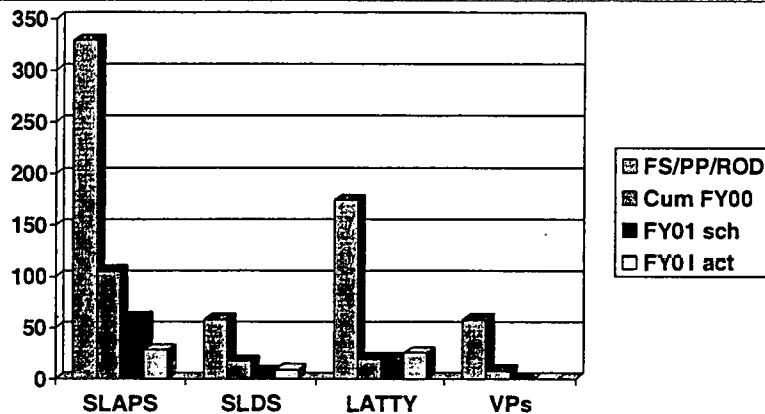

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles
June 2001

9



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Briefing and SLAPS Tour at the DOD LLRW Generators Meeting 23 MAY
 - Briefing for Washington University Life Sciences class - 24 MAY
- **Upcoming Events**
 - Briefing for the New Piasa Chautagua Group - 25 JUN
 - Newsletter published - 29 JUN

June 2001

10



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**

- Provide the Oversight Committee copies of correspondence on water treatment (Working - MSD letter pending)
- Provide a briefing (separate from the monthly meeting) of North County FS/PP highlights prior to release to the public. (Working)
- Will SLOC be able to review the AAA report or will it be classified as an internal review document? (Working)
- Provide a flowchart to the Oversight Committee for the RD process
- Provide a copy of the "Friendly Neighbor" letter to the Oversight Committee (Working)
- Provide a list of the "new" FUSRAP sites to Tom Horgan (Complete)
- Speak to MoDOT about the 170/270 Interchange and its impacts to FUSRAP (Complete)
- Provide the Oversight Committee information on the New Piasa Chautagua Group (Complete)
- The Oversight Committee will draft a letter to the Chairman of the Energy and Water Committee (Working)

- **New Taskers**

June 2001

11



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

June 2001

12

FUSRAP Document Management System

Year	ID	Further Info?	
00	2614	<input type="checkbox"/>	
Operating Unit	Site	Area	MARKS Number
St. Louis Sites			FN:1110-1-8100g
Primary Document Type	Secondary Document Type		
Public Affairs/Community Relation	Public Meeting Minutes/Transcripts		
Subject or Title			
St. Louis Oversight Committee Meeting Minutes/Presentation from June 2001 (6/08/01)			
Author/Originator	Company	Date	
Richard Cavanagh	St. Louis County DOH	6/8/2001	
Recipient(s)	Company (-ies)	Version	
Distribution		Final	
Original's Location	Document Format	Confidential File?	
Central Files	Paper	<input type="checkbox"/>	
Comments	Include in which AR(s)?	ETL	
	<input checked="" type="checkbox"/> North County	8.10	
SAIC number	<input type="checkbox"/> Madison	Filed in Volume	
	<input type="checkbox"/> Downtown	8	
Bechtel ID	<input type="checkbox"/> Iowa		
	
