

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

*c/o 111 So. Meramec*

*Clayton, MO 63105*

*314.615.1635*

*Ric-Cavanagh@Stlouisco.com*

August 3, 2001

**MEMORANDUM**

TO: FUSRAP Oversight Committee  
Other Interested Parties

FROM: Richard R. Cavanagh, CHE  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, August 10, 11:30 am at the trailers on Latty Ave.

Oversight Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

**c/o 111 So. Meramec**

**Clayton, MO 63105**

**314.615.1635**

**Ric-Cavanagh@Stlouisco.com**

**Summary of July 13, 2001 Meeting**

Committee Members Present: Jim Grant, Sally Price, Tom Binz, Ric Cavanagh, Tom Manning

Committee Members Excused: Jan Titus

Other Interested Parties: Larry Erickson, Jack Fraunhoffer, Eric Gilstrap

The following comments are in addition to the handouts provided by USACE at the meeting.

Page 4 - The Airport Authority's biggest concern is standing water (which brings birds which creates a danger to planes). Fundamentally, this is a grading issue. The cost of the water treatment is estimated at \$4 million/year for four years.

Page 5 - The RFP is being held until the second week in September with the hopes of getting new money by then. There really is only 4 - 6 weeks of work there.

Page 7 - 6E/6E 1/2 shows that the model used was not effective. Staff have to keep chasing new areas. The model left too much area unidentified.

Page 8 - Regarding the MOU, how much does this apply to Mallinckrodt? USACE staff to provide answer at next meeting.

Page 11 - In answer to a question raised at the June meeting, an open bag is a DOT violation. However, with the violation, only a corrective action report is required. The Corrective Action document is approved by the facility and then kept on file at the facility.

**NEXT MEETING**

**Friday, August 10, 2001**

**11:30 am**

**At the Trailers on Latty Ave.**



US Army  
Corps of Engineers  
St. Louis District





# **FUSRAP**



Gateway to Excellence

## **St. Louis Oversight Committee Meeting Corps Update**

13 JULY 01



July 2001

1



US Army  
Corps of Engineers  
St. Louis District

## **Agenda**



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

July 2001

2




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

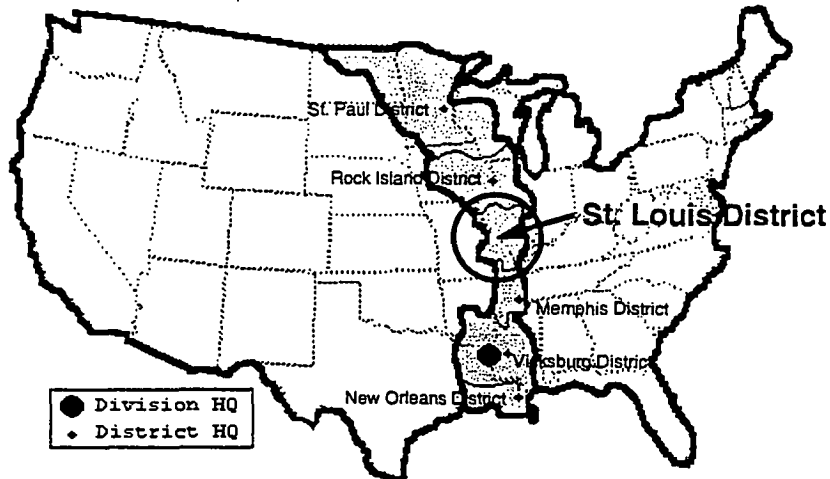

3



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
  - **Work Description for Phases 2 / 3 (IA2 / 3)** - W and SW of the Radium Pits - 90% due 27 JUL
  - **Currently finalizing Site Wide Grading Plan** - Will be coordinated with the Airport Authority.
- **Removal Actions**
  - **East End - Excavation ongoing in the Eastern End Right of Way**
    - The contractor is currently excavating at SU12 & SU13
      - 2 of 10 Survey Units (7 and 8) are currently being backfilled, 9 and 11 are pending Final Status Survey
    - 45,000 cyds expected, 31,300 cyds excavated to date
    - Soil is being sent to both EnviroSafe and EnviroCare (Avg concentration is 471 pCi/g)
  - **Status of water treatment system**
    - Plant may be operational by end of FY. (Contractor is currently preparing for a bench test which will be conducted next week)
    - Currently awaiting MSD response to discharge application
  - **Rail Shipments off SLAPS**
    - 34,761 cyds shipped to date / 60,000 planned (Due to funding constraints, 42,000 cyds anticipated)

July 2001

4



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Remedial Design**
  - Main Pile North Half - 9,500 cyds
    - Request for Proposal (RFP) on hold due to funding constraints
    - Target start date is late in the FY with completion early in FY02.
- **Remedial Action**
  - **GIFREHC - Working Right of Entry for roof work**
    - MVS is responding to the latest RoE proposal from GIFREHC on roof replacement costs / schedule
    - It is expected that MVS will support GIFREHC contract with radiological operations only. Transportation and disposal may be done by USACE pending agreement. Some asbestos, not related to FUSRAP, is on the roof
    - GIFREHC would like to start 1 AUG; however, still need RoE agreement, resolution of funding issues and radiological plan development
      - Not likely to start until at least 30 days after signed agreement
  - **Rail Shipments off HISS**
    - 25,694 cyds shipped to date / 20,000 cyds planned

July 2001

5



US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Data Evaluation**
  - VP removal action assessments on hold for 30 DoE remediated properties.
    - Document is pending regulator review
      - 12 - Expect No Further Action
      - 12 - Need Additional Investigation to determine status
      - 6 - Need Additional Investigation and Probable Remedial Action
- **Characterization Surveys / Remedial Design**
  - Continue to gain real estate access to properties to obtain walkover and sampling data for Plans and Specifications in FY01
    - 56/57/58/59/1C & Pershall & I-270 ROW (@2,000 cyds) - DBM due mid JUN
    - 9/10/11/12 & Hotspots in the ballfields and IA 10 - 60% design submitted
  - One design will be completed this year by SAIC (One delayed due to funding)
- **"Friendly Neighbor" letter to VP owners -**
  - Sent to owners, tenants and affected state / city organizations.
  - Press release sent out
- **Remedial Action - None scheduled for this FY**
  - Rail Shipments of VP soils (Shipped from HISS)

July 2001

• 0 cyds planned; however, based on funding / utility work, the number could increase 6



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Preliminary Design Investigation** - Ongoing at Cash, Christiana and Star Bedding
- **Remedial Design**
  - **Pre Design Investigation** - Plant 7N/7S, McKinley Bridge and Thomas / Proetz Lumber are currently pending or under review
  - **Work Description for Small Area Remediation - REV 0 published 4 MAY**
    - PSC Metals is due 16 JUL, Heintz Steel due 18 JUL.
- **Remedial Action**
  - **Plant 2 PRAR is under regulator review.**
  - **Plant 1 continues (@2,750 cyds) - 2,545 cyds remediated to date**
    - Current completion date is 30 SEP 01. 5 small areas remain - 3 still need to be remediated, 2 are pending Final Status Survey.
  - **Plant 6E / 6E1/2 (15,000 cyds) began 3 DEC - 7,625 cyds remediated to date**
    - Phase I excavation continues to chase contamination. New completion date is next FY
    - Soils are going to Envirocare.
  - **VP's - Midwest Waste (950 cyds) - 910 cyds removed to date. 6 of 14 areas in FSS.**
    - **MSD Lift Station** - Final Status Survey - MSD and regulator review completed
  - **Rail Shipments off SLDS**
    - 9,227 cyds shipped / 7,500 planned

July 2001

7



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
  - FS/PP regulator review is the next step
    - USACE continues to incorporate updated cost data into the FS/PP
    - Currently answering MDNR follow on ARAR's question
    - USACE continues to develop the Administrative Record - JUL completion
- **Stockpiling of soils will occur at SLDS and SLAPS due to funding constraints.**
- **Long Term Stewardship**
  - Long Term Stewardship Workshop 30 JUL - 2 AUG in Grand Junction
  - 20 AUG - ASTSWMO meeting in Tampa will discuss Stewardship Issues
- **Status of MDNR request for additional funding under the Cooperative Agreement.**
  - \$437,000 - Split between the remainder of 2001 and 2002
  - Meeting held 29 JUN - MDNR will provide updated numbers based upon USACE scheduled activities
- **DoE Program POC's interactions** - HQUSACE and the DoE continue to talk.
- **The Army Audit Agency continues their audit of our FUSRAP - Draft pending in JUL**
- **USACE and the NRC recently signed a MOU for FUSRAP sites with NRC licenses**

July 2001

8




US Army  
Corps of Engineers  
St. Louis District

## Volume Shipped Using Environmental Documents



Gateway to Excellence

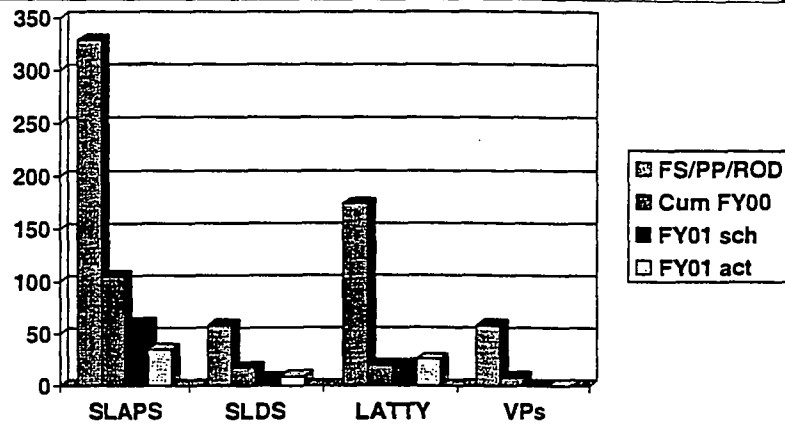

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles  
July 2001

9



US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- **Recent Events**
  - Briefing for the New Piasa Chautagua Group - 25 JUN
- **Upcoming Events**
  - Newsletter to be published and distributed next week

July 2001

10



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- **Old Taskers**

- Provide the Oversight Committee copies of correspondence on water treatment (Working - MSD letter pending)
- Will SLOC be able to review the AAA report or will it be classified as an internal review document? (Working)
- Provide a copy of the "Friendly Neighbor" letter to the Oversight Committee (Complete)
- Speak to MoDoT about the 170/270 Interchange and other area work completed, future work and its impacts to FIIIRAP (Complete)
- The Oversight Committee will draft a letter to the Chairman of the Energy and Water Committee (Complete?)
- How is the stockpile at Midwest Waste being protected? (Fencing installed and area posted - Complete)
- Is an "open burrito" bag on a shipment a DoT violation? (Complete)

- **New Taskers**

July 2001

11



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions? Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?

July 2001

12

# FUSRAP Document Management System

Year ID

00 2686

Further Info?

☐

Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs/Community Relation

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting Minutes from July 13, 2001 Meeting

Author/Originator

Richard Cavanagh

Company

St. Louis County DOH

Date

8/3/2001

Recipient(s)

Distribution

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?

☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

☒ North County

☐ Madison

☐ Downtown

☐ Iowa

ETL

8.10

Filed in Volume

8

