

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, MO 63105

31/615.1635

Ric_Cavanagh@Stlouisco.com

May 31, 2001

MEMORANDUM

TO: FUSRAP Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh, CHE
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be on Friday, June 8, 2001, 11:30 am, at the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, MO 63105

314.615.1635

Ric_Cavanagh@Stlouisco.com

Summary of May 11, 2001 Meeting

Committee Members Present: Jim Grant, Tom Manning, Ric Cavanagh, Tom Binz, Jan Titus, Sally Price, Bill Brandes

Other Interested Parties: Sharon Cotner, Lou Dell'Orco, Larry Erickson, Eric Gilstrap, JoAnne Wade, Jack Fraenhoffer, Virgil Janson, Dave Wagoner, Tom Horgan, Mike Zlatic

The following comments are in addition to the handouts provided by USACE at the meeting (see attached).

Chairperson Ric Cavanagh reported that he had talked with Anna Ginsberg, Co-Chairperson of the Oversight Committee, regarding her continued involvement with the project as a result of the election of a new mayor for the City of St. Louis. Since the transition to a new mayor was just under way, she stated that she would seek clarification from Mayor Slay's office and report back as soon as possible.

Page 4 - USACE will provide a flow chart of the review and approval process at our next meeting. There probably will only be between 45-50,000 cyds of rail shipments (not 60,000) due to funding restrictions.

Page 5 - Sharon Cotner reported that last Friday, two rail cars arrived at Envirocare with ripped or torn covers. Fortunately, the content of the cars was low level materials. This is the first time such an incident has occurred. It may be the result of faulty bags (1% of bags may have some defects). Tom Binz asked if this was a DOT reportable incident. Staff could not provide an answer but will do so at next month's meeting. As part of the beginning of the Long Term Stewardship planning process, a Friendly Neighbor letter signed by Col. Morrow will go out to property owners in the FUSRAP area advising them to contact the FUSRAP office before doing any work on their property. Tom Manning asked if there are any contaminated areas that might be effected by the construction work on I-270 and I-170 that is supposed to begin in the fall. Staff will check on this and report back at our next meeting.

Page 7 - Correction: PSC is done. Plant 2 PRAR no longer on hold (will go forward as is). Rail shipments will exceed the 7500 planned

Page 8 - Regarding Long Term Stewardship, neither the federal or state governments have the power to place deed restrictions on properties. The Long Term Stewardship

Committee will seek to clarify the role of the city and county in such proposed activities.
It may require legislation on the local level.

Page 9 -



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

11 MAY 01

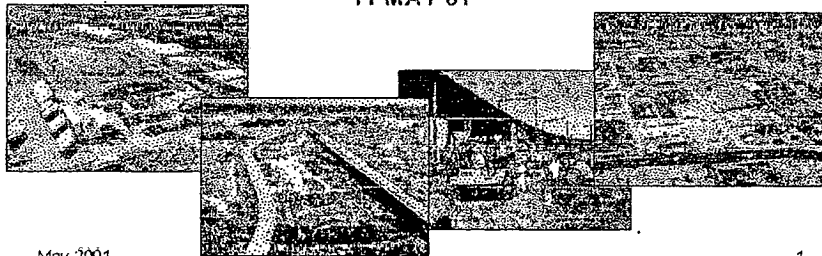

May 2001

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- Mississippi Valley Division
- Progress Report
- Community Interactions
- Taskers
- Questions

May 2001

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

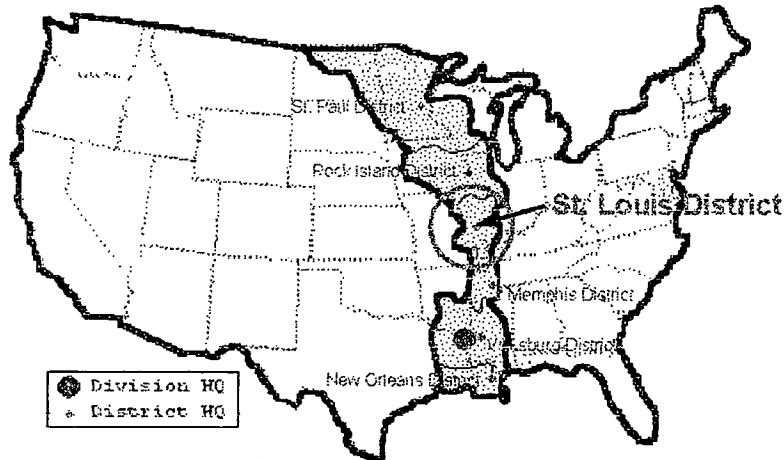

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - **Site Wide Preliminary Design Investigation Report pending completion in MAY.**
 - **Work Description for Phase I (IA5)**
 - Regulator Review comments were received 10 MAY, final is expected in late JUN
 - **Work Description for Phases 2 / 3 (IA2 / 3) - W and SW of the Radium Pits - 60% due 18 MAY**
- **Removal Actions**
 - **East End - Excavation ongoing in the Eastern End Right of Way**
 - The contractor is currently excavating at SU14, adjacent to McDonnell Boulevard.
 - 45,000 cyds expected, 25,900 cyds excavated to date
 - Soil is being sent to both EnviroSafe and EnviroCare
 - **Status of treatment of selenium (Se) in water - options being evaluated**
 - USACE is in the process of following up with MDNR Water Pollution Control
 - Currently in the process of awarding RFP for treatment
 - Plant may be operational by end of FY. (USACE will know more after JUL bench test)
 - Currently awaiting MSD response to discharge application
 - **Rail Shipments off SLAPS**
 - 26,913 cyds shipped to date / 60,000 planned
 - **Modular office building move in on schedule for late MAY**

May 2001

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Laffey Avenue



Gateway to Excellence

- **Remedial Design**
 - **Main Pile North Half**
 - Request for Proposal (RFP) on hold until funding becomes available
- **Remedial Action**
 - **Main Pile South Half (12,500 cyds on the South Half)**
 - Contractor is complete - currently decontaminating equipment & demobilizing
 - 15,839 cyds were removed, remaining pile area is being covered until next contract
 - Soil was sent to Envirocare.
 - **GIFREHC**
 - MVS continues to talk with GIFREHC on roof replacement costs / schedule
 - It is expected that MVS will support GIFREHC contract with radiological operations only. Transportation and disposal may be done by USACE pending agreement.
 - GIFREHC would now like to start in the JUL - OCT timeframe
 - Some asbestos, not related to FUSRAP, is on the roof
 - **Rail Shipments off HISS**
 - 25,694 cyds shipped to date / 20,000 cyds planned

May 2001

5



US Army
Corps of Engineers
St. Louis District

Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Data Evaluation**
 - VP removal action assessments on hold for 30 DoE remediated properties.
 - Based upon the dose assessment
 - 12 - Expect No Further Action
 - 12 - Need Additional Investigation to determine status
 - 6 - Need Additional Investigation and Probable Remedial Action
- **Characterization Surveys / Remedial Design**
 - **Continue to gain real estate access to properties to obtain walkover and sampling data for Plans and Specifications in FY01**
 - 56/57/58/59/1C & Pershall & I-270 ROW(@2,000 cyds) - DBM due mid JUN
 - 9/10/11/12 & Hotspots in the ballfields and IA 10 - 60% design due early JUL
 - Coordinating design with Laclede Gas on VP 12
 - Two designs to be completed this year by SAIC (Groupings are as listed above)
- **"Friendly Neighbor" letter to VP owners - Due 15 JUN**
- **Remedial Action**
 - The VP38 PRAR will be finalized once all above criteria contamination is removed.
 - **Rail Shipments of VP soils (Shipped from HISS)**
 - 0 cyds planned; however, based on funding / utility work, the number could increase ⁰

May 2001



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
 - **Pre Design Investigation** - Plant 7 borings to be taken in late MAY
 - McKinley Bridge, Thomas / Proetz Lumber, PSC Metals and Heintz Steel are currently under review
 - **Work Description for Small Area Remediation - REV 0 published 4 MAY**
 - Includes Midwest Waste, Gunther Soil and small areas at Mallinckrodt
 - PSC Metals complete
- **Remedial Action**
 - **Plant 2 PRAR is on hold awaiting HQUSACE guidance.**
 - **Plant 1 continues (@2,750 cyds) - 2,524 cyds remediated to date**
 - Current completion date is 30 JUN 01.
 - Concurrent small area excavation is ongoing (4 of 14 areas complete & 4 working).
 - **Plant 6E / 6E1/2 (11,000 cyds) began 3 DEC - 6,100 cyds remediated to date**
 - Phase I excavation continues. New completion date is end of JUL.
 - Volume has doubled from original estimate. Soils are going to Envirocare.
 - **VP's - Midwest Waste (700 cyds) to start in late MAY**
 - **Rail Shipments off SLDS**
 - 7,297 cyds shipped / 7,500 planned

May 2001

Unity Policy - expect completion by JUL



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - FS/PP regulator review is the next step
 - USACE is currently incorporating cost data due to IC's
 - USACE continues to develop the Administrative Record - JUL completion
- **Long Term Stewardship discussions meeting #2 was held 10 MAY**
 - Long Term Stewardship Workshop 30 JUL - 2 AUG in Grand Junction
- **FUSRAP Program Review was held 19 APR in Portland.**
 - MVS received an additional \$1.1 million for SLDS
- **DoE Program POC's interactions**
 - None during this timeframe, although HQUSACE and the DoE met on 27 APR - notes forthcoming.
- **The Army Audit Agency continues their audit of our FUSRAP - No new information**
- **Status of additional funds**
 - Total MVS FUSRAP budget for this FY is \$60.5 million
 - We have a "capability" to quickly expend funds, through Transportation and Disposal of stockpiled soils at SLAPS and SLDS late in the FY should they become available.

May 2001

8




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

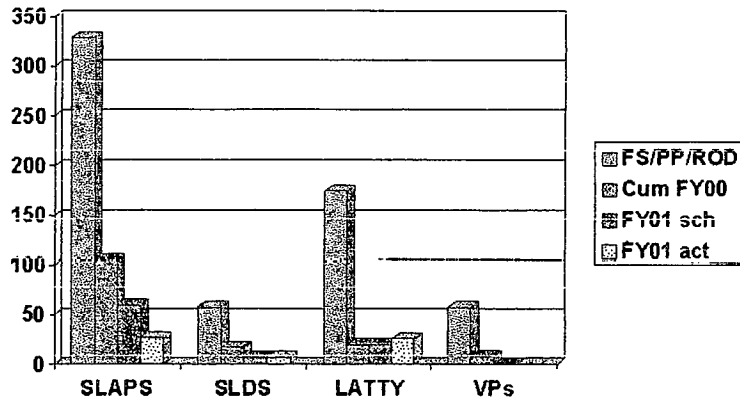

Note 1. North County volumes are based on the North County FS/PP
Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal
Note 3. SLDS volumes do not include Inaccessibles
May 2001

9



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Set up a booth / display at Earth Day in Forest Park on 22 APR
 - Provided a briefing and display at the St. Louis District Real Life Sciences Day - 2 May
- **Upcoming Events**
 - Briefing and SLAPS Tour at the DOD LLRW Generators Meeting 23 MAY
 - Briefing for the New Plaza Chautagua Group - 25 JUN
 - Newsletter published - 29 JUN

May 2001

10



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Provide the Oversight Committee copies of correspondence on water treatment (Working)
 - Provide a briefing (separate from the monthly meeting) of North County FS/PP highlights prior to release to the public. (Working)
 - Will SLOC be able to review the AAA report or will it be classified as an Internal review document? (Working)
- **New Taskers**

May 2001

11



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

May 2001

12

Administrative Record for the Formerly Utilized Sites Remedial Action Program (FUSRAP) North St. Louis County Sites

St. Louis County, Missouri



**US Army Corps
of Engineers**
St. Louis District®

Volume 8.10f
Public Affairs/Community Relations
Public Meeting Minutes / Transcripts

SLAP_000732

FUSRAP Document Management System

Year ID
00 2603

Further Info?
☐

Operating Unit
St. Louis Sites

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting Minutes from 5/11/01

Author/Originator
Richard Cavanagh

Company
St. Louis County DOH

Date
5/31/2001

Recipient(s)

Company (-ies)
Distribution

Version
Final

Original's Location
Central Files

Document Format
Paper

Confidential File?
☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

- ☒ North County
☐ Madison
☐ Downtown
☐ Iowa

ETL
8.10

Filed in Volume
8

