

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**  
**c/o 111 So. Meramec**  
**Clayton, Missouri 63105**  
**314.615.1635**  
**Ric\_Cavanagh@Stlouisco.com**

September 7, 2001

**MEMORANDUM**

TO: Oversight Committee Members  
Other Interested Parties

FROM: Richard R. Cavanagh, CHE  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, September 14, 2001, at 11:30 am, in the trailers on Latty Ave. Summary minutes from the August 10 meeting will be provided at that meeting.

Committee members who cannot attend should contact the chairperson at the above numbers to be excused.

Thank you.

:RRC



US Army  
Corps of Engineers  
St. Louis District

# FUSRAP



Gateway to Excellence

## St. Louis Oversight Committee Meeting *Corps Update*

10 AUGUST 01



August 2001

1



US Army  
Corps of Engineers  
St. Louis District

## Agenda



Gateway to Excellence

- Mississippi Valley Division
- Progress Report
- Community Interactions
- Taskers
- Questions

August 2001

2




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

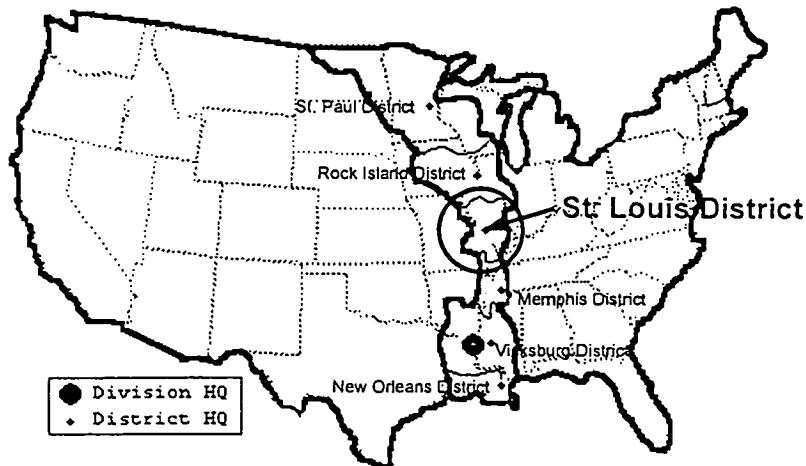

3



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- Remedial Design
  - Work Description for Phases 2 / 3 (IA2 / 3) - REV A under review
  - Work Description for Phases 4 / 5 (IA1 - adjacent to Coldwater Creek) - DBM in process
  - Currently finalizing Site Wide Grading Plan - Will be coordinated with the Airport Authority.
- Removal Actions
  - East End - Excavation ongoing in the Eastern End Right of Way
    - The contractor is currently excavating at SU12 & SU13
      - SU 9 is currently being backfilled and 11 is in the Final Status Survey process
    - 45,000 cyds expected, 33,694 cyds excavated to date
  - Status of water treatment system
    - Pilot plant testing is complete, results are pending
    - Received final MSD response to discharge application
  - Rail Shipments off SLAPS
    - 38,723 cyds shipped to date / 60,000 planned. No further shipments are expected this FY.
    - Soil will be stockpiled on the loadout pad.

August 2001

4



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- Remedial Design
  - Main Pile North Half - 9,500 cyds
    - Proposal with contractor, due 14 August
    - Target start date is early SEP with completion early in FY02 (6 weeks work effort).
- Remedial Action
  - GIFREHC - Continue Working Right of Entry for roof work
    - MVS responded to the latest RoE proposal from GIFREHC on roof replacement costs / schedule.
    - MVS will support GIFREHC contractor by conducting radiological support, transportation and disposal associated with the roof removal.
    - GIFREHC has indicated that they will either split the work between this fall and next spring or delay the project until next spring.
      - Work is not likely to start until at least 30 days after a signed agreement
  - Rail Shipments off HISS
    - 25,694 cyds shipped to date / 20,000 cyds planned

August 2001

5



US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- Data Evaluation
  - VP removal action assessments on hold for 30 DoE remediated properties.
    - Document has completed internal review and will be sent for regulator review by 15 AUG.
- Characterization Surveys / Remedial Design
  - Continue to gain real estate access to properties to obtain walkover and sampling data for Plans and Specifications in FY01
    - 56/57/58/59/1C & Pershall & I-270 ROW (@2,000 cyds) - on hold
    - 9/10/11/12 & Hotspots in the ballfields and IA 10 - 90% design submitted - on hold
- Working with MoDOT for 2001
- MVS sampling report is being finalized, after which we will schedule a meeting with St. Louis County Highways and Traffic to discuss remediation of areas under the shoulder of McDonnell Blvd.
  - 3 areas under the shoulder, from 3 to 5 feet deep, have been identified.
- Remedial Action - None scheduled for this FY
  - Rail Shipments of VP soils (Shipped from HISS)
    - 0 cyds planned; however, based on funding / utility work, the number could increase

August 2001

6



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- Remedial Design
  - Pre Design Investigation - Mallinckrodt West, Plant 7N/7S, McKinley Bridge, Cash, Christiana, Star Bedding and Thomas / Proetz Lumber are currently pending or under review
  - Work Description for Small Area Remediation - REV 0 published 4 MAY
    - Heintz Steel due 15 SEP.
    - Working with MDNR on potential dioxin at PSC Metals / McKinley Bridge shadow area
- Remedial Action
  - Plant 2 PRAR is under regulator review. Comments due 30 AUG.
  - Plant 1 continues (@2,750 cyds) - 2,545 cyds remediated to date
    - Current completion date is 30 SEP 01. 4 small areas remain.
  - Plant 6E / 6E1/2 (15,000 cyds) began 3 DEC - 9,030 cyds remediated to date
    - Phase I excavation continues. North / South sewer will need to be replaced. New completion date is FEB 02.
  - VP's - Midwest Waste (950 cyds) - 910 cyds removed to date. 7 of 14 areas in FSS.
    - MSD Lift Station - Currently finalizing release letter to City.
  - Rail Shipments off SLDS
    - 9,227 cyds shipped / 7,500 planned
    - Soil is currently being stockpiled at the SLDS and Midwest Waste - 1,000 cyds

August 2001

7



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- North County Feasibility Study/ Proposed Plan
  - FS/PP regulator review is the next step. Expected to begin @ Labor Day.
    - Updated cost data has been added to the FS/PP
    - Provided a response to the MDNR follow on ARAR's question
    - USACE has developed the Administrative Record to date
- Stockpiling of soils will occur at SLDS and SLAPS due to funding constraints.
- Long Term Stewardship
  - DoE LTS program POC's will tour the St. Louis Sites on 14 OCT.
  - LTS Meeting held 9 AUG. Plan outline development is next. Next meeting 25 OCT.
  - Long Term Stewardship Workshop 30 JUL - 2 AUG in Grand Junction
  - 20 AUG - ASTSWMO meeting in Tampa will discuss Stewardship Issues
- Status of MDNR request for additional funding under the Cooperative Agreement.
  - \$50,000 will be provided for the remainder of the FY.
- DoE Program POC's interactions - New POC's have been appointed.
- The Army Audit Agency continues their audit of our FUSRAP - Draft is under internal review.
  - Another audit, focused on Transportation and Disposal is underway.

August 2001

8




US Army  
Corps of Engineers  
St. Louis District

## Volume Shipped Using Environmental Documents



Gateway to Excellence

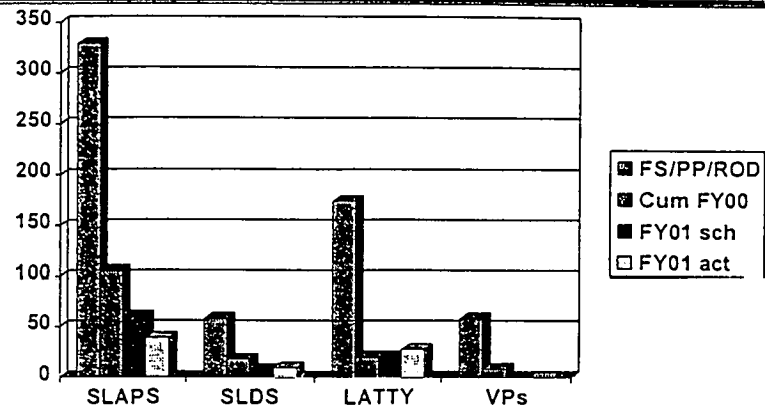

Note 1. North County volumes are based on the North County FS/PP  
Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal  
Note 3. SLDS volumes do not include inaccessible  
August 2001

9



US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- Recent Events
  - Nowclotter published and distributed.
  - Developing abstracts for Waste Management 02 Conference
- Upcoming Events

August 2001

10



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- Old Taskers
  - Provide the Oversight Committee copies of correspondence on water treatment (Complete - MSD letters provided)
  - Will SLOC be able to review the AAA report or will it be classified as an internal review document? (No - Complete)
  - How much does the NRC / CoE MOU apply to Mallinckrodt? (Complete)
- New Taskers

August 2001

11



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions? Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?

August 2001

12

# FUSRAP Document Management System

Year ID

00 2741

Further Info?

☐

Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs/Community Relations

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting Minutes from August 10, 2001 Meeting

Author/Originator

Richard Cavanagh

Company

Oversight Chairman

Date

9/7/01

Recipient (s)

Distribution

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?

☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

- ☐ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL

8.10

Filed in Volume

