

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

*c/o 111 So. Meramec*

*Clayton, Missouri 63105*

*314.615.1635*

*Ric\_Cavanagh@Stlouisco.com*

October 4, 2001

**MEMORANDUM**

TO: Oversight Committee Members  
Other Interested Parties

FROM: Richard R. Cavanagh, CHE  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, October 12, 2001, 11:30 am at the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

*c/o 111 So. Meramec  
Clayton, Missouri 63105  
314.615.1635  
Ric\_Cavanagh@Stlouisco.com*

Summary of September 14, 2001 Meeting

Committee Members Present: Jim Grant, Tom Binz, Ric Cavanagh, Sally Price

Other Interested Parties: Jack Fraenhoffer, Larry Erickson, Eric Gilstrap, Bill Fitzgerald, David Wagoner, Bob Marchant, Lou Dell'Orco, Jacqui Mattingly

The following comments are in addition to the information in the handouts provided by USACE (see attached).

Page 4 - 4/5/6 are the last remaining phases. There probably will be no additional funds available this year.

Page 5 - There will be nothing going on at this site until 9/10. Contractors are now using gondolla cars with lids, which then cover the burrito bags. This has slowed down the rate of work but proven effective in controlling the content of the cars.

Page 6 - Saint Louis County Highways and Traffic has been much more cooperative regarding this project.

Page 7 - Mallinckrodt West is Plant 11. Lots of dirt will be shipped out from this site in the next fiscal year (starting October 1). The state has raised issues regarding institutional controls (ie. concern regarding clean up to industrial standards only).

Page 8 - North County FS/PP public hearing now will likely be after the first of January. Project staff acknowledge that USACE's proposals do vary from the Task Force proposals for clean up standards. USACE proposal is based on findings of risk scenarios.

Page 9 - Over 100,000 cyds moved year to date. The volume has been increasing every year.

Larry Erickson of MDNR reported that (1) DOE and USACE headquarters staff have been meeting to resolve issues and (2) EPA has announced that they will not be signing off on ROD's without a Long Term Stewardship plan in place.

Next Meeting  
Friday, October 12, 2001  
11:30 am  
Latty Ave. Trailers



US Army  
Corps of Engineers  
St. Louis District


# **FUSRAP**



Gateway to Excellence

## **St. Louis Oversight Committee Meeting Corps Update**

14 SEPTEMBER 01

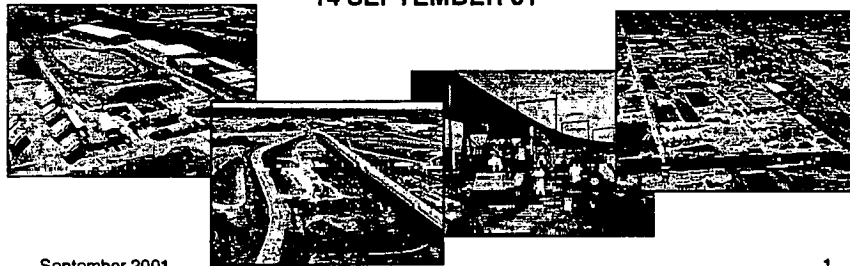

September 2001

1



US Army  
Corps of Engineers  
St. Louis District

## **Agenda**



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

September 2001

2




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

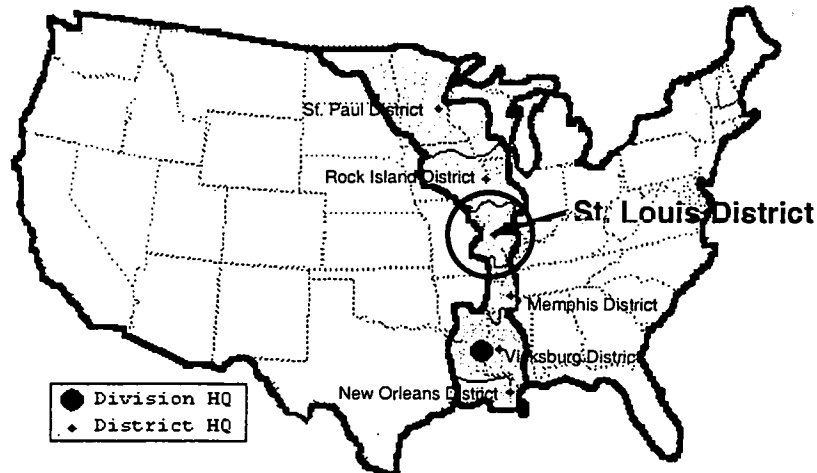

3



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
  - **Work Description for Phases 2 / 3 (IA2 / 3)** - Published
    - Work Description for Phases 4 / 5 / 6 (Remainder of SLAPS) - DBM in process
    - Site Wide Grading Plan - Meeting with the Airport Authority 19 SEP prior to finalizing.
- **Removal Actions**
  - **East End - Excavation ongoing in the East End**
    - The contractor is currently excavating at SU12
      - SU 11 is currently being backfilled, SU 12 is in the Final Status Survey process
    - 65,000 cyds expected, 39,942 cyds shipped to date, 15,000 cyds stockpiled
      - Approximately 55,000 cyds have been excavated.
  - **Status of water treatment system**
    - Expect plant to arrive on site within 2 weeks, equipment is being mobilized.
  - **Rail Shipments off SLAPS**
    - 44,971 cyds shipped to date / 60,000 planned. No further shipments are expected this FY.
      - 572 cars were shipped
    - Soil stockpiled on the loadout pad - 15,000 cyds.

September 2001

4



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Remedial Design** - None at this time
- **Remedial Action**
  - **Main Pile North Half - 9,500 cyds**
    - Notice to proceed issued. Contractor began work 10 SEP
    - Target completion date is end of OCT
    - 160 cyds shipped to date
  - **GIFREHC - Roof Replacement**
    - MVS and GIFREHC have agreed to a RoE for the GIFREHC roof replacement.
    - MVS will support GIFREHC contractor by conducting radiological support, transportation and disposal associated with the roof removal.
    - GIFREHC has indicated that they will either split the work between this fall and next spring or delay the project until next spring.
      - Work is not likely to start until mid OCT
  - **Rail Shipments off HISS**
    - 27,353 cyds shipped to date / 20,000 cyds planned

September 2001

5



US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Data Evaluation**
  - Assessment of the 30 DoE remediated properties.
    - Document is under regulator review - comments due 18 SEP.
- **Characterization Surveys / Remedial Design**
  - **Continue to gain and renew real estate access to properties to obtain walkover and sampling data for Plans and Specifications in FY01**
    - 56/57/58/59/1C & Pershall & I-270 ROW (@2,000 cyds) - PDI and DBM working
    - 9/10/11/12 & Hotspots in the ballfields and IA 10 - 90% design submitted - on hold
- **Working with MoDOT for work to be done at Pershall / I-170**
  - Awaiting archived samples for analysis (Contractor is moving)
- **MVS met with the St. Louis County Highways and Traffic to discuss remediation of areas under the shoulder of McDonnell Blvd.**
  - 7 areas under the shoulder, from 3 to 5 feet deep, have been identified.
  - SLCH agreed to let USACE remediate these areas up to the edge of pavement
- **Remedial Action - None scheduled for this FY**
  - **Rail Shipments of VP soils (Shipped from HISS)**
    - 0 cyds planned, however, based on funding / utility work, the number could increase

September 2001

6



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
  - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Christiana, Star Bedding and Thomas / Proetz Lumber are currently pending or under review
    - Collins currently not allowing access
  - **Work Description for Small Area Remediation - REV 0 published 4 MAY**
    - Heintz Steel, McKinley Bridge, Gunther Salt working.
    - PSC Metals complete
- **Remedial Action**
  - **Plant 2 PRAR regulator review comments received. Working response.**
  - **Plant 1 continues (@3,500 cyds) - 3,352 cyds remediated to date**
    - Current completion date is 28 SEP 01. 4 small areas remain.
  - **Plant 6E / 6E1/2 (12,000 cyds) began 3 DEC - 10,065 cyds remediated to date**
    - Phase I excavation continues. New completion date is FEB 02.
  - **VP's - Midwest Waste (1,500 cyds) - 1,020 cyds removed to date. 7 of 14 areas ready for FSS; however, crews have been shifted to complete Plant 1.**
    - **MSD Lift Station** - Sent release letter to City and MSD.
  - **Rail Shipments off SLDS**
    - 11,229 cyds shipped / 7,500 planned

September 2001 Soil is currently being stockpiled at the SLDS - 5,000 cyds

7



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
  - Document is currently at HQ, CX and MVD for modified review
  - FS/PP regulator review is the next step.
- **Stockpiling of soils is ongoing at SLDS and SLAPS due to funding constraints.**
  - Approximately 20,000 cyds are stockpiled between SLDS and SLAPS
- **Long Term Stewardship**
  - DoE LTS program POC's toured the St. Louis Sites on 14 AUG.
  - Next LTS Meeting is 25 OCT. Plan outline development is ongoing.
- **FUSRAP Program Review will be held in St. Louis 24/25 OCT**
- **Status of MDNR request for additional funding under the Cooperative Agreement.**
  - \$50,000 was provided for the remainder of the FY.
- **DoE Program POC's interactions -**
  - A Corps liaison, ex Corps employee, has been appointed.
- **The Army Audit Agency continues their audit of our FUSRAP - Comments were submitted to AAA for first audit - next step is to consider comments and finalize.**
  - The second audit, focused on Transportation and Disposal, continues.

September 2001

8




US Army  
Corps of Engineers  
St. Louis District

## Volume Shipped Using Environmental Documents



Gateway to Excellence

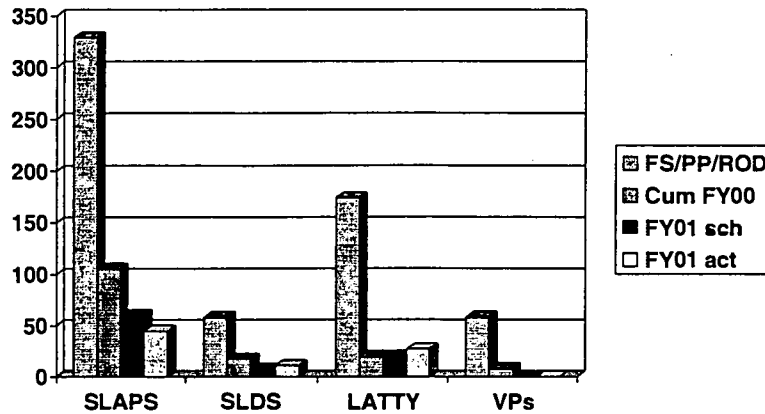

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Incitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles  
September 2001

9



US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- **Recent Events**
  - Submitted abstracts for Waste Management 02 Conference
- **Upcoming Events**
  - Publish newsletter in OCT

September 2001

10



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- **Old Taskers**
  - Will SLOC be able to review the AAA report or will it be classified as an internal review document? (Working)
  - How much has the AAA audits cost in terms of dollars (Working)
- **New Taskers**

September 2001

11



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions? Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?

September 2001

12



# FUSRAP Document Management System

Year ID

00 2807

Further Info?

☐

Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs/Community Relation

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting Minutes from September 2001 (9/14/01) meeting

Author/Originator

Richard Cavanagh

Company

St. Louis County DOH

Date

10/4/2001

Recipient (s)

Distribution

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?

☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

☒ North County

☐ Madison

☐ Downtown

☐ Iowa

ETL

8.10

Filed in Volume

8

