

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

*c/o 111 So. Meramec*

*Clayton, MO 63105*

*314.615.1635*

Ric\_Cavanagh@Stlouisco.com

February 4, 2002

**MEMORANDUM**

TO: FUSRAP Oversight Committee Members  
Other Interested Parties

FROM: Richard R. Cavanagh, CHE  
Chairperson

RE: Next Meeting

The next meeting of the FUSRAP Oversight Committee will be held on Friday, February 8, 2002, at 11:30am, in the trailers on Latty Avenue.

Committee Members who cannot attend should contact the Chairperson at the above numbers to be excused.

A summary of the January meeting will be distributed at this meeting.

Thank you.

:RRC



US Army  
Corps of Engineers  
St. Louis District


# ***FUSRAP***



Gateway to Excellence

## **St. Louis Oversight Committee Meeting *Corps Update***

11 JANUARY 02

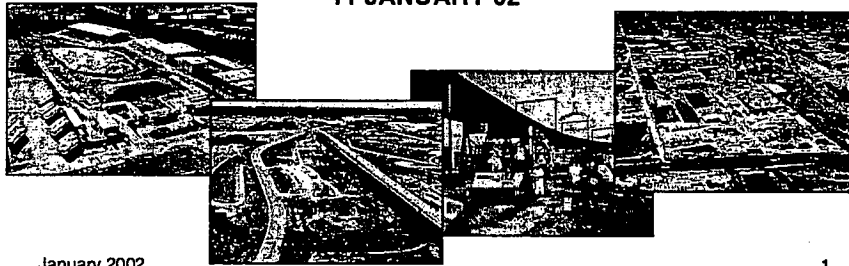

January 2002

1



US Army  
Corps of Engineers  
St. Louis District

## **Agenda**



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

January 2002

2




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

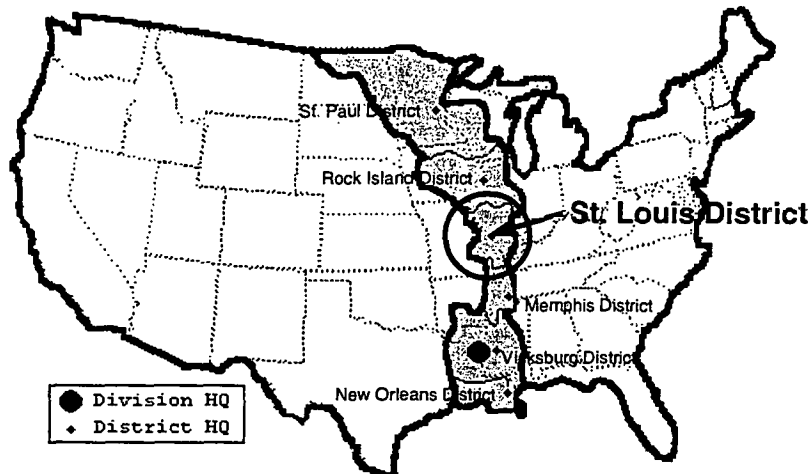

3



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
  - Pre Design Investigation for Phases 4 / 5 / 6 - Published 31 OCT
    - Addendum 1 for portion of Coldwater Creek (adjacent to Phases 4/5) - Due mid JAN
  - Work Description for Phases 4 / 5 - 60% due in FEB
  - Work Description for Phase 6 - 60% due in APR
- **Removal Actions**
  - **Began Phase I (IA5) excavation 10 DEC** - 43,000 cyds expected
    - 6,088 cyds removed to date. Working in SU23 /24 (Middle of site, S of Radium Pits)
  - **East End - Excavation is substantially complete** - 58,044 cyds removed
    - The contractor is currently backfilling to grade
  - **Status of water treatment system** - Next Bench test scheduled for 6 FEB
    - System is being modified / equipment being changed to ensure it meets contractual specifications
  - **MVS and MDNR FFG met with MDNH water Pollution Control 17 DEC**
    - Discussed removal of Outfall 3 from SLAPS permit equivalent and reduced sampling on Outfall 2 due to remediation completed to date.
  - **Rail Shipments off SLAPS**
    - 24,221 cyds shipped to date / 50,000 planned.

January 2002

4



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Remedial Design** - None at this time
- **Removal Actions** - None at this time
  - **GIFREHC**
    - **Roof Replacement**
      - MVS support of the GIFREHC roofing contractor, which consists of providing radiological support, transportation and disposal associated with the roof removal, is on hold due to weather and will resume in the spring.
      - 8 of 63 areas removed and replaced to date.
      - 4,000 cyds are expected. 222 removed to date
    - **Entrance Pad Assessment**
      - USACE took samples under the entrance pad to GIFREHC in anticipation of upcoming removal and replacement - no concentrations found above background.
  - **Rail Shipments off HISS**
    - 3223 cyds shipped to date / 5,000 cyds planned

January 2002

5



US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Data Evaluation**
  - Assessment of the 30 DoE remediated properties.
    - Regulator review comments received. Currently working responses.
- **Characterization Surveys / Remedial Design - No Change**
  - **Designs are on hold, expected to be completed by the end of FY02**
    - 56/57/58/59/1C & Pershall & I-270 ROW (@2,000 cyds) - 60% design on hold
    - 9/10/11/12 & Hotspots In the ballfields and IA 10 - 90% design submitted - on hold
- **Working with MoDOT for work to be done at Pershall / I-170**
  - Archived samples are pending analysis
- **Supporting proposed property improvements at VP24.**
  - Sample results are pending.
- **Contract for remediation of VP's cancelled**
  - Preplaced Remedial Action Contract (PRAC) delayed due to funding and North County ROD
- **Remedial Action - None to date**
  - **Rail Shipments of VP soils**
    - 700 cyds planned; 0 expected this FY

January 2002

6



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **No remediation letters** - Working "model" letter for Thomas and Proetz (DT-10)
- **Remedial Investigation** - USACE assembling data for Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - Draft expected in FEB.
- **Remedial Design**
  - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Christiana, Star Bedding, Collins, Cotto Waxo and Thomas / Proetz Lumber are currently in progress
  - **Work Descriptions - REV 1's may be issued after PDI re-evaluation**
    - PSC Metals, Heintz Steel complete. McKinley Bridge, Gunther Salt working.
    - ADM showed no elevated levels during re-evaluation, PSC Metals re-evaluation ongoing.
- **Remedial Action**
  - **Plant 2 PRAR** - Response to comments sent. PRAR being finalized.
  - **Plant 1 continues (@3,650 cyds) - 3,625 cyds remediated to date**
    - Current completion date is FEB 02. 1 small area remains (@ 25 cyds)
  - **Plant 6E / 6E1/2 (15,000 cyds) began 3 DEC 00 - 13,042 cyds remediated to date**
    - Phase I excavation continues. Completion date is MAY 02 due to Plant 1 delays.
  - **VP's - Midwest Waste (1,500 cyds) - 3,339 cyds removed to date. 95% complete.**
  - **Rail Shipments off SLDS**
    - 5,549 cyds shipped / 15,000 planned

January 2002

7



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
  - USACE comments, including OC in the HTRW-CX, have been received and the responses are being finalized. Issues exist with the CX OC comments.
  - CX issue resolution and FS/PP regulator review are the next steps.
- **Long Term Stewardship - Next meeting is 24 JAN**
  - LTS document development is ongoing.
  - Responsibilities for writing split between MVS and MDNR
- **DoE Program POC's interactions -**
  - None during this timeframe
- **The Army Audit Agency continues their audits**
  - Audit 1 - Expected to be final within 2 months (MAR 02)
  - Audit 2 - Draft for internal USACE comment expected in MAR 02.
- **Possible strike at MI on 1 MAR** - Should not effect MVS operations at SLDS
- **MVS SLDS TERC (IT Corp)** - Expect company to be bought this month. Should not effect site operations.
- **Bi-Annual Utility Policy Meeting**
  - Held 11 JAN 02.

January 2002

8




US Army  
Corps of Engineers  
St. Louis District

## FY 02 Volume Shipped Using Environmental Documents



Gateway to Excellence

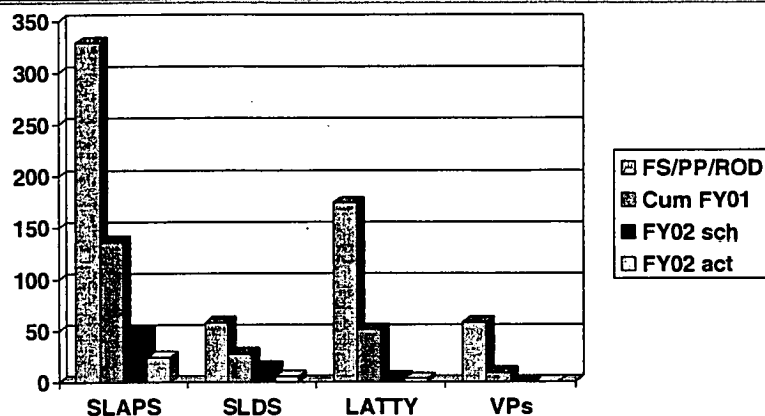

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles  
January 2002

9



US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- Recent Events
  - None
- Upcoming Events
  - Publish Newsletter - FEB 02

January 2002

10



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- **Old Taskers**

- Put the updated maps of the Phases of SLAPS and properties at SLDS in the next newsletter (Working)
- The Oversight Committee will meet to discuss how to increase public awareness on clean up standards and LTS (Ongoing - Meeting held)
- Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)

- **New Taskers**

January 2002

11



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions? Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?

January 2002

12

# FUSRAP Document Management System

Year ID  
00 3015

Further Info?  
☐

Operating Unit  
St. Louis Sites

Site

Area

MARKS Number  
FN:1110-1-8100g

Primary Document Type  
Public Affairs/Community Relation

Secondary Document Type  
Public Meeting Minutes/Transcripts

## Subject or Title

St. Louis Oversight Committee Meeting Minutes from January 11, 2002

Author/Originator  
Richard Cavanagh

Company  
St. Louis County DOH

Date  
1/11/2002

Recipient(s)  
Distribution

Company (-ies)

Version  
Final

Original's Location  
Central Files

Document Format  
Paper

Confidential File?  
☐

## Comments

SAIC number

Bechtel ID

## Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL  
8.10

Filed in Volume  
8

