

**ST. LOUIS FUSRAP OVERSIGHT COMMITTEE**

*c/o 111 So. Meramec*

*Clayton, MO 63105*

*314.615.1635*

Ric\_Cavanagh@Stlouisco.com

April 5, 2002

**MEMORANDUM**

TO: St. Louis FUSRAP Oversight Committee  
Other Interested Parties

FROM: Richard R. Cavanagh, CHE  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, April 12, 2002, 11:30 am, in the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

***ST. LOUIS FUSRAP OVERSIGHT COMMITTEE***

*c/o 111 So. Meramec*

*Clayton, MO 63105*

*314.615.1635*

*Ric\_Cavanagh@Stlouisco.com*

Summary of Meeting

March 8, 2002

Committee Members Present: Jim Grant, Jon Lagerak, Ric Cavanagh, Jan Titus, Sally Price.

Committee Members Excused: Bill Brandes, Tom Manning

Other Interested Parties: Sharon Cotner, Lou Dell'Orco, Mike Zlatic, Angela Minor, Larry Erickson, Eric Gilstrap, Jack Fraenhoffer

The following information is in addition to the handouts provided by USACE.

Page 4 - Contractor has one more chance to meet deliverables for Water Treatment.

Page 6 - The Right of Entry issue has been resolved with Midwest Waste but now Midwest is talking about selling their property. (If this happens there is no guarantee that we will cooperation from the new owner).

Page 7 - North County ROD - staff are considering a public hearing if the technical issues cannot be resolved. The Committee expressed concern about the current delays with getting this ROD. The Committee will work with staff to do what is necessary to move this process along.

**NEXT MEETING**

Friday, April 12, 2002

11:30 am

Trailers on Latty Ave.



US Army  
Corps of Engineers  
St. Louis District


# ***FUSRAP***



Gateway to Excellence

## **St. Louis Oversight Committee Meeting *Corps Update***

8 MARCH 02

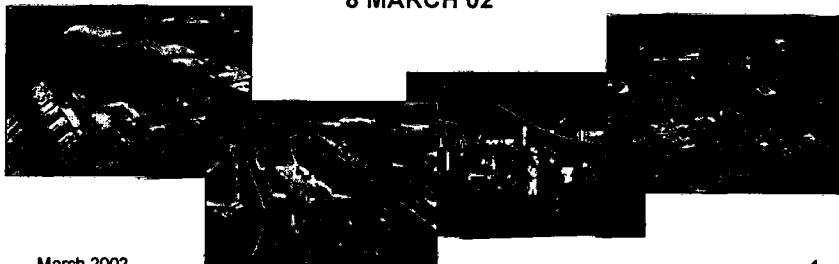

March 2002

1



US Army  
Corps of Engineers  
St. Louis District

## **Agenda**



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Excavation to Backfill Process**
- **Taskers**
- **Questions**

March 2002

2




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

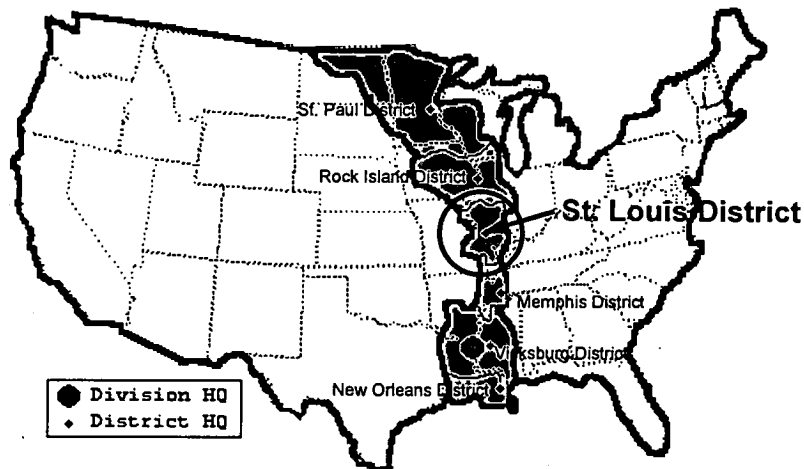

3



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Investigation**
  - Walkover of Airport Authority property S of Banshee Road pending
- **Remedial Design**
  - **Work Description for Phases 4 / 5** - 60% under internal MVS review, hold at 90%
    - Addendum 1 for the portion of Coldwater Creek adjacent to 4/5 is pending.
  - **Work Description for Phase 6** - 60% due in APR, hold at 90% this FY.
- **Removal Actions**
  - **Began Phase I (IA5) excavation 10 DEC** - 43,000 cyds expected
    - 14,334 cyds removed to date. Phase 1 has been removed to 1' above the water table.
    - 1,000 cyds have been removed from SU 14 - 50% complete, SU 22 is next.
    - Need to relocate site support trailers to east end before further removals can take place.
  - **Status of water treatment system** - Bench test was completed - did not meet standard.
    - Contractor was defaulted. Working on next course of action.
  - **MVS and MDNR FFS met with MDNR Water Pollution Control 17 DEC**
    - Received approval for removal of Outfall 3 from SLAPS permit equivalent and reduced sampling on Outfall 2 due to remediation completed to date.
  - **Rail Shipments off SLAPS**
    - 32,467 cyds shipped to date / 50,000 planned.

March 2002

4



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
  - Meeting with MDNR Water Pollution Control on sampling at HISS today.
  - GIFREHC Roof Replacement
    - MVS support of the GIFREHC roofing contractor will resume @ 18 MAR.
    - 8 of 63 areas removed to date. 4,000 cyds are expected. 300 removed to date
  - Rail Shipments off HISS
    - 3301 cyds shipped to date / 5,000 cyds planned
- **SLAPS VP's**
  - Data Evaluation
    - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
  - Designs are on hold and expected to be completed in FY03
    - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Bailfield hotspots
  - Supporting Pershall Utility / I-170 MoDoT work
    - No contamination above criteria was identified:
      - in Pershall east of the Hazelwood / Pershall intersection for the I-170 MoDoT work.
      - In the shoulders of Pershall west of the Hazelwood / Pershall intersection in support of the Missouri American Water Line Utility support.
  - Supporting proposed property improvements at VP 24 and 56/57.

March 2002 Sample results show some contamination at 24, MVS is currently bounding.  
• 56/57 cleared for installation of a fire suppression system.

5



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **No remediation letters** - Working issue within the Corps. Meeting with Thomas and Proetz next week.
- **Remedial Investigation** - USACE assembling data for Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - Internal USACE draft is under review.
- **Remedial Design**
  - Pre Design Investigation - Mallinckrodt West, Plant 7N/7S, Christiana, Star Bedding, Collins, Cotto Waxo and Thomas / Proetz Lumber are currently on hold
  - Work Descriptions - REV 1's may be issued after PDI re-evaluation
    - PSC Metals, Heintz Steel, Thomas and Proetz and McKinley Bridge deep soils evaluation working. Also working additional PDI issues at McKinley Bridge.
- **Remedial Action**
  - Plant 1 continues (@3,750 cyds) - 3,724 cyds remediated to date
    - Remediation is complete. Authorization to backfill is pending on area 7/8w.
  - Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 13,304 cyds remediated to date
    - Excavation and backfill of Phase I Survey Units continues. Completion date is DEC 02.
  - VP's - Midwest Waste (4,500 cyds) - 4,322 cyds removed to date, spot excavation is ongoing. Expect completion in MAY 02.
  - ADM (DT-1) - Final Status Survey is under internal review.
  - Rail Shipments off SLDS
    - 8,784 cyds shipped / 15,000 planned

March 2002

6



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
  - USACE comments, including QC in the HTRW-CX, have been received and the responses are being finalized. Issues exist with the CX QC comments - MVS working response
  - CX issue resolution and FS/PP regulator review are the next steps.
- **Long Term Stewardship - Next meeting is 21 MAR**
  - Meeting was held 24 JAN. LTS document development is ongoing
  - DoE may be coming to view site next week - pending scheduling issues
- **DoE Program POC's interactions -**
  - None during this timeframe
- **The Army Audit Agency continues their audits**
  - Audit 1 - Final copy has been released at the HQ level, expect receipt next week at the site
  - Audit 2 - Draft for internal USACE comment expected in MAR 02.
- **Met with MDNR on out years funding 4 MAR**
- **Possible strike averted at MI on 1 MAR**
- **MVS SLDS TERC (IT Corp) -** Company is in the process of being purchased, most likely by the Shaw Group. Site operations have not been affected to date.

March 2002

7




US Army  
Corps of Engineers  
St. Louis District

## FY 02 Volume Shipped Using Environmental Documents



Gateway to Excellence

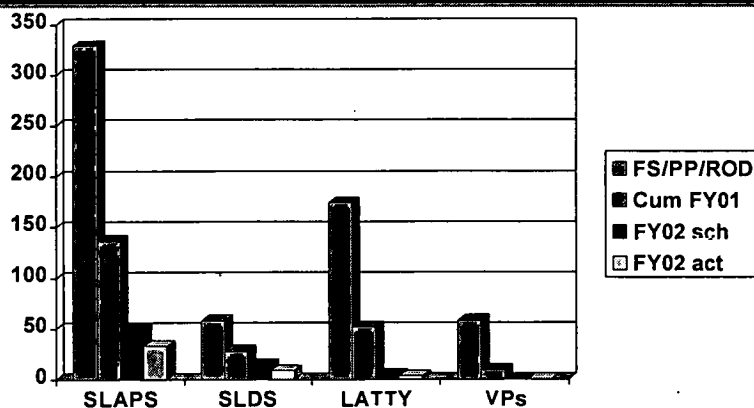

Note 1. North County volumes are based on the North County FS/PP  
 Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal  
 Note 3. SLDS volumes do not include Inaccessibles  
 March 2002

8



US Army  
Corps of Engineers  
St. Louis District



Gateway to Excellence

## Community Interactions

- **Recent Events**

- Newsletter Published - FEB 02
- Briefed at Incarnate Word Science Olympiad - 28 FEB

- **Upcoming Events**

- None at this time.

March 2002

9



US Army  
Corps of Engineers  
St. Louis District



Gateway to Excellence

## Taskers

- **Old Taskers**

- Put the updated maps of the Phases of SLAPS and properties at SLDS in the next newsletter (Complete)
- The Oversight Committee will meet to discuss how to increase public awareness on clean up standards and LTS (Ongoing - Meeting held)
- Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)

- **New Taskers**

March 2002

10



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions? Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?  
Questions? Questions?

March 2002

11



# FUSRAP Document Management System

Year ID  
00 3149

Further Info?  
☐

Operating Unit  
St. Louis Sites

Site

Area

MARKS Number  
FN:1110-1-8100g

Primary Document Type  
Public Affairs/Community Relation

Secondary Document Type  
Public Meeting Minutes/Transcripts

## Subject or Title

St. Louis Oversight Committee Meeting Minutes from the 3/08/02 meeting

Author/Originator  
Richard Cavanagh

Company  
St. Louis County

Date  
4/5/2002

Recipient (s)  
Distribution

Company (-ies)

Version  
Final

Original's Location  
Central Files

Document Format  
Paper

Confidential File?  
☐

## Comments

SAIC number

Bechtel ID

## Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL  
8.10

Filed in Volume  
8

