

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, MO 63105

314.615.1635

Ric_Cavanagh@Stlouisco.com

MEMORANDUM

TO: Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh, CHE
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, May 10, 2002, 11:30am, in the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, Missouri

314.615.1635

Ric_Cavanagh@Stlouisco.com

SUMMARY OF MEETING

April 12, 2002

Committee Members Present: Jim Grant, Ric Cavanagh, Tom Binz, Jon Langerak, Jan Titus, Sally Price.

Excused: Tom Manning

Other Interested Parties: Sharon Cotner, Lou Dell'Orco, Jack Frauenhoffer, Larry Erickson, Mike Zlatic

The following comments are in addition to the handouts provided by USACE staff at the meeting.

Page 4 – The water treatment contractor was terminated due to default (could not achieve objectives of the deliverables). Excavated soil is now being stockpiled due to (a) lack of funds until next fiscal year and (b) no valid water treatment solution.

Page 5 – GIFREHC contract claim (prior to transfer of project from DOE to USACE) has now been assumed by DOE (\$800,000). USACE staff will inform the Committee who the POC will be. VP 24 has a situation that could be precedent setting for future VP's. The property owner can't build because the soil has contamination above background levels, but not sufficiently high enough to meet the criteria for USACE clean up (unregulated material). If Long Term Stewardship is being required for the site, then there is no justification for high level clean up.

Page 7 – A meeting is scheduled for April 16 to resolve the one outstanding issue with the Center for Excellence (CX). It is believed that the Division Office in Vicksburg will make the final decision on criteria. St. Louis staff are to submit their response to questions by the end of May. It will take about thirty days for Division to make a decision. We need to force the issue by the end of June since there will be a change in command both locally and at the Division). It is expected that the earliest release of the FS/PP will be the end of June.

Recommendation from Audit 1 – need to do more work with Potentially Responsible Parties (PRP's).

NEXT MEETING: May 10, 2002, 11:30 am



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

12 APRIL 02

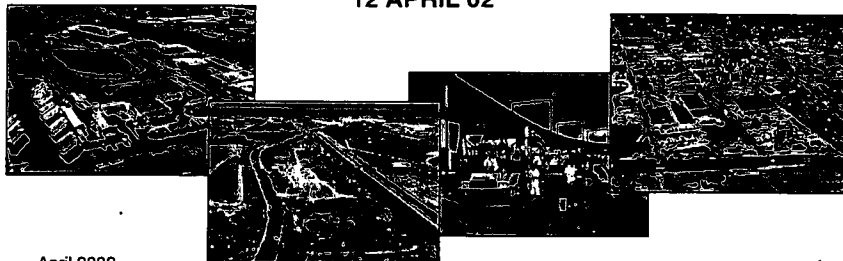

April 2002

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

April 2002

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

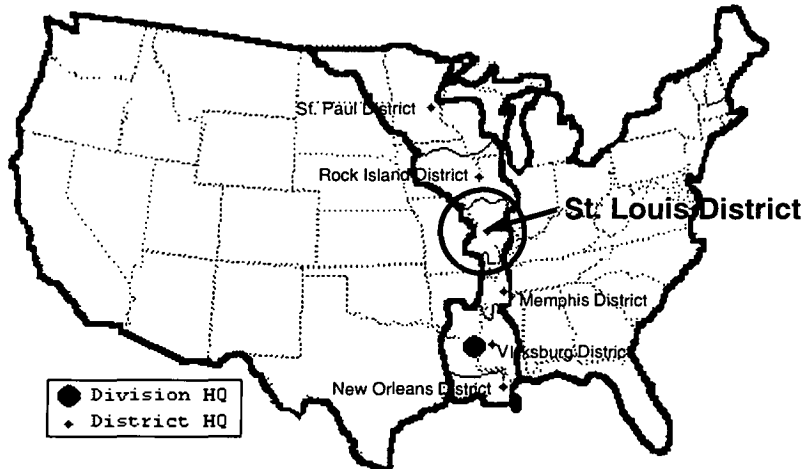

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Investigation**
 - Walkover of Airport Authority property S of Banshee Road is 95% complete - results will define nature and extent of contamination.
- **Remedial Design**
 - **Work Description for Phases 4 / 5** - 60% under internal MVS review, hold at 90%
 - Addendum 1 for the portion of Coldwater Creek adjacent to 4/5 is pending.
 - **Work Description for Phase 6** - 60% due in APR, hold at 90% this FY.
- **Removal Actions**
 - **Began Phase I (IA5) excavation 10 DEC** - 43,000 cyds expected
 - 16,050 cyds removed to date. Phase 1 has been removed to 1' above the water table.
 - Remediation of area adjacent to the edge of pavement along McDonnell Blvd is complete.
 - Site support trailers are in the process of being relocated to the east end to prior to resumption of removal actions in Phase 1.
 - **Status of water treatment system** - Bionitrification of batch of water begins 15 APR.
 - Bench study may proceed next. Alternatives including evaporation, electrocoagulation and land farming, among others, are being considered.
 - **Rail Shipments off SLAPS**
 - 34,989 cyds shipped to date / 50,000 planned.

April 2002

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Met with MDNR Water Pollution Control 8 MAR on sampling at HISS.
 - Only feedback to date is that USACE needs to remove the oversized debris on the site.
 - GIFREHC Roof Replacement
 - MVS support of the GIFREHC roofing contractor resumed 18 MAR.
 - 11 of 63 areas removed to date. 4,000 cyds are expected. 400 removed to date
 - Rail Shipments off HISS
 - 3301 cyds shipped to date / 5,000 cyds planned
- **SLAPS VP's**
 - Data Evaluation
 - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
 - Designs are on hold and expected to be completed in FY03
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - Supporting proposed property improvement at VP 24.
 - Approximately 120 cyds of material have been removed to date.
 - Rail Shipments from VP's
 - 0 planned, 120 cyds pending

April 2002

5



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **No remediation letters** - Working issue within the Corps. Met with Thomas and Proetz.
- **Remedial Investigation** - USACE assembling data for Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - Internal USACE draft is under review.
- **Remedial Design**
 - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Christiana, Star Bedding, Collins, and Cotto Waxo are currently on hold
 - **Work Descriptions** - REV 1's may be issued after PDI re-evaluation
 - Thomas and Proetz deep soils evaluation working. Heintz Steel is next.
 - Also working additional PDI issues at McKinley Bridge and PSC Metals.
- **Remedial Action**
 - **Plant 1 continues (@3,750 cyds) - 3,724 cyds remediated to date**
 - Remediation is complete. Beginning work on Post Remedial Action Report.
 - **Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 13,304 cyds remediated to date**
 - Excavation and backfill of Phase I Survey Units continues. Completion date is DEC 02.
 - **VP's - Midwest Waste (4,500 cyds) - 4,322 cyds removed to date, spot excavation is ongoing. Expect completion in MAY 02.**
 - **ADM (DT-1) - Final Status Survey comments received from MDNR.**
 - Residual does over the site is less than 1 mrem / yr for all modeled scenarios w/o cover.
 - **Rail Shipments off SLDS**

April 2002 — 8,829 cyds shipped / 15,000 planned

6



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - USACE comments, including OC in the HTRW-CX, have been received and the responses are being finalized. Issues exist with the CX OC comments - MVS working response
 - CX issue resolution and FS/PP regulator or public review are the next steps.
- **Long Term Stewardship - Next meeting is 27 JUN**
 - Meeting was held 21 MAR. LTS document development is ongoing
- **DoE Program POC's Interactions -**
 - None during this timeframe
- **The Army Audit Agency continues their audits**
 - Audit 1 - Received
 - Audit 2 - Draft for internal USACE comment expected in MAR 02.
- **Met with MDNR on out years funding 4 MAR**
- **MVS SLDS TERC (IT Corp)** - Company is in the process of being purchased, most likely by the Shaw Group. Site operations have not been affected to date.
- **HQSACE Chief Counsel** - Received a program briefing and toured the sites on 10 APR.

April 2002

7




US Army
Corps of Engineers
St. Louis District

FY 02 Volume Shipped Using Environmental Documents



Gateway to Excellence

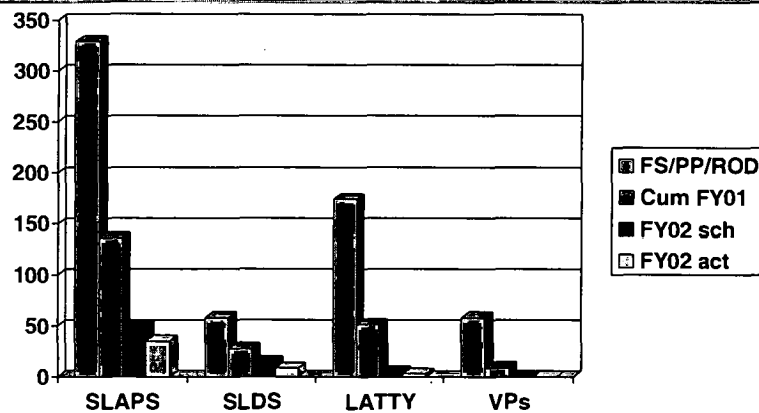

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles

April 2002

8



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Briefed SLDS Community Advisory Panel (CAP) - 9 APR
- **Upcoming Events**
 - Brief North Broadway Business Association (NBBA) - 17 APR

April 2002

9



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - The Oversight Committee will meet to discuss how to increase public awareness on clean up standards and LTS (Ongoing)
 - Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)
- **New Taskers**

April 2002

10



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? **Questions?** **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**

April 2002

11

FUSRAP Document Management System

Year ID

00 3162

Further Info?

☐

Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs/Community Relation

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis FUSRAP Oversight Committee Meeting Minutes (undated) from the 4/12/02 Meeting

Author/Originator

Richard Cavanagh

Company

St. Louis County

Date

4/12/2002

Recipient (s)

Distribution

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?

☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL

8.10

Filed in Volume

8

