

***ST LOUIS FUSRAP OVERSIGHT COMMITTEE***

*c/o 430 Adams St.  
St. Louis, MO 63135  
314-313-2959  
[rcavanagh@ltcop-stl.org](mailto:rcavanagh@ltcop-stl.org)*

**MEMORANDUM**

TO: Oversight Committee Members  
Other Interested Parties

FROM: Richard R. Cavanagh  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, September 10, 2004 at 11:30 am in the trailers on Latty Ave.

Committee members who cannot attend should contact the chairperson at the above numbers to be excused.

Thank you.

:RRC

***ST LOUIS FUSRAP OVERSIGHT COMMITTEE***

*c/o 430 Adams  
St. Louis, MO 63135  
314-313-2959  
[rcavanagh@ltcop-stl.org](mailto:rcavanagh@ltcop-stl.org)*

Summary of Meeting  
August 13, 2004

Committee Members Present: Tom Binz, Ric Cavanagh, Jim Grant, Michelle Morgenstern, Tom Manning

Committee Members Excused: Bill Brandes

Other Interested Parties: Larry Erickson, Ron Rauh, Gerald Allen, Sharon Cotner, Jacqueline Mattingly, Michael Zlatic, Eric Gilstrap

The following comments are in addition to the handouts provided by USACE at the meeting.

Page 5 – Coldwater Creek should be done by 8/20. Crews are working two, ten hour shifts daily, seven days/week. Some soil and debris in creek are questionable. They are being evaluated prior to disposal.

Page 7 – VP 13 which is just adjacent to SLAPS has been seeded and completed.

Page 9 – There is a question as to whether the new DOT regulations apply to that which is enroute or only to newly dug soil. The problem with intermodals is that they are harder work with and harder to get. The current condolas are on a long term lease.

Additional comments:

1. A representative from Senator Talent's office will tour the sites August 11.
2. The Assistant Secretary of the Army for Civil Works will tour the sites on September 1.
3. No additional funds have been received year to date, and it is unlikely that we will get any this fiscal year.
4. It is likely that the federal budget will again be under a CRA (continuing resolution authorization) through March.



US Army  
Corps of Engineers  
St. Louis District


# ***FUSRAP***



Gateway to Excellence

## **St. Louis Oversight Committee Meeting *Corps Update***

13 AUG 04

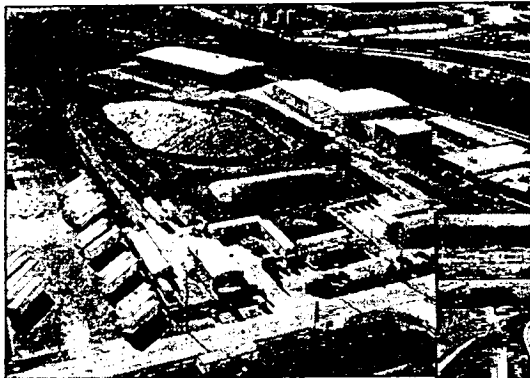


August 2004



US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
  - **MI - Plant 7N/S** PDIR out for regulator review. Design in progress.  
Plant 7W sampling complete. PDIR in progress.
  - **South of Anglerodt VPs –**  
Thomas & Proetz PDIR finalized. Design in progress  
Gunther- Sampling at north property continues. PDIR in progress.
  - **West of Broadway VPs –** Sampling complete.
- **Remedial Action**
  - **MI Plant 6W South of Bldg 101 –** Excavation ~½ way complete. Area 1 complete. Area 3 working. 2,254 cy excavated. (1,338cy shipped, remainder to be reused for backfill).
  - **Post Remedial Action Reports (PRARs) –** 4 in progress, Plant 1, Plant 7E, City of Venice (McKinley Bridge) and DT 6/7 (Heintz Steel / Midwest Waste).
  - **Rail Shipments –** 4,934 cy excavated this FY; 4,018 cy shipped. (5,000 cy planned for FY04).



US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design** – Phase 6 Sheetpile wall design under NS-RR review.
- **Removal Actions**
  - **Phase 2/3** - 85,000+ cy total shipped to date (43,000+ cy this FY).
    - No activities currently.
    - SU-35 utilized for one water storage basin.
  - **Phase 4/5** – ~37,000 cy shipped to date.
    - **Ameren/UE relocation complete.**
    - **Coldwater Creek** – *Initiated 5 Aug; nearing 50% complete.*
    - *SU-43 complete; SU-44 excavation and stone placement in-progress.*
  - **Phase 6** – RR signal line relocation in-progress; complete by e/o AUG.
  - **Water Storage / Water Treatment**
    - Minimum water being retained on site, currently.
    - 1 batch being prepared for discharge.
  - **Rail Shipments off SLAPS this FY**
    - 91,000 cy shipped to date / 85,000 cy planned.




US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## St. Louis Airport Site (SLAPS)



Gateway to Excellence

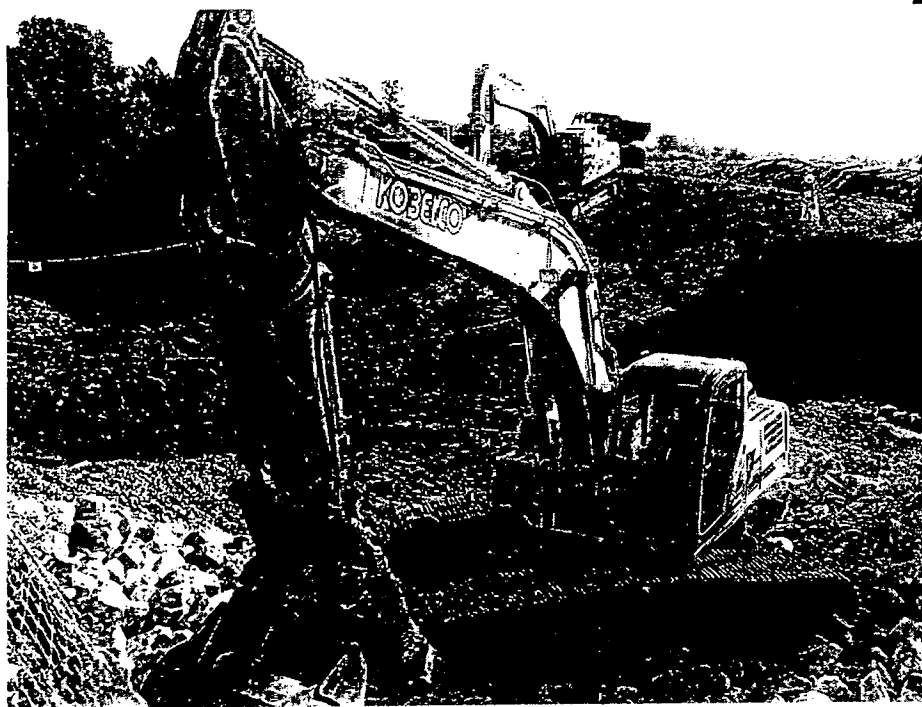

August 2004




US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS

---



Gateway to Excellence

- **HISS / Latty Avenue**
  - Group 1 VPs (2L, 3L, 4L, 5L) PreDesign Investigation (PDI) – Draft work plan .
  - VPs 1L, 8C and 40a Parcel – preparing Draft Summary Report
  - Rail Shipments off HISS – No shipments planned for FY04
- **SLAPS VP's**
  - Assessment of the 30 DoE remediated properties. Complete; issue after ROD.
  - Characterizations – On-going.
  - Designs are on hold in FY04
    - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
  - Utility Support – 19 this FY in N. Cty; mostly along haul road ROW.
  - VP-13 – Completed; 1,250 cy estimated excavation volume.
  - Rail Shipments from VP's – No shipments planned for FY04, however...
    - ~1,800 cy shipped from VPs – 10, 13 and 4C/5C.




US Army  
Corps of Engineers  
St. Louis District

# Volume Removed Using Environmental Documents



Gateway to Excellence

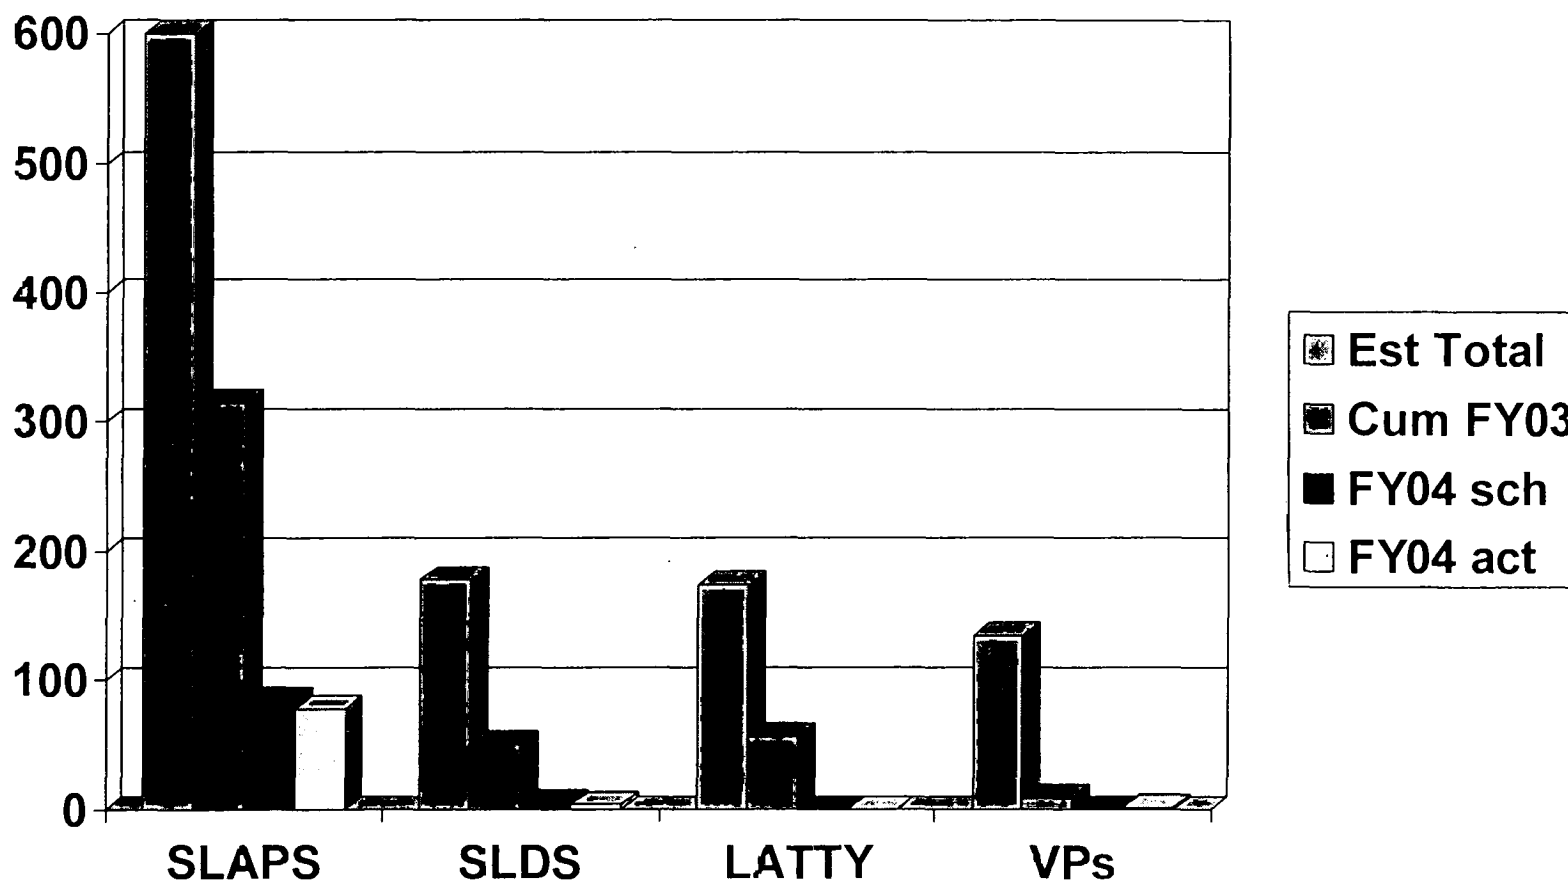

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles

August 2004





US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## Other Issues



Gateway to Excellence

- **New Transportation Regulations**
  - Request made for DOT exemption, to transport material via gondola cars, as currently done.
- **Long Term Stewardship -**
  - Next Meeting 13 AUG.
- **North County Haul Road Study** – Draft for Regulator review pending.
- **DoE Program POC (Jeff Short)** – No interactions during this timeframe.
- **CERCLA 5 year Review** – for all St. Louis FUSRAP Sites
  - Public review copy issued – 29 Jun.
  - Finalization of document pending.



US Army  
Corps of Engineers  
St. Louis District

# North County ROD Status




Gateway to Excellence

- **Current Status / Recent Events**
  - MVS revised responses and draft ROD (per 22-23 June discussion with EPA and MDNR) and issued to CX, MVD and HQ for concurrence.
  - Minor comments received. Document being revised for issuance.



US Army  
Corps of Engineers  
St. Louis District

# Community Interactions



Gateway to Excellence

- **Recent Events**

- **Five-Year Review** public review period closed – Jun 28.
- **Derivation of Site Specific DCGLs for N. County Structures** (DCGL doc) and memorandum explaining rationale.
  - Public notice published in Post Dispatch – 7 July. Letters issued to mailing list.
  - Request for extension received. Review period extended to 18 Aug.
  - Document available electronically via website, or paper copies w/ Admin Records.

- **Upcoming Events**

- Newsletter working



US Army  
Corps of Engineers  
St. Louis District

# Taskers



Gateway to Excellence

- **Old Taskers**
  - USACE to provide a summary briefing on the North County ROD – TBD.
  - USACE to schedule a time w/DOE Office of Legacy Management to brief Oversight Committee on Long-Term Stewardship – TBD.
  
- **New Taskers**



US Army  
Corps of Engineers  
St. Louis District

# Questions



Gateway to Excellence

**Questions?**

**Questions?**

**Questions?**

**Questions?**

*Questions?*

**Questions?**

**Questions?**

**Questions?**

**Questions?**

**Questions?**

**Questions?**

**Questions?**

# FUSRAP Document Management System

Year ID  
00 4451

Further Info?  
☐

Operating Unit  
North County

Site

Area

MARKS Number  
FN:1110-1-8100g

Primary Document Type  
Public Affairs/Community Relation

Secondary Document Type  
Meeting Minutes/Transcripts

## Subject or Title

St. Louis FUSRAP Oversight Committee Meeting Minutes dated 13 Aug 2004.

Author/Originator

Company  
Oversight Committee

Date  
8/13/2004

Recipient (s)

Company (-ies)

Version  
Final

Original's Location  
Central Files

Document Format  
paper

Confidential File?  
☐

Comments

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL

8.10

SAIC number

Filed in Volume

8

Bechtel ID

