



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

08 October 04



October 2004

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **North County ROD**
- **Community Interactions**
- **Taskers**
- **Questions**

October 2004

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

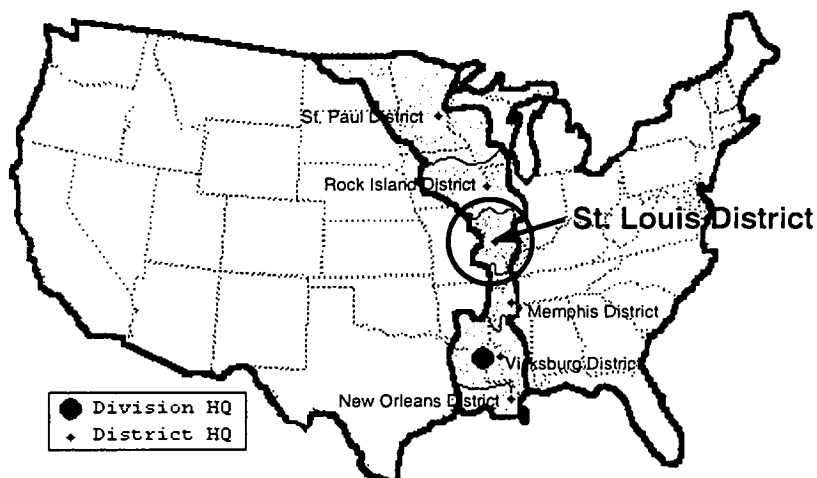

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
 - **MI - Plant 7N/S** PDIR Rev 0 issued. Design in progress. **Plant 7W** sampling complete. PDIR in USACE review.
 - **South of Anglerodt VPs** – **Thomas & Proetz** PDIR & Design finalized. **Gunther** Sampling complete. PDIR in progress.
 - **West of Broadway VPs** – Sampling complete.
- **Remedial Action**
 - **MI Plant 6W South of Bldg 101** – Excavation 95% complete. Areas 1 & 2 returned to MI. Soil nailing underway for remaining portion of Area 3 along Destrehan. 3,200 cy excavated. (appx. 500 cy to be reused).
 - **Post Remedial Action Reports (PRARs)** – 4 in progress: **Plant 7E**, **City of Venice (McKinley Bridge)**, **DT 6/7 (Heintz Steel / Midwest Waste)** and **Plant 10**. **Plant 1** PRAR finalized.
 - **Rail Shipments** – 6190 cy shipped. (5,000 cy planned for FY04).

October 2004

4



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design** – Phase 6 Sheetpile wall design being coordinated w/ NS-RR.
- **Removal Actions**
 - Main activity is grading/seeding of drainage ditch to CWC.
 - **Phase 2/3** - 89,000+ cy total shipped to date (46,000+ cy in FY04).
 - **Phase 4/5** – 45,000 cy shipped to date; SU-41 in-progress.
 - **Phase 6** – 11,700 cy shipped. Sheetpile wall construction next.
 - **Water Storage / Water Treatment**
 - 25 batches discharged this construction season.
 - **Rail Shipments off SLAPS in FY04**
 - 106,800 cy shipped to date / 85,000 cy planned for FY04.

October 2004

5



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Group 1 VPs (2L, 3L, 4L, 5L) PreDesign Investigation (PDI) – Draft work plan .
 - VPs 1L, 8C and 40a Parcel – preparing Draft Summary Report
 - Rail Shipments off HISS – No shipments planned for FY04
- **SLAPS VP's**
 - **Assessment of the 30 DoE remediated properties.** Complete; issue after ROD.
 - **Characterizations** – On-going.
 - **Designs are on hold in FY04**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Utility Support** – 1 this FY in N. Cty; 20 in FY04..
 - **Rail Shipments from VP's** – No shipments planned for FY04, however...
 - ~1,800 cy shipped from VPs – 10, 13 and 4C/5C.

October 2004

6




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

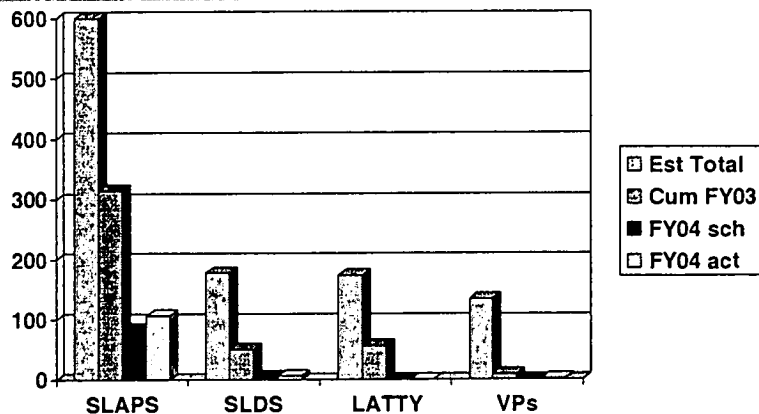

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles

October 2004

7



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **Funding** – operating under CRA 1 Oct – 20 Nov
- **New Transportation Regulations**
 - Request made for DOT exemption, to transport material via gondola cars, as currently done.
 - Still awaiting response
- **Long Term Stewardship** - Next Meeting in December.
- **North County Haul Road Study** – Draft under Regulator review.
- **DoE Program POC (Jeff Short)** – No interactions during this timeframe.
- **CERCLA 5 year Review** –Finalization of document pending.

October 2004

8



US Army
Corps of Engineers
St. Louis District

North County ROD Status



Gateway to Excellence

- **Current Status / Recent Events**

- MVS revised responses and draft ROD (per 22-23 June discussion with EPA and MDNR) and issued to CX, MVD and HQ for concurrence.
- Minor comments received and document was revised.
- Draft Final issued to EPA and MDNR on 13 Sep.

October 2004

9



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**

- Derivation of Site Specific DCGLs for N. County Structures (DCGL doc) and memorandum explaining rationale.
 - Response to comments issued 20 Sep 04.
 - Final expected later this month.

- **Upcoming Events**

- Newsletter working

October 2004

10



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Tour of SLAPS - Today
 - USACE to provide a summary briefing on the North County ROD – TBD.
 - USACE to schedule a time w/DOE Office of Legacy Management to brief Oversight Committee on Long-Term Stewardship – TBD.
- **New Taskers**

October 2004

11



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

October 2004

12

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 430 Adams St.

St. Louis, MO 63135

314-313-2959

rcavanagh@ltcop-stl.org

Summary of Meeting

October 8, 2004

Committee Members Present: Ric Cavanagh, Tom Manning, Michelle Morgenstern

Committee Members Excused: Bill Brandes, Jim Grant, Jack Fraenhoffer

Other Interested Parties: Jacque Mattingly, Sharon Cotner, Eric Gilstrap

The following comments are in addition to the handouts provided by USACE staff at the meeting.

Page 4 – 6W should be done the week of 10/18

Page 5 – some seeping along the Creek; most goals have been met or exceeded

Page 6 – one sewer support project for Boeing

Page 8 – Lou Dell 'Orco may be returning in January. The Long Term Stewardship Committee is meeting in December.

Funds from the CRA have been received. Eric Gilstrap of MDNR reported that the state has submitted preliminary comments on the ROD but staff are awaiting MDNR management's approval on actual wording of the comments.

Following the meeting, attendees had a very useful tour of SLAPS and HISS. Thanks to USACE staff for making these arrangements.

Next Meeting

Friday, November 12, 2004

11:30am

FUSRAP Document Management System

Year ID
00 4488

Further Info?
☐

Operating Unit
St. Louis Sites

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting dated 8 Oct 04

Author/Originator

Company

Date

10/8/2004

Recipient (s)

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

paper

Confidential File?

☐

Comments

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL

0810

SAIC number

Filed in Volume

08

Bechtel ID

