

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 430 Adams St.

St. Louis, MO 63135

314.313.2959

rcavanagh@ltcop-stl.org

MEMORANDUM

To: Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, January 14, 2005, 11:30 am, in the trailers on Latty Ave.

Members who cannot attend should contact the chairperson at the above numbers to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

*c/o 430 Adams St.
St. Louis, MO 63135
314.313.2959
rcavanagh@ltcop-stl.org*

Summary of Meeting

December 10, 2004

Committee Members Present: Tom Binz, Tom Manning, Michelle Morganstern, Jack Frauenhoffer, Ric Cavanagh, Jan Titus, Bill Brandes

Committee Members Excused: Jim Grant, Sally Price

Other Interested Parties: Larry Erickson, Eric Gilstrap, Debbie Roush, Mike Zlatic, Sharon Cotner

The following comments are in addition to the handouts provided by USACE staff at the meeting.

Page 4 – 262 cy taken out of Thomas and Proetz (There still is a small area behind the building where lumber is stored). One rail car derailed which has slowed some of the work in this area.

Page 5 – Staff met with airport on 2/7 re: final grading and future maintenance/back out strategy (the airport itself is considered a VP property). SLAPS should be done in FY 06. REQUEST: Give committee an update on the airport area (size, characterization)

Page 6 – HISS basically in on hold. Staff did coordinate some services with MSD

Page 8 – LTS: Debbie Roush will taking this over. Federal Facilities Agreement (FFA): state requested that they be a signatory, especially regarding LTS. The request was declined because of the resulting delays due to legal reviews.

Committee and staff agree that we need to get DoE actively involved in the LTS process once the ROD is signed.

Funding: Nationally, FUSRAP got an extra \$25 million in budget. St. Louis could easily use \$5 million more. This means that the national FUSRAP allocation jumped from \$140 million to \$165 million. St. Louis will get \$48.5 million with an additional \$5-10 million possible (which would allow SLAPS to be completed).

Staffing: Jacqui has two months detail downtown. Sharon will be on detail for three months starting in April.



US Army
Corps of Engineers
St. Louis District



FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting Corps Update

10 December 04



December 2004

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **North County ROD**
- **Community Interactions**
- **Taskers**
- **Questions**

December 2004

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

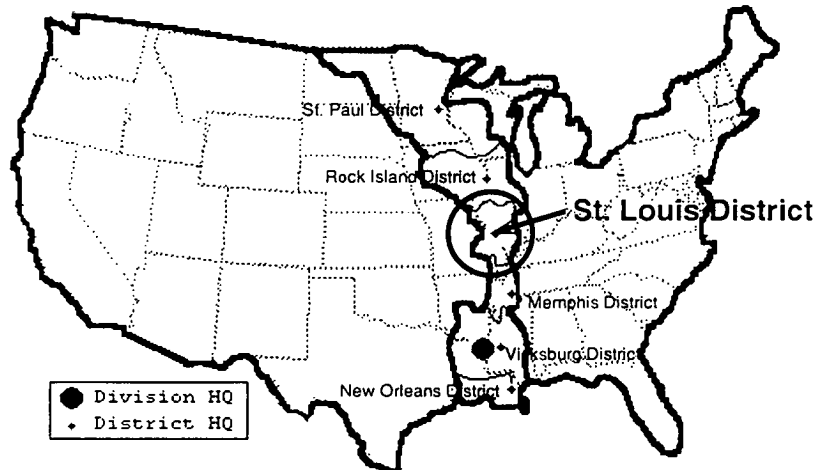

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- Remedial Design – Upcoming Work Descriptions for Reg. Review
 - MI Plant 6W Phase II RAWD: Spring 05.
 - Gunther Salt RAWD: Spring 05
- Remedial Action
 - MI Plant 6W South of Bldg 101: Final Inspection held, punchlist work remains. 3,300 cy excavated (Approx. 200 cy reused).
 - DT-10 (Thomas & Proetz): 5 of 8 small areas remediated.
 - DT-29 (Midtown Garage): COMPLETE; 155 cy.
 - Post Remedial Action Reports (PRARs): 4 in progress: Plant 7E, City of Venice (McKinley Bridge), DT 6/7 (Heintz Steel / Midwest Waste) and Plant 10.
 - Rail Shipments: 656 cy shipped. (3,500 cy planned for FY05).

December 2004

4



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Site Work – Impacted due to wet weather / conditions.**
 - **Phase 4/5:** Limited excavation/confirmation/backfill remains and will resume – pending conditions.
 - **Phase 6:** Sheetpile wall construction start – e/o Dec '04.
 - **Water Storage / Water Treatment:** ~600,000 gal. on site for discharge
 - **Rail Shipments off SLAPS in FY05**
 - 13,400 cy shipped this FY/ 80,000 cy planned FY05 = 17%

December 2004

5



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - **Group 1 VPs (2L, 3L, 4L, 5L) Pre-Design Investigation (PDI) – Draft work plan .**
 - **VPs 1L, 8C and 40a Parcel – preparing Draft Summary Report**
 - **Rail Shipments off HISS – No shipments planned for FY05**
- **SLAPS VP's**
 - **Assessment of the 30 DoE remediated properties. Complete; issue after ROD.**
 - **Characterizations – On-going.**
 - **Designs are on hold in FY04**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Rail Shipments from VP's – No shipments planned for FY05**

December 2004

6




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

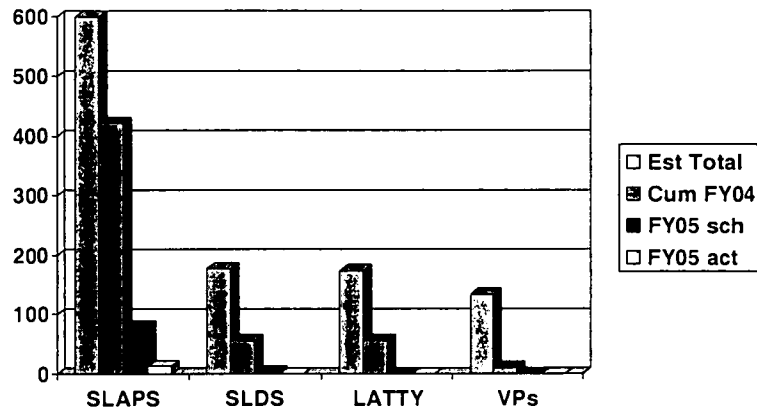

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles

December 2004

7



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

-
- **New Transportation Regulations**
 - Request made for DOT exemption, to transport material via gondola cars, as currently done.
 - Still awaiting response
- **Long Term Stewardship** - Next Meeting in January (tentative)
- **North County Haul Road Study** -Regulator review complete. Working response to comments.
- **FFA Amendment** - Response to MDNR request issued 30 Sep.
- **DoE Program POC (Jeff Short)** - No interactions during this timeframe.

December 2004

8



US Army
Corps of Engineers
St. Louis District

North County ROD Status



Gateway to Excellence

- **Current Status / Recent Events**
 - Draft Final issued to EPA and MDNR on 13 Sep.
 - Comments received 1 Nov.
 - Working responses to comments.

December 2004

9



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Derivation of Site Specific DCGLs for N. County Structures (DCGL doc) and memorandum explaining rationale.
 - Final issued 29 Oct 04.
- **Upcoming Events**
 - Newsletter working

December 2004

10



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - USACE summary briefing on the North County ROD – TBD.
 - USACE to schedule a time w/DOE Office of Legacy Management to brief Oversight Committee on Long-Term Stewardship – TBD.
- **New Taskers**

December 2004

11



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

December 2004

12

FUSRAP Document Management System

Year ID

00 4509

Further Info?



Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis FUSRAP Oversight Committee Agenda and other materials from December 10, 2004 meeting

Author/Originator

R. C. Cavanagh

Company

Oversight Committee

Date

12/10/2004

Recipient(s)

Company (-ies)

FUSRAP

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?



Comments

Include in which AR(s)?

☒ North County

☐ Madison

☐ Downtown

☐ Iowa

ETL

810

SAIC number

Filed In Volume

8

Bechtel ID

