

ST LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 430 Adams St.

St. Louis, MO 63135

314-313-2959

rcavanagh@ltcop-stl.org

MEMORANDUM

TO: Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, September 10, 2004 at 11:30 am in the trailers on Latty Ave.

Committee members who cannot attend should contact the chairperson at the above numbers to be excused.

Thank you.

:RRC

ST LOUIS FUSRAP OVERSIGHT COMMITTEE

*c/o 430 Adams
St. Louis, MO 63135
314-313-2959
rcavanagh@ltcop-stl.org*

Summary of Meeting
August 13, 2004

Committee Members Present: Tom Binz, Ric Cavanagh, Jim Grant, Michelle Morgenstern, Tom Manning

Committee Members Excused: Bill Brandes

Other Interested Parties: Larry Erickson, Ron Rauh, Gerald Allen, Sharon Cotner, Jacqueline Mattingly, Michael Zlatic, Eric Gilstrap

The following comments are in addition to the handouts provided by USACE at the meeting.

Page 5 – Coldwater Creek should be done by 8/20. Crews are working two, ten hour shifts daily, seven days/week. Some soil and debris in creek are questionable. They are being evaluated prior to disposal.

Page 7 – VP 13 which is just adjacent to SLAPS has been seeded and completed.

Page 9 – There is a question as to whether the new DOT regulations apply to that which is enroute or only to newly dug soil. The problem with intermodals is that they are harder work with and harder to get. The current condolas are on a long term lease.


Additional comments:

1. A representative from Senator Talent's office will tour the sites August 11.
2. The Assistant Secretary of the Army for Civil Works will tour the sites on September 1.
3. No additional funds have been received year to date, and it is unlikely that we will get any this fiscal year.
4. It is likely that the federal budget will again be under a CRA (continuing resolution authorization) through March.



US Army
Corps of Engineers
St. Louis District

FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

13 AUG 04




August 2004



US Army
Corps of Engineers
St. Louis District

Progress Report

St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**

- **MI - Plant 7N/S** PDIR out for regulator review. Design in progress. Plant 7W sampling complete. PDIR in progress.
- **South of Anglerodt VPs –**
Thomas & Proetz PDIR finalized. Design in progress
Gunther- Sampling at north property continues. PDIR in progress.
- **West of Broadway VPs –** Sampling complete.

- **Remedial Action**

- **MI Plant 6W South of Bldg 101 –** Excavation ~½ way complete. Area 1 complete. Area 3 working. 2,254 cy excavated. (1,338cy shipped, remainder to be reused for backfill).
- **Post Remedial Action Reports (PRARs) –** 4 in progress, Plant 1, Plant 7E, City of Venice (McKinley Bridge) and DT 6/7 (Heintz Steel / Midwest Waste).
- **Rail Shipments –** 4,934 cy excavated this FY; 4,018 cy shipped. (5,000 cy planned for FY04).

August 2004



US Army
Corps of Engineers
St. Louis District

Progress Report

St. Louis Airport Site (SLAPS)



Gateway to Excellence


- **Remedial Design** – Phase 6 Sheetpile wall design under NS-RR review.
- **Removal Actions**
 - **Phase 2/3** - 85,000+ cy total shipped to date (43,000+ cy this FY).
 - No activities currently.
 - SU-35 utilized for one water storage basin.
 - **Phase 4/5** – ~37,000 cy shipped to date.
 - **Ameren/UE relocation complete.**
 - **Coldwater Creek** – *Initiated 5 Aug; nearing 50% complete.*
 - *SU-43 complete; SU-44 excavation and stone placement in-progress.*
 - **Phase 6** – RR signal line relocation in-progress; complete by e/o AUG.
 - **Water Storage / Water Treatment**
 - Minimum water being retained on site, currently.
 - 1 batch being prepared for discharge.
 - **Rail Shipments off SLAPS this FY**
 - 91,000 cy shipped to date / 85,000 cy planned.



US Army
Corps of Engineers
St. Louis District

Progress Report

St. Louis Airport Site (SLAPS)



Gateway to Excellence



August 2004



US Army
Corps of Engineers
St. Louis District

Progress Report

Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Group 1 VPs (2L, 3L, 4L, 5L) PreDesign Investigation (PDI) – Draft work plan .
 - VPs 1L, 8C and 40a Parcel – preparing Draft Summary Report
 - Rail Shipments off HISS – No shipments planned for FY04

- **SLAPS VP's**
 - Assessment of the 30 DoE remediated properties. Complete; issue after ROD.
 - Characterizations – On-going.
 - Designs are on hold in FY04
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - Utility Support – 19 this FY in N. Cty; mostly along haul road ROW.
 - VP-13 – Completed; 1,250 cy estimated excavation volume.
 - Rail Shipments from VP's – No shipments planned for FY04, however...
 - ~1,800 cy shipped from VPs – 10, 13 and 4C/5C.




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

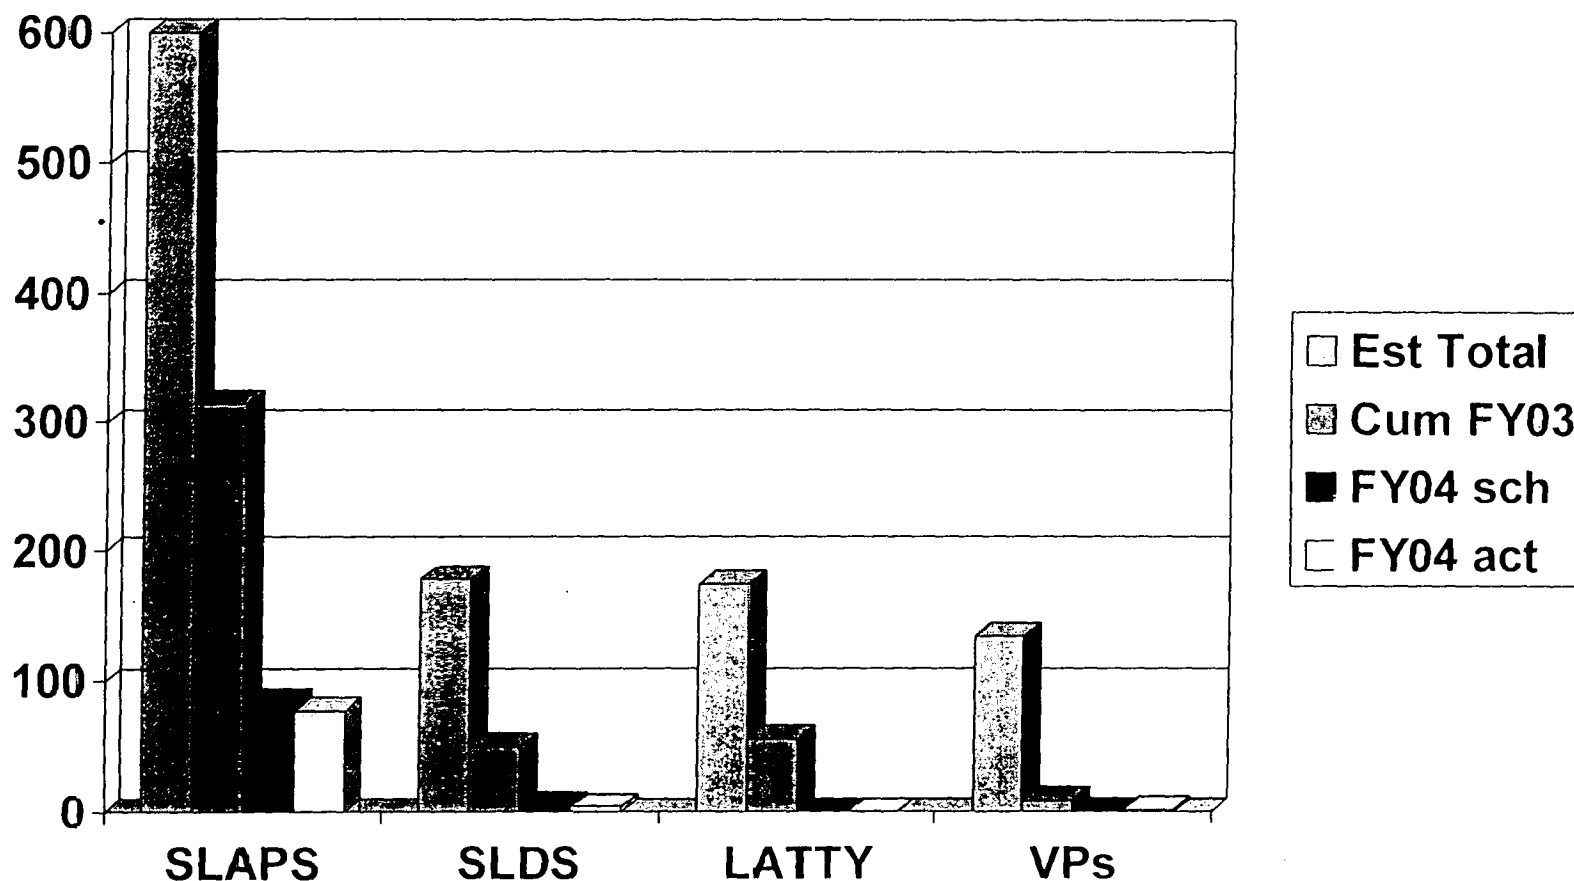

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 2. SLDS volumes do not include Inaccessibles


August 2004



US Army
Corps of Engineers
St. Louis District

Progress Report

Other Issues




Gateway to Excellence

- **New Transportation Regulations**
 - Request made for DOT exemption, to transport material via gondola cars, as currently done.
- **Long Term Stewardship -**
 - Next Meeting 13 AUG.
- **North County Haul Road Study** – Draft for Regulator review pending.
- **DoE Program POC (Jeff Short)** – No interactions during this timeframe.
- **CERCLA 5 year Review** – for all St. Louis FUSRAP Sites
 - Public review copy issued – 29 Jun.
 - Finalization of document pending.



US Army
Corps of Engineers
St. Louis District

North County ROD Status



Gateway to Excellence

- **Current Status / Recent Events**
 - MVS revised responses and draft ROD (per 22-23 June discussion with EPA and MDNR) and issued to CX, MVD and HQ for concurrence.
 - Minor comments received. Document being revised for issuance.



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**

- **Five-Year Review** public review period closed – Jun 28.
- **Derivation of Site Specific DCGLs for N. County Structures** (DCGL doc) and memorandum explaining rationale.
 - Public notice published in Post Dispatch – 7 July. Letters issued to mailing list.
 - Request for extension received. Review period extended to 18 Aug.
 - Document available electronically via website, or paper copies w/ Admin Records.

- **Upcoming Events**

- Newsletter working



US Army
Corps of Engineers
St. Louis District

Taskers




Gateway to Excellence

- **Old Taskers**
 - USACE to provide a summary briefing on the North County ROD – TBD.
 - USACE to schedule a time w/DOE Office of Legacy Management to brief Oversight Committee on Long-Term Stewardship – TBD.
- **New Taskers**



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

FUSRAP Document Management System

Year ID
00 4729

Further Info?
☐

Operating Unit
North County

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Meeting Minutes/Transcripts

Subject or Title

St. Louis FUSRAP Oversight Committee Meeting Minutes dated 13 Aug 2004. Next meeting scheduled 10 Sep 2004.

Author/Originator

Company
Oversight Committee

Date
8/13/2004

Recipient (s)

Company (-ies)

Version
Final

Original's Location
Central Files

Document Format
paper

Confidential File?
☐

Comments

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

SAIC number

Bechtel ID

ETL

114

Filed in Volume

