


ST. LOUIS FUSRAP OVERSIGHT COMMITTEE
c/o 111 So. Meramec
Clayton, Missouri 63105
314.615.1635

MEMORANDUM

TO: FUSRAP Oversight Committee
Other Interested Parties

FROM: Richard R. Cavanagh 
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held this Friday, September 8, 2000. The meeting will begin at 11:30 am at the new location of the trailers (8945 Latty Ave.).

Since this meeting has snuck up on the Chairperson (blame the Labor Day Holiday), summaries of the August 11 meeting will be distributed at the meeting. My apologies.

Members of the Committee who are unable to attend should contact the Chairperson at the above phone number to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, Missouri 63105

314.615.1635

Ric.Cavanagh@Stlouisco.com

Summary of August 11, 2000 Meeting

Members Present: Ric Cavanagh, Sally Price, Tom Manning, Tom Binz, Jon Langerak, Jack Fraenhoffer, Jan Titus

Other Interested Parties: Tom Horgan, Dave Wagoner, Jacque Mattingly, Sharon Cotner, Larry Erickson, Eric Gilstrap, Steve Welling

The following comments are in addition to the handouts provided by USACE (see attached).

Page 4 – The water is both treated and untreated. Selenium was totally unexpected. This could severely challenge the water treatment budget. This is a high priority issue. Some of the Selenium may be in the ground water table. On the whole, there have been a few more hot spots than expected (but actually less contamination than expected).

Page 5 – Trailers are off site, utilities capped.

Page 6 – 57/58 are the Allied Systems Property. PRAR = Post Remedial Action Report. 36 is the open area at Latty and Frost.

Page 8 – FS/PP – 30 days for regulators review, then thirty days thereafter. Public review is likely in late November, early December. (DOE at Grand Junction has also been sent a copy).

Jack Fraenhoffer et al. commented on DOE's Long Term Stewardship Conference. Key ideas: don't take long term stewardship for granted ; don't underestimate costs. The best route is to "clean up to clean standards" so that there is no long term stewardship required.

Tom Horgan from Rep. Talent's office commented that the House has supported \$140 million for FUSRAP (same amount as requested by the President) which reflects no cut in the budget. In the Senate, appropriations are tied up in a non-partisan squabble over fish and water issues. It might result in a continuing resolution (but shouldn't effect the work in St. Louis). He also commented that General Flowers from Ft. Leonard Wood would likely be the new head of the Corps of Engineers.

Page 9 – the new numbers will be effective 8/14

Dave Wagoner commented on a regulatory issue: high concentrations of contamination in the fill might cause a problem. Envirocare can't open a new cell until the old one is capped off. To do so will require more low level fill to top off cells.

Larry Erickson of MDNR commented that DOE Grand Junction will be visiting soon at Weldon Springs (next three to four months).



US Army
Corps of Engineers
St. Louis District



FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

11 AUG 00



August 2000

1

Notes



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

August 2000

2

Notes




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

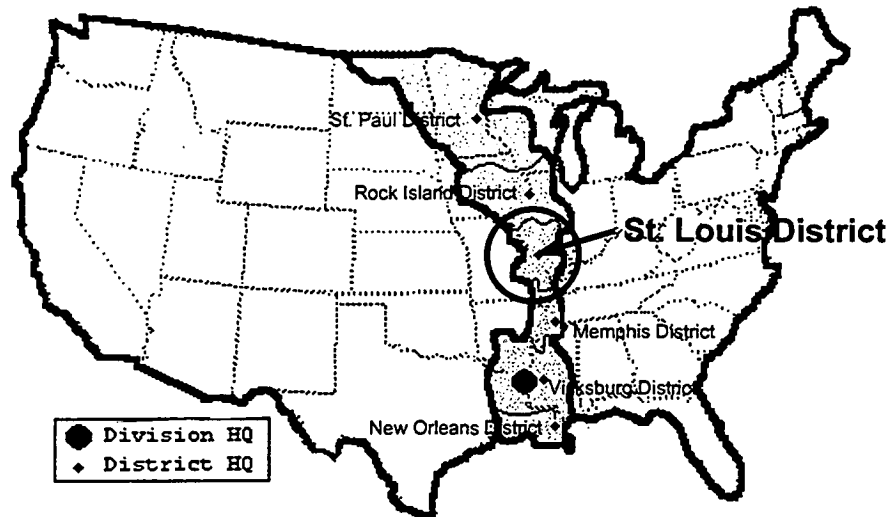

3

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - East End Work Area Pre Design Investigation continues in area adjacent to McDonnell Blvd.
 - REV 0 by mid AUG
- **Remedial Action at Radium Pits - 93% excavated**
 - Progress continues. 31,000 cyds excavated and disposed of to date
 - 36,000 cyds of material are expected to be removed.
 - Gross excavation completed
 - Precision excavation is ongoing
 - Water is still being stored on site which impacts our ability to clear the western survey units of the Radium Pits
 - Status of treatment of selenium in water - options being evaluated
 - Sprinkler system and dust control being utilized
 - **Rail Shipments off SLAPS**
 - 500 gondola railcars & 89 intermodals shipped to date in FY 00 (36,966 cyds)

August 2000

4

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Supplementary Pile Contract (5,750 cyds)**
 - The proposal was received from the contractor on 17 JUL, negotiations were completed 27 JUL.
 - Contract Award is the next step
 - Removal of the Supplemental Pile is expected to start by the end of AUG and be completed early in FY01.
 - Soils will be sent to Envirosafe.
- **Main Pile**
 - Plans and Spec's are being developed
 - An Acquisition Strategy Meeting was held to select the type of contract to be utilized
 - Two small business contracts will be used, each for 1/2 of the pile
 - Plans and Specifications for the N half are expected to be complete by 15 OCT.

August 2000

5

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Characterization Surveys**
 - Completed walkovers at VP 57/58 as well as Class 2 and 3 and characterization samples.
- **Remedial Design**
 - Bounding and Data Gap samples are analyzed for VP's 9/10/11/12.
 - The design is currently on hold
- **Remedial Action**
 - A PRAR is now being prepared for the VP38 removal action.
- **VP 36**
 - First Industrial building a new warehouse. Samples taken. ARCO Construction Company cleared to proceed.

August 2000

6

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Design**
 - **Plant 6E/ 6E1/2 Remedial Design status**
 - Rev 0 finalized and sent to the regulators
 - **Pre Design Investigation sampling is complete for SLDS VP's**
 - Gunther Salt, PVO Foods, MSD Lift Station, the shadow of the McKinley Bridge area and BFI.
 - The McKinley Iron work description is currently being developed
 - **Plant 6W Design status - 30% complete**
- **Remedial Action**
 - **Plant 2 is complete. PRAR is due 30 SEP.**
 - **Plant 1 is ongoing (@1,500 cyds)**
 - Excavation has begun.
- **4,750 cyds shipped this FY (58 railcars) / 8,500 scheduled**
- **MVS working Utility Agreement at SLDS**
 - Maps provided to utility companies

August 2000

7

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - Received additional HTRW-CX comments on 25 JUL, provided response to comments on 26 JUL
 - Also received comments from HQUSACE Real Estate and Office of Counsel
 - Draft FS/PP to regulators on 8 AUG
 - Signed ROD date is 29 AUG 01
- **DoE Program POC's interactions**
 - Attended Long Term Stewardship Workshop from 7-10 August
 - Mallinckrodt, MDNR and USEPA also attended.
- **Boxer / Buttonwillow Congressional Hearing**
 - Conducted on 25 JUL with USACE, NRC, EPA amongst others
- **Annual Cooperative Agreement Meeting with MDNR was held 17 JUN**
 - Corps reviewing budget.
- **Site trailer move completed**

August 2000

8 .

Notes



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**

- Summer newsletter will be published in AUG
- Presentation given to St. Louis County Health Department

- **Upcoming Events**

- Society of American Military Engineers (SAME) St. Louis Post Conference presentation - SEP
- SAME National Conference Presentation - OCT

- **New Contact Numbers for 8945 Latty Avenue**

- FUSRAP Main line (314) 524-3905
- FUSRAP Fax (314) 260-3941
- Sharon Cotner, Program Manager (314) 260-3915
- Lou Dell'Orco, Project Manager (314) 260-3932
- Jacque Mattingly, Management Asst. (314) 260-3919

August 2000

9

Notes



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Provide a copy of the Supplemental Pile Plans and Specifications to the MDNR (Complete)
 - Note: www.eh.doe.gov/workers/ is a website for information about the former MED/AEC workers
- **New Taskers**

August 2000

10

Notes



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?
Questions? Questions?

August 2000

11

Notes

Cataloging Form

{Technical/Project Managers fill in C through G, K through Q. RM completes other fields}

A. Document ID Number: Assigned by database 00-288

B. Further Information Required?: ☐

C. Operable Unit (Choose One):

USACE ☐
St. Louis Sites ☐
Downtown ☐
North County ☐
Madison Sites ☐
Inaccessible Areas ☐
PRP ☐
Oversight Committee ☒

D. Site (Optional):

SLDS VPs ☐
Mallinckrodt ☐
SLAPS ☐
SLAPS VPs ☐
CWC ☐
HISS ☐
Madison ☐

E. Area (Optional): _____

F. Primary Document Type (Choose One):

Site Management Records ☐
Removal Response ☐
Remedial Investigation ☐
Feasibility Study ☐
Record of Decision ☐
Remedial Design ☐

Remedial Action ☐
Public Affairs/Community Relations ☒
Congressional Relations ☐
Freedom of Information Act ☐
Real Estate ☐
Project Management ☐

G. Secondary Document Type (see back of form): Public Meetings Minutes Correspondence

H. Bechtel Number: _____

I. SAIC Number: _____

J. MARKS Number(Choose One): FN: 1110-1-8100e ☐ FN: 1110-1-8100f ☐ FN: 1110-1-8100g ☒

K. Subject/Title: Oversight Committee Meetings

L. Author: Richard Cavanagh M. Author's Company: Chaperson

N. Recipient(s): Committee Members O. Recipient(s) Company: _____

P. Version (Choose One): Draft ☐ Final ☒ Q. Date: 8-11-00

R. Include in the ARF? ☒ S. Include in the ARF? ☒ T. Filed as Confidential/Privileged? ☐

U. Document Format (Choose one):

Paper ☒ Photographic ☐ Cartographic/Oversize ☐
Electronic ☐ Audio-visual ☐ Microform ☐

V. Filed in AR Volume Number: _____

W. Physical Location (Choose One):

Central Files ☒ Microfilm Vendor ☐ In ARF ☐
Records Holding Area ☐ Department of Energy ☐ In AR ☐

X. Associated with Document(s): _____
