

Mattingly, Jacqueline MVS

From: Richard Cavanagh [rcavanagh@ltcop-stl.org]

Sent: Friday, February 07, 2003 10:24 AM

To: Mattingly, Jacqueline MVS


Subject: Meeting Announcement

Attached are the meeting announcement and minutes of the January meeting of the Oversight Committee. Please send out to members, et al.

Thanks.

Ric Cavanagh
Executive Director
LTCOP
314-918-8222

2/7/2003



**U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134**

FROM: Jacque Mattingly

Phone: 314-260-3924

Fax: 314-260-3941

TO:

John Langerak, 524-0243

Anna Ginsburg, 613-3120

Date: February 7, 2003

No. Pages Including Cover Sheet: 4/

REMARKS:

For your information –

A copy of the St. Louis Oversight Committee meeting minutes follows. The next meeting is scheduled for Friday, February 14, 2003 at the FUSRAP Project Office.

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE
c/o 17125 Old Jamestown Rd.
Florissant, MO 63034-1416
314.313.2959
rcavanagh@ltcop-stl.org

MEMORANDUM

TO: Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh
Chairperson

RE: Next Meeting and Update

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, February 14, 2003, 11:30 am, at the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Important Budget Considerations!

The Committee needs to discuss proposed FY 2004 budget recommendations for the St. Louis sites. As currently proposed, St. Louis could see a reduction of over \$2 million dollars in FY 2004 (compared to previous years), despite the overall national FUSRAP budget still being pegged at the same \$140 million. It would seem that St. Louis is being "rewarded" for all of its good work by having its budget reduced! No logic here!

I have taken the liberty of contacting the County Executive's office as well as sending letters to the St. Louis area Congressional delegation offices in Washington, D.C. I also have gotten permission to utilize the County's lobbyist, Laura Madden, to help us in this effort. Hopefully, we can get changes in the Corps of Engineers budget that will allow St. Louis project staff to continue to do the good work that has won them awards in the past.

I will share more details at our meeting.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 17125 Old Jamestown Rd.

Florissant, MO 63034-1416

314.313.2959

rcavanagh@ltcop-stl.org

Summary of Meeting

January 10, 2003

Committee Members Present: Ric Cavanagh, Jim Grant, Bill Brandes, Sally Price, Tom Binz, Jan Titus,

Other Interested Parties: Col. Kevin Williams, Jacqui Mattingly, Lou Dell'Orco, Angela Minor, Michael Zlatic, Eric Gilstrap, Larry Erickson, Jim Mitas

The following comments are in addition to the handouts provided by the USACE project staff at the meeting.

The Committee welcomed Col. Kevin Williams to its meeting and thanked him for his support.

Page 4 – 34,684 cyds have been removed (not 71). Phase 1 should be done by the end of January. Se issues: Larry Erickson briefed the committee on MDNR review status and issues. Three issues are being reviewed. 1) the status of Coldwater Creek as a metro “no-discharge” creek 2) the effluent rate (more data needed) 3) questions about the Se values submitted (ie. values were based on Western states, these values may be lower in Missouri). In answer to the question as to whether concern is about discharges only in emergency situations or on a daily basis, Larry stressed that this really pertains to post rainstorm situations only.

Page 5 – not much is planned for HISS due to funding limitations

Page 6 – A meeting is scheduled for next week with Thomas and Proetz regarding disruption of owner's business. Remedial Action – rail line will be done last (backing out of the property via the rail line).

Page 7 – The Division is to get the draft ROD in two weeks. March is still the target date for release and public comment. Some recent decisions in New York regarding clean up standards may be in our favor. CRA – we may get an additional \$5.7 million for this quarter. Sharon Cotner announced that Brig. General Donald Riley is the new Division Chief.

Page 9 – A newsletter is due out in February.

Next Meeting

Friday, February 14, 2003, 11:30 am



US Army
Corps of Engineers
St. Louis District



FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting ***Corps Update***

10 JANUARY 02



January 2003

1

Notes



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

January 2003

2

Notes




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

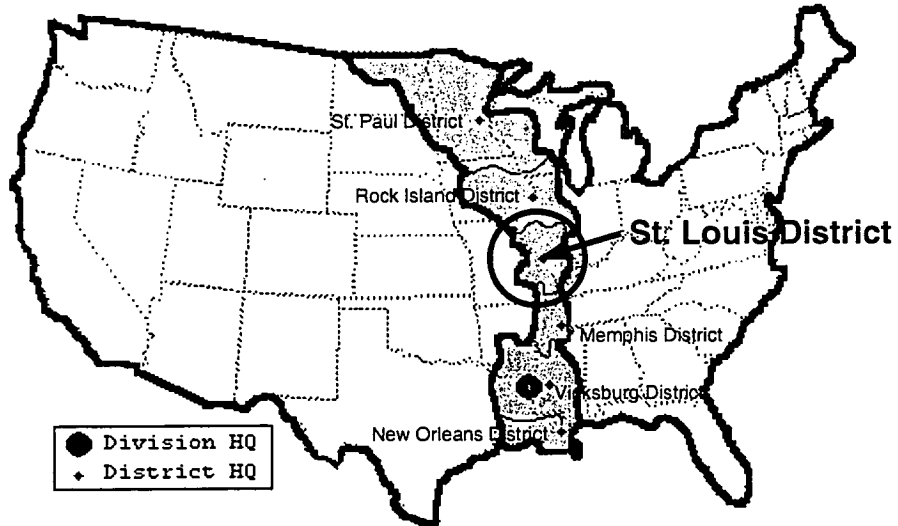

3

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - **Work Descriptions for Phases 4 / 5 and Phase 6** - Next step is regulator review for Phase 4/5 (after North County ROD). The USACE 90% review for Phase 6 has been completed. Coordination with the railroad for support during Phase 6 is ongoing and will be incorporated into the document. Regulator review is the next step.
- **Removal Actions**
 - **Began Phase I (IA5) excavation 10 DEC 01** - 75,000 cyds expected
 - 71,000 cyds removed to date. Phase 1 removal continues - 1 Survey Unit remains.
 - 4 of the 5 Survey Units have been cleared / backfilled to date.
 - Survey Units 15 and 16, adjacent to McDonnell Blvd., are next.
 - **Status of Corps Proposal for Selenium (Se) discharge limits**
 - Resubmitted the USACE proposed discharge limit for Se to the MDNR for further consideration.
 - Met with the MDNR on 29 August, awaiting response
 - **Rail Shipments off SLAPS**
 - 30,000 cyds shipped to date / 75,000 planned.

January 2003

4

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Requesting removal of NPDES permit at HISS.
 - Letter sent to MDNR, no response to date. MDNR is looking at our request (29 August meeting).
 - GIFREHC Roof Replacement complete
 - MVS support of the GIFREHC roofing contractor was completed 19 DEC.
 - Rail Shipments off HISS
 - 450 cyds shipped to date / 500 cyds planned
- **SLAPS VP's**
 - Data Evaluation
 - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
 - Designs are on hold and expected to be completed in FY03
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - Support to the City of Florissant completed
 - Area is adjacent to Coldwater Creek where it intersects Paddock Creek
 - 3 samples were taken and a partial walkover conducted on the property. No results were detected above background and the area was cleared for the City development.
 - Rail Shipments from VP's
 - 0 planned in FY03

January 2003

5

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Investigation** - USACE completed internal draft for the Groundwater Remedial Action Alternatives Assessment due to high levels of U in a well at Plant 6W - It is currently under internal review.
- **Remedial Design**
 - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Heintz Steel, Gunther Salt, Christiana Ct, Star Bedding, Collins, and Cotto Waxo are currently on hold
 - **Plant 7E** - Currently in the process of conducting an area walkover.
 - **Work Descriptions - REV 1's may be issued after PDI re-evaluation.**
 - Thomas and Proetz deep soils evaluation results and City of Venice results are pending USACE internal review.
 - PSC Metals PDI is ongoing.
- **Remedial Action**
 - **Plant 1 - 3,724 cyds remediated**
 - Post Remedial Action Report - internal review draft is due in FEB.
 - **Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 22,298 cyds remediated to date**
 - Continuing excavation in the final phase, Phase 3. Completion date is MAR 03.
 - **VP's - Midwest Waste (4,800 cyds) - 4,775 cyds removed to date, Final status survey and spot excavation is ongoing in the remaining Survey Unit. 5 of 6 Survey Units cleared for backfill to date.**
 - **Rail Shipments off SLDS**
 - 1,334 cyds shipped / 13,000 planned.

January 2003

6

Notes



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - One remaining major issue exists with the CX OC comments - MVS continues to work on finalizing our position paper
 - CX issue resolution and public review are the next steps.
- **Long Term Stewardship -**
 - DOE LTS Meeting for Weldon Spring will be held on 30 JAN.
- **Bi-Annual Utility Support Meeting was held today.**
- **DoE Program POC's interactions -**
 - None at this time
- **New MDNR Cooperative Agreement**
 - Working new agreement with the MDNR
- **Funding**
 - Energy and Water Appropriation has not been signed by the President. FUSRAP is currently operating under a Continuing Resolution Authority (CRA)
 - Current CRA is in effect until 11 JAN, next is 12 - 31 JAN, then 1-28 FEB
- **Reprogramming Issue Status**
 - No change to date. Current language limits transfers between projects to \$1 million without Congressional approval. Old language stated 15% of site authorization could be transferred without approval.

January 2003

7

Notes




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

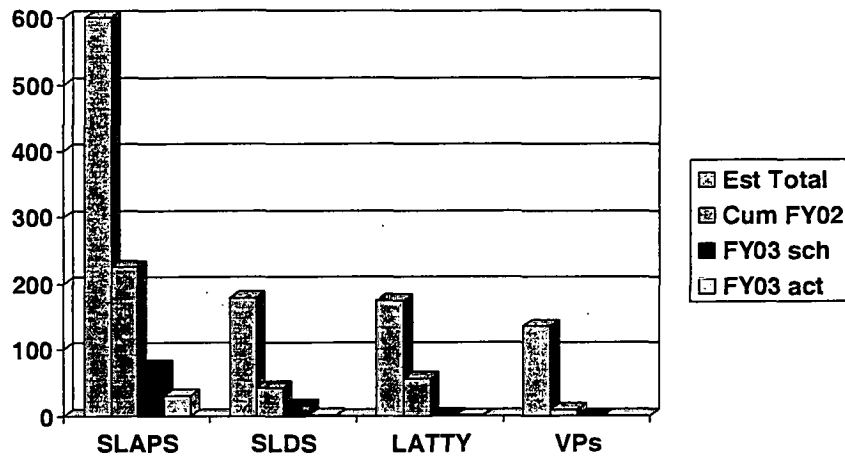

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal
Note 2. SLDS volumes do not include inaccessible

January 2003

8

Notes



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - None
- **Upcoming Events**
 - FUSRAP has been requested to speak to Ameren UE employees on 23 JAN

January 2003

9

Notes



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)
- **New Taskers**

January 2003

10

Notes



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? **Questions?** **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**

January 2003

11

Notes

FUSRAP Document Management System

Year ID
00 3663

Further Info?
☐

Operating Unit
St. Louis Sites

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Public Meeting Minutes/Transcripts

Subject or Title

E-mail of Meeting minutes from 10-Jan-03 and schedule for next meeting.

Author/Originator
Richard Cavanagh

Company
LTCOP

Date
2/7/2003

Recipient(s)
Jacqueline Mattingly

Company (-ies)
FUSRAP

Version
Final

Original's Location
Central Files

Document Format
paper

Confidential File?
☐

Comments

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL
8.10

SAIC number

Filed in Volume
8

Bechtel ID

