

**Mattingly, Jacqueline MVS**

---

**From:** Richard Cavanagh [RCavanagh@ltcop-stl.org]

Friday, June 04, 2004 5:07 PM

**To:** Mattingly, Jacqueline MVS

**Subject:** May Meeting Minutes

Attached are the May minutes and the memorandum announcing the next meeting. Please distribute.

Thanks.

Richard Cavanagh  
Executive Director  
LTC Ombudsman Program  
314-918-8222

6/15/2004

ST. Louis FUSRAP Oversight Committee  
c/o 17125 Old Jamestown Rd.  
Florissant, MO 63034  
314-313-2959  
[rcavanagh@ltcop-stl.org](mailto:rcavanagh@ltcop-stl.org)

**MEMORANDUM**

TO: FUSRAP Oversight Committee Members  
Other Interested Parties

FROM: Richard R. Cavanagh  
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, June 11, 2004, 11:30 am, at the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

*St. Louis FUSRAP Oversight Committee*  
*c/o 17125 Old Jamestown Rd.*  
*Florissant, MO 63034*  
*314-313-2959*  
[rcavanagh@ltcop-stl.org](mailto:rcavanagh@ltcop-stl.org)

Summary of Meeting  
May 14, 2004

Committee Members Present: Jack Frauenhoffer, Michelle Morgenstern, Jan Titus, Sally Price, Ric Cavanagh, Jim Grant, Tom Manning

Committee Members Excused: Tom Binz

Other Interested Parties: Bob Marchant, Larry Erickson, Eric Gilstrap, Sharon Cotner

The following comments are in addition to the handouts provided by the USACE staff at the meeting.

Page 4 – The bike path was completed in April

Page 5 – Meeting today with Stone Container re: some property changes. Sharon commented that there is a need to get some projects under way so that funds are not cut (cuts may be made on projects “planned but not implemented.”)

Page 6 – CSC=Coldwater Creek. Water treatment is working very well. Some funds have been moved from other sites to keep this project going. Staff have requested \$1-4 million more for this year.

Page 8 – DOT proposals would require more expensive packaging and/or intermodels. Therefore, staff are requesting exemption (since our materials aren’t heavily contaminated).


Page 9 – Many comments received from state and EPA. Still targeting a ROD in this fiscal year.

Next Meeting  
Friday, June 11, 2004



US Army  
Corps of Engineers  
St. Louis District




# ***FUSRAP***



Gateway to Excellence

## **St. Louis Oversight Committee Meeting *Corps Update***

14 May 04

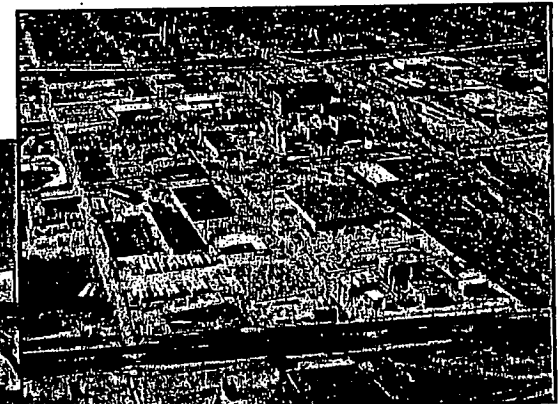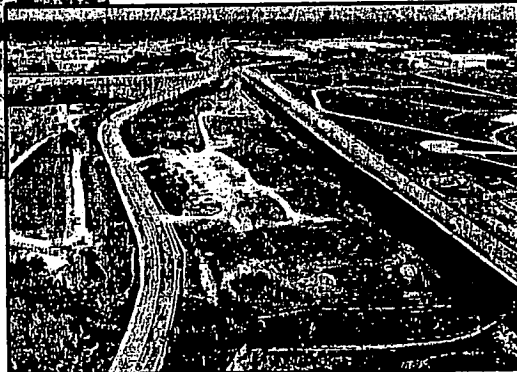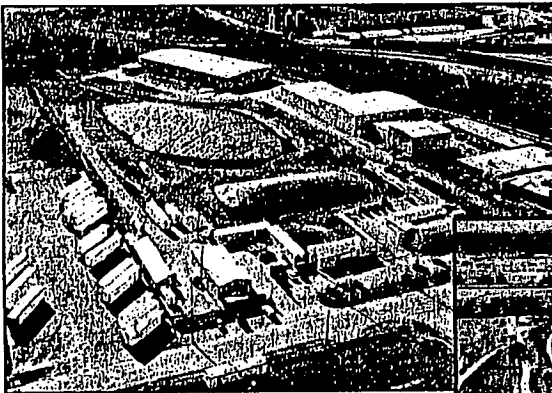


May 2004




US Army  
Corps of Engineers  
St. Louis District

# Agenda




Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **North County ROD**
- **Community Interactions**
- **Taskers**
- **Questions**




US Army  
Corps of Engineers  
St. Louis District

# Mississippi Valley Division



Gateway to Excellence

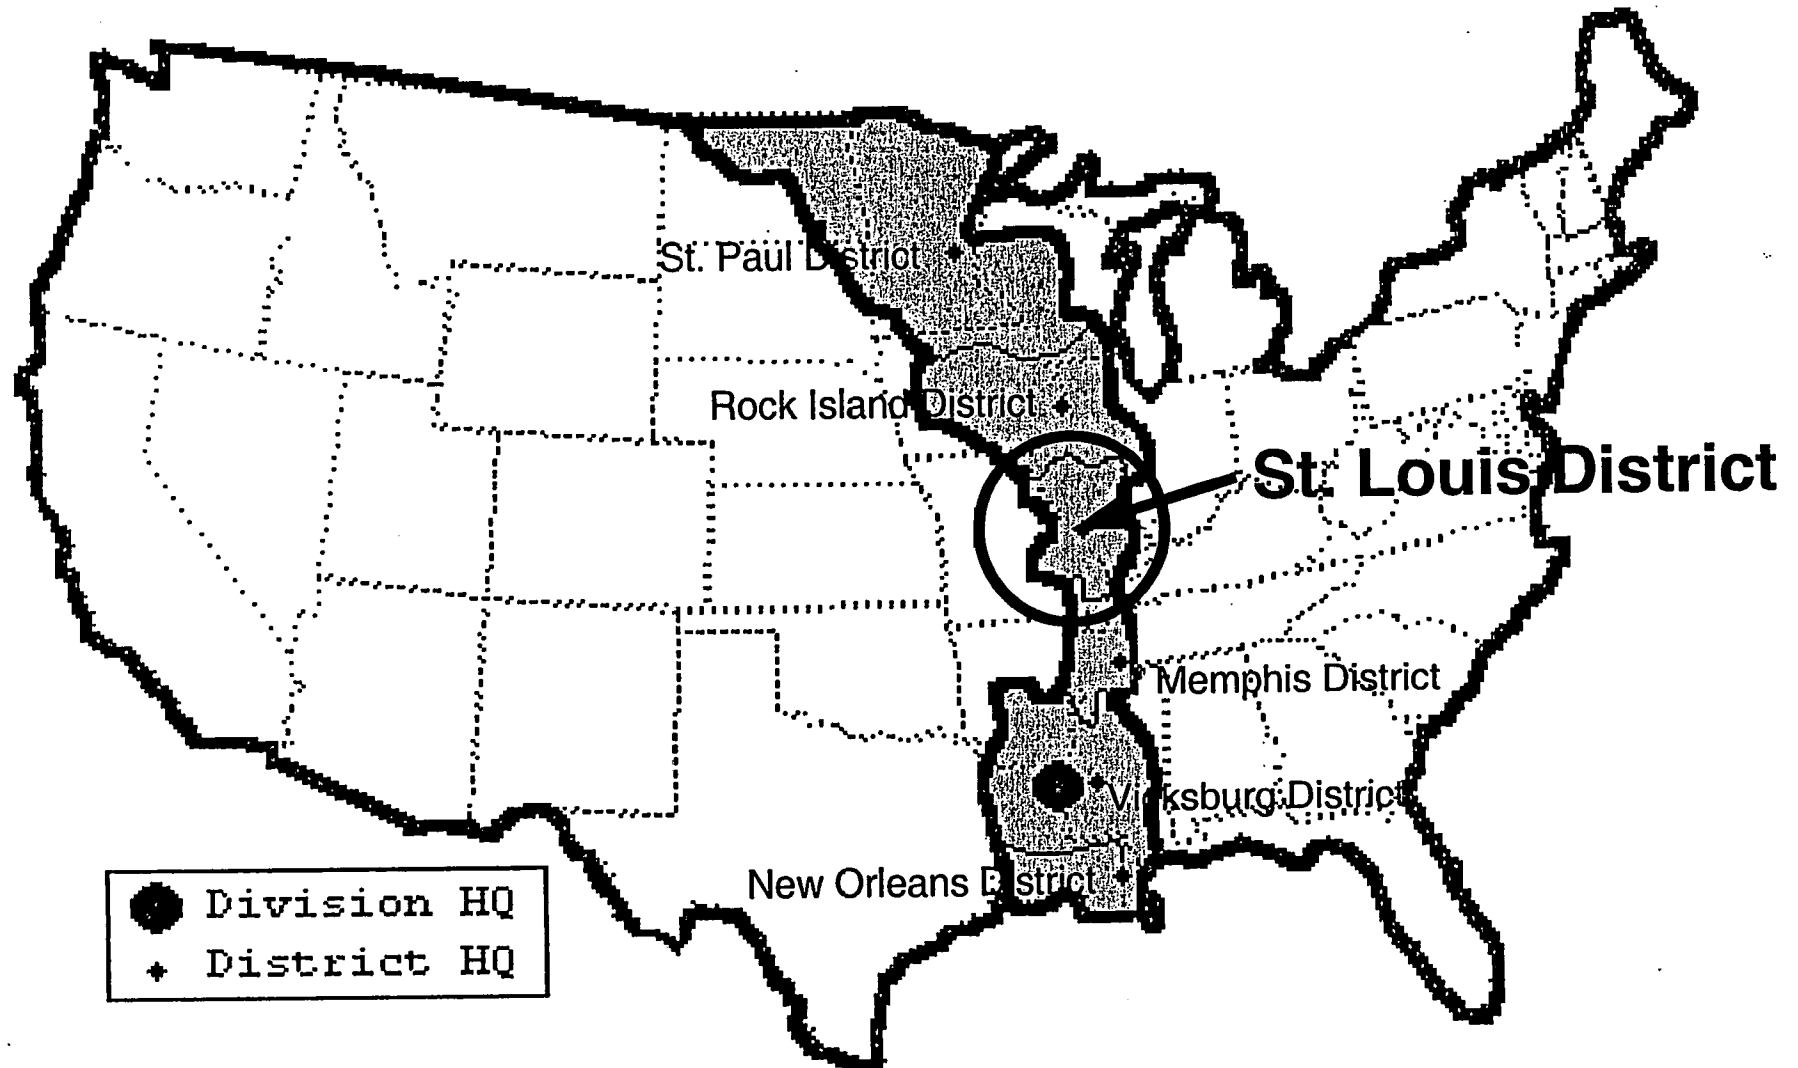




US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## St. Louis Downtown Site (SLDS)



Gateway to Excellence


### Remedial Design

- **MI - Plant 6W** Pre-design Investigation Report (PDIR) for South Bldg 101 – being finalized. Design out for regulator review. Letter of accessibility from MI received. Additional PDI sampling west Bldg 101 complete. Plant 7N/S PDIR regulator review pending. Plant 7W sampling plan under development.
- **South Angelrodt VPs** - PDIR for Thomas & Proetz under review. PDI sampling on Gunther South complete. Sampling scheduled to begin on Gunther North. Historical assessments pending for Cotto Waxo, Starr Bedding, Christiana Court
- **West Broadway VPs**- Sampling complete except for one property.

### Remedial Action

- **MI Plant 1** (3,724 cyds remediated) - PRAR out for regulator review. **Plant 7E** completed SEP 03 (1,319 cy remediated) - PRAR pending for internal review. **Plant 6E/EH** (22,958 cyds remediated) PRAR being developed.
- **Midwest Waste/Heintz Steel (DT-6/-7)** completed SEP 01 & SEP 03, respectively. PRAR being developed. **McKinley Bridge (DT-11)** completed Jan 04. Final restoration of asphalt bike path completed in April. RAS for internal review is pending.


**Rail Shipments off SLDS** - 2,680 cyds shipped / 5,000 planned



US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

### HISS / Latty Avenue

- **PDIs** under development for VPs 1L, 8C & 40a Parcel as well as 2L, 3L, 4L & 5L
- **Rail Shipments off HISS** - 0 cyds planned in FY04

### SLAPS VP's

- **Data Evaluation** - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
- **Characterization** - ongoing for VP's
- **Designs are on hold and expected to be completed in FY04-** 56/57/58/59/1C & Pershall & I-270 ROW + 8/9/10/11/12 & Ballfield hotspots
- **MSD support in FY04** - Sewer line project along Eva and Frost next FY
- **Property Owner Support** – Support for VP 4C / 5C provided in MAR. 90 cy removed in support of the property owner's development plans.
- **Rail Shipments from VP's** - 0 cyds planned in FY04, 135 cyds shipped to date






US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## St. Louis Airport Site (SLAPS)




Gateway to Excellence

- **Designs – Complete for SLAPS**
- **Removal Actions**
  - **Phase 2/3 excavation** – Continues. 75,000 cyds expected
    - Approximately 83,500 cyds have been shipped to date
    - This Phase consists of 10 Survey Units – 6 complete to date. Backfilled SUs 33 & 34B. Currently working next to McDonnell Boulevard.
  - **Phase 4/5 (CWC removal action/restoration)**
    - Approximately 8,000 cyds have been excavated to date.
    - CWC removal action/restoration on hold until August. AmerenUE working GKN power supply relocation. Target completion still end of June.
    - SU38 excavation complete, confirmation in progress. Currently working SU39.
  - **Phase 6 excavation**
    - Approximately 8,000 cy removed.
  - **Water storage/treatment**
    - Water storage – approximate 850,000 gal stored onsite.
    - Water treatment - 1<sup>st</sup> batch ready for discharge, pending chemical sampling results..
- **Rail Shipments off SLAPS**
  - 64,500 cyds shipped to date / 85,000 planned.




US Army  
Corps of Engineers  
St. Louis District

# Volume Removed Using Environmental Documents



Gateway to Excellence

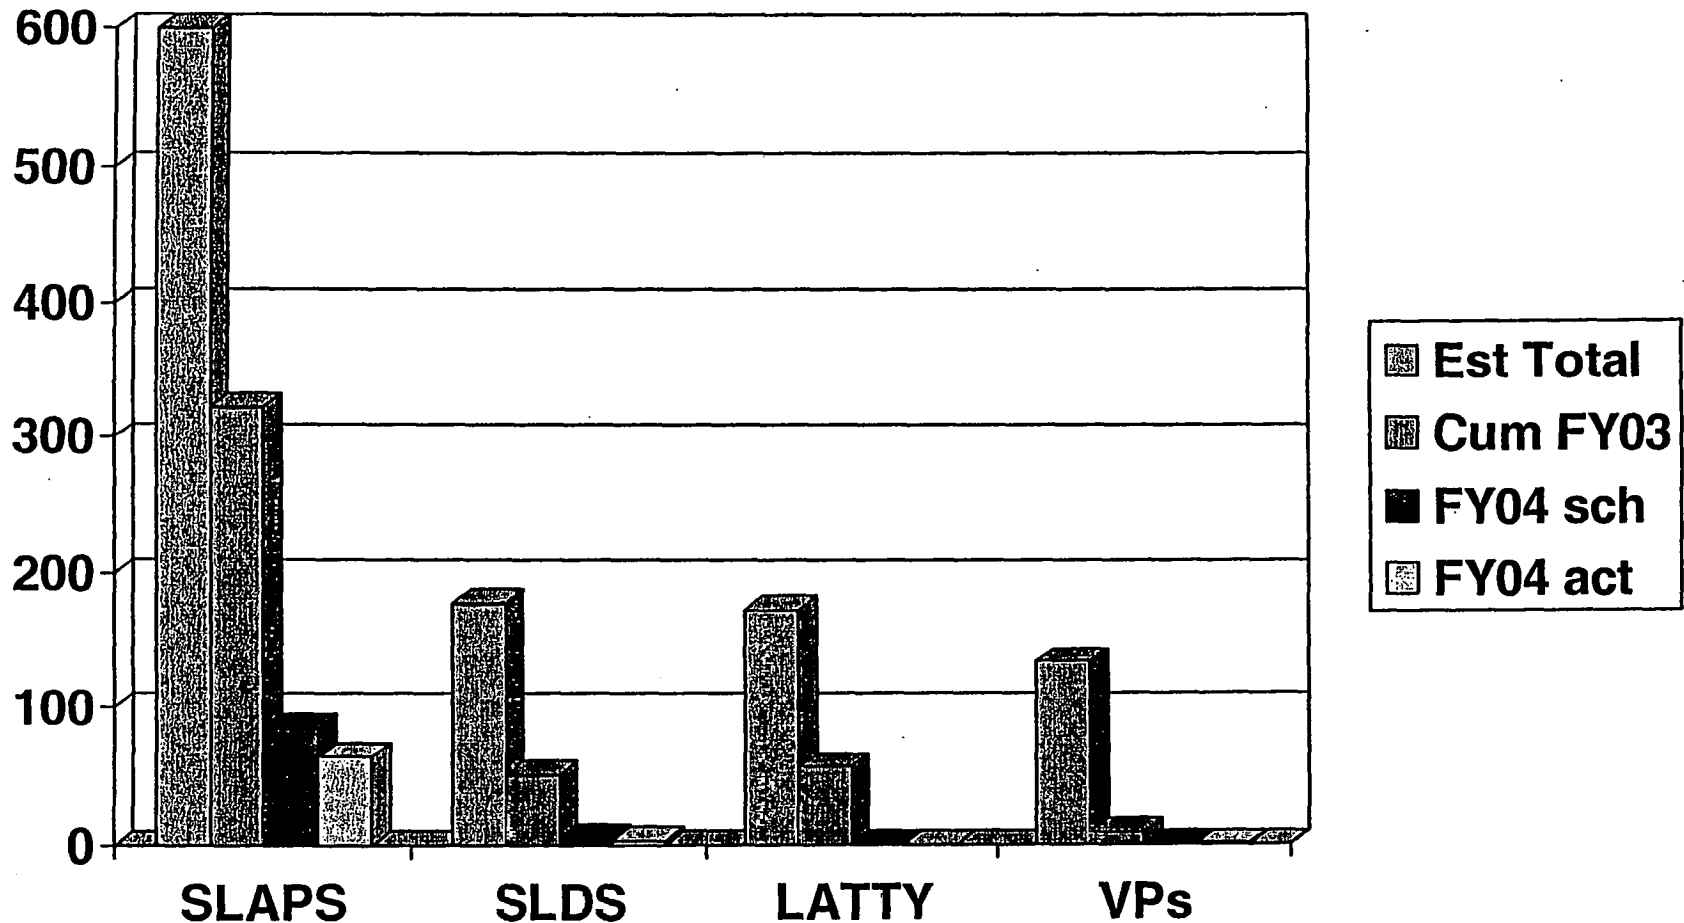

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal


Note 2. SLDS volumes do not include Inaccessibles



US Army  
Corps of Engineers  
St. Louis District

# Progress Report

## Other Issues




Gateway to Excellence

- **New Transportation Regulations**
  - Requested DOT exemption to transport material in gondola cars as is currently done.
- **Long Term Stewardship -**
  - Next meeting 29 July
  - Drafting of the background sections (Site description, History, etc.) of the report is proceeding.
- **North County Haul Road Study**
  - Pending for regulator review.
- **DoE Program POC (Jeff Short)**
  - No interactions during this timeframe
- **CERCLA 5 year Review for all St. Louis FUSRAP Sites**
  - Responses to EPA & MDNR comments under review. Public review 20 days after responses issued.



US Army  
Corps of Engineers  
St. Louis District

# North County ROD Status



Gateway to Excellence


## Current Status

- Comments on the Draft ROD and Responsiveness Summary received from EPA & MDNR on 3 May.
- USACE developing draft responses and red-line document for forwarding to EPA & MDNR 24 May.
- Next step? Meeting in St. Louis 15 & 16 June between EPA, MDNR, USACE.




US Army  
Corps of Engineers  
St. Louis District

# Community Interactions




Gateway to Excellence

- 
- **Recent Events**
    - Incarnate Word (Elementary School) Science Fair on 20 Apr
    - St. Louis Earth Day in Forest Park on 25 Apr
  - **Upcoming Events**
    - St. James Science Fair on May 18
    - Public availability of the Five-Year Review
    - Publish newsletter



US Army  
Corps of Engineers  
St. Louis District

# Taskers



Gateway to Excellence

- **Old Taskers**


- USACE to provide a summary briefing for North County ROD - likely late summer when document closer to final version
- USACE will schedule a time with the DOE Office of Legacy Management to brief the Oversight Committee on Long Term Stewardship (Date / Time TBD)
- Issue current list of members with contact information. (complete)
- Current list of email recipients with identification of the individual associated with each email address. (complete)
- Issue meeting minutes for February (complete).

- **New Taskers**



US Army  
Corps of Engineers  
St. Louis District

# Questions



Gateway to Excellence

**Questions?** **Questions?** **Questions?**  
**Questions?** **Questions?**  
**Questions?** **Questions?**  
**Questions?** **Questions?**  
**Questions?** **Questions?**
