

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

***c/o R. Cavanagh
9011 Manchester
Brentwood, MO 63144
314-313-2959
rcavanagh@ltcop-stl.org***

November 26, 2002

Memorandum

TO: FUSRAP Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh, CHE
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, December 13, 2002, 11:30 am, in the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

**c/o R. Cavanagh
9011 Manchester
Brentwood, MO 63144
314-313-2959
rcavanagh@ltcop-stl.org**

Summary of Meeting
November 8, 2002

Committee Members Present: Sally Price, Tom Manning, Jon Langerak, Ric Cavanagh, Anna Ginsburg

Committee Members Excused: Bill Brandes, Jim Grant, Tom Binz

Other Interested Parties: Sharon Cotner, Lou Dell'Orco, Jack Fraenhoffer, Larry Erickson, Mike Zlatic, Elaine Seele, Jim Mitas

The following comments are in addition to the handouts provided by USACE staff at the meeting.

Page 5 – The permit goes with piles; therefore the project got rid of the permit. GIFREHC will require only 12 workdays, but it will have to be mostly weekend work.

Page 6 – Our site got about \$2 million less than last year so the work is going slower. Sally Price asked if the committee can get the data regarding Uranium in the well at Plant 6. Staff will provide this at the next meeting. Since buildings T, V, and W have been torn down, they are now accessible and must be remediated.

Page 7 – Best case scenario for public hearing on North County ROD is now March, 2003. The next meeting regarding Long Term Stewardship at Weldon Springs is December 5 at 7 pm. The topic is institutional controls. Sharon reported that Reprogramming (moving funds around within the project) is now limited to \$1 million per year (versus 15% previously). This now also means that St. Louis cannot get surplus funds transferred at the end of the fiscal year from other sites. All project budgets are now being funded on Continuing Resolution Appropriations until the new federal budget is approved.

NEXT MEETING

Friday, December 13, 2002
11:30 am
The Trailers on Latty Ave.

Mattingly, Jacqueline MVS

From: Mattingly, Jacqueline MVS

Sent: Tuesday, November 26, 2002 10:39 AM


To: Brandes, Bill; Cavanagh, Richard; Cotner, Sharon; DellOrco, Lou; ensowest@pacbell.net; Erickson, Larry; Fitzgerald, Bill; Frauenhoffer, Jack; Geller, Bob; Gilstrap, Eric; Grant, Jim; Groboski, Jill; Manning, Tom; Marchant, Robert; Meeks, Jacquelynn; Mitas, Jim; Price, Sally; Seele, Elaine; Slaten, Neal; Titus, Jan; Wall, Dan; Wolf, Rick; Zlatic, Michael

Subject: Oversight Committee Meeting Minutes

The next St. Louis Oversight Committee meeting is scheduled for 11:30 a.m. on December 13th at the FUSRAP Project Offices on Latty Avenue. Meeting minutes are being distributed early since I will be out until December 16th.

Have a happy Thanksgiving!

11/26/2002



**U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134**

FROM: Jacque Mattingly

Phone: 314-260-3924

Fax: 314-260-3941

TO: John Langerak


Phone: 314-524-3313

Fax: 314-524-0243

Date: November 26, 2002

No. Pages Including Cover Sheet: 2 ✓

REMARKS:



U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134

FROM: Jacque Mattingly

Phone: 314-260-3924

Fax: 314-260-3941

TO: Anna Ginsburg

Phone: 314-622-4628

Fax: 314-613-3120

Date: November 26, 2002

No. Pages Including Cover Sheet: ~~3~~ 4

REMARKS:



US Army
Corps of Engineers
St. Louis District

FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

8 NOVEMBER 02



November 2002

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

November 2002

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

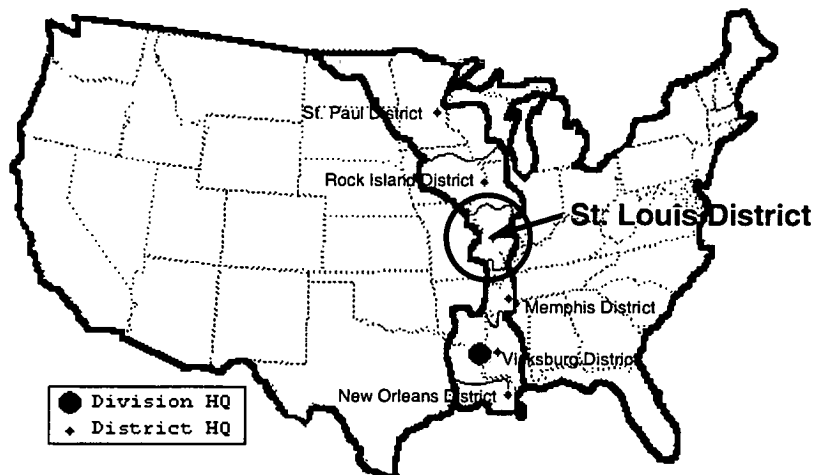

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - **Work Descriptions for Phases 4 / 5 and Phase 6** - Next step is regulator review for Phase 4/5 (after North County ROD). USACE 90% review for Phase 6 has been completed. Work Description will be updated and sent for Regulator Review after Phase 4/5.
- **Removal Actions**
 - **Began Phase I (IA5) excavation 10 DEC 01** - 75,000 cyds expected
 - 63,000 cyds removed to date. Phase 1 removal continues.
 - 3 of the 5 Survey Units have been cleared / backfilled to date, Remaining 2 SU's working.
 - **Removal of the Radium Pits sump area (Survey Unit 21A) is ongoing.**
 - Expect completion within 2 weeks.
 - **Status of water treatment system**
 - **Pilot test**
 - Large scale pilot test (110,000 gallons) which began 9 SEP is pending discharge.
 - Resubmitted the USACE proposed discharge limit for Se to the MDNR for further consideration.
 - Met with the MDNR on 29 August, awaiting response
 - **Rail Shipments off SLAPS**
 - 9,500 cyds shipped to date / 75,000 planned.

November 2002

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - **Requesting removal of NPDES permit at HISS.**
 - Letter sent to MDNR, no response to date. MDNR is looking at our request (29 August meeting).
 - **GIFREHC Roof Replacement**
 - MVS support of the GIFREHC roofing contractor continues. Expect DEC completion.
 - 85% complete. 2,250 cyds removed to date. Roofing contractor estimates that it will take 12 working days to complete from 7 NOV.
 - Some of these days have to be weekends due to the facilities production schedule.
 - **Rail Shipments off HISS**
 - 171 cyds shipped to date / 500 cyds planned
- **SLAPS VP's**
 - **Data Evaluation**
 - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
 - **Designs are on hold and expected to be completed in FY03**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Supporting VP3L/4L property improvement**
 - **Rail Shipments from VP's**
 - 0 planned in FY03

November 2002

5



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **Remedial Investigation** - USACE completed internal draft for the Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - It is currently under internal review.
- **Remedial Design**
 - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Heintz Steel, Gunther Salt, Christiana Ct, Star Bedding, Collins, and Cotto Waxo are currently on hold
 - **Work Descriptions - REV 1's may be issued after PDI re-evaluation**
 - Thomas and Proetz deep soils evaluation results are pending USACE internal review.
 - MVS completed its PDI at McKinley Bridge / City of Venice property, PSC Metals PDI is ongoing.
- **Remedial Action**
 - **Plant 1 - 3,724 cyds remediated**
 - Post Remedial Action Report - data from additional sampling being evaluated.
 - Sampling is being conducted under Buildings T,V and W which were recently torn down by MI.
 - **Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 15,696 cyds remediated to date**
 - Backfill of Phase I ongoing, continuing Phase 3 remediation. Completion date is MAR 03.
 - **VP's - Midwest Waste (4,800 cyds) - 4,750 cyds removed to date, Final status survey and spot excavation is ongoing. 4 of 6 Survey Units cleared for backfill to date. Expect completion in DEC 02.**
 - **Rail Shipments off SLDS**
 - 246 cyds shipped / 13,000 planned.

November 2002

6



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - One remaining major issue exists with the CX OC comments - MVS continues to work on finalizing our position paper
 - CX issue resolution and public review are the next steps.
- **Long Term Stewardship -**
 - Next meeting will be scheduled in the DEC timeframe
 - DOE LTS Meeting for Weldon Spring was held 23 OCT
- **DoE Program POC's interactions -**
 - None at this time
- **FUSRAP Program Review**
 - The USACE FUSRAP Program Review was held 15-17 OCT
- **New MDNR Cooperative Agreement**
 - Working new agreement with the MDNR
- **Funding**
 - Energy and Water Appropriation has not been signed by the President. FUSRAP is currently operating under a Continuing Resolution Authority (CRA)
 - Current CRA is in effect until 22 NOV

November 2002

7




US Army
Corps of Engineers
St. Louis District

Volume Removed Using Environmental Documents



Gateway to Excellence

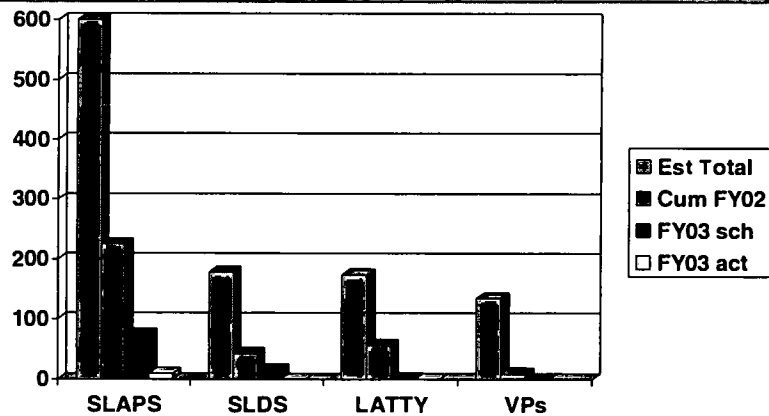

Note 1. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal
Note 2. SLDS volumes do not include Inaccessibles

November 2002

8



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Presentation / Exhibit at Rockwood School District Science Fair on 7 NOV
- **Upcoming Events**
 - Newsletter working towards DEC publication

November 2002

9



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)
 - Speak with Tom Manning to determine if there is any pending redevelopment in the City Of Hazelwood that would be impacted by FUSRAP contamination. (Complete)
- **New Taskers**

November 2002

10



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? **Questions?** **Questions?**
Questions? *Questions?*
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**

November 2002

11

FUSRAP Document Management System

Year ID
00 3705

Further Info?
☐

Operating Unit
St. Louis Sites

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Public Meeting Minutes/Transcripts

Subject or Title
Oversight Committee Meeting November 26, 2002

Author/Originator
Richard Cavanagh

Company
Chairperson

Date
11/26/2002

Recipient(s)
FUSRAP Oversight Com

Company (-ies)

Version
Final

Original's Location
Central Files

Document Format
paper

Confidential File?
☐

Comments

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL
8.10

SAIC number

Filed in Volume
8

Bechtel ID

