LOCK 25 NEW 1200-FT. LOCK MEGA PROJECT - WINFIELD, MO

U.S. ARMY

US Army Corps of Engineers ®
St. Louis District

- FEB 2024 — Phase 2A Award
- MAR 2024 — Phase 1 Complete
- SEP 2024 — Phase 2C Award
- JUL 2025 — Phase 2B Award
- JUN 2026 — Phase 2D Award
- MAR 2027 — Phase 2A Complete
- MAY 2027 — Phase 2B Complete
- SEP 2027 — Phase 2 Award
- OCT 2027 — Phase 2C Complete
- JAN 2028 — Phase 2D Complete
- MAY 2035 — Phase 2 Complete

Legend: Contract / Award Complete

Lockwall Construction Phase 1

- Design ☑
- Acquisition ☑
- Construction ☑

- First construction contract ever on NESP authority
- Contract completed March 2024

Bulkheads Phase 2A

- Design ☑
- Acquisition ☑
- Fabrication 32%

- Required for unwatering & construction of lock floor
- Long lead time item

Downstream Cell Phase 2B

- Design ☑
- Acquisition 66%
- Construction — Not started

- Industry requested navigational aide
- Required before Intermediate wall construction begins
- Design complete 15 AUG 24
- Construction contract advertised 07 JAN 25
- Open bids 07 MAR 25

Construction Operations Facilities Phase 2C

- RFP Development ☑
- Acquisition ☑
- Contractor Design 53%
- Construction — Not started

- Contains QA concrete lab facilities for USACE oversight
- Required to operate & maintain both lock facilities
- Issued Notice to Proceed for design 24 OCT 24

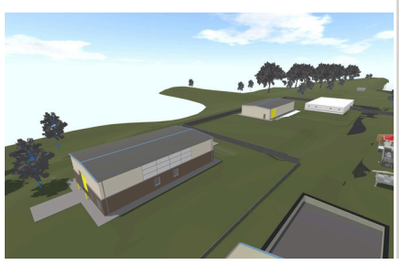

Lock Foundation & Site Prep Phase 2D

- Design 26%
- Acquisition — Not started
- Construction — Not started

- Re-establishes lock foundation post 2012 scour event
- Accelerated contract mitigates one year of schedule risk
- Entering 65% design review phase

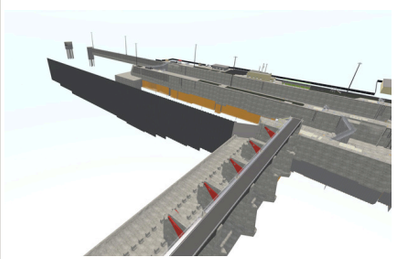

Main Lock Phase 2

- Design 68%
- Acquisition 26%
- Construction — Not started

- 65% design complete
- 65% reviews ongoing
- 95% design ongoing
- 95% cost update ongoing
- Market research for Design Bid Build contract

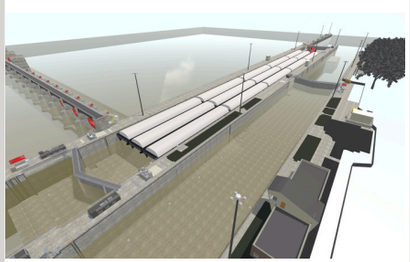

Quarterly Outlook

3rd Quarter FY25:

- 95% design continues
- 65% cost update complete
- Complete boundary surveys
- Begin Real Estate acquisition negotiations

4th Quarter FY25:

- Phase 2 draft plans and specs complete
- 95% Market research initiated
- Contract award of Phase 2B
- Notice to proceed for Phase 2B issued

1st Quarter FY26:

- Phase 2B construction begins
- Phase 2D design complete
- Phase 2 95% design reviews

As of: 10 FEB 25

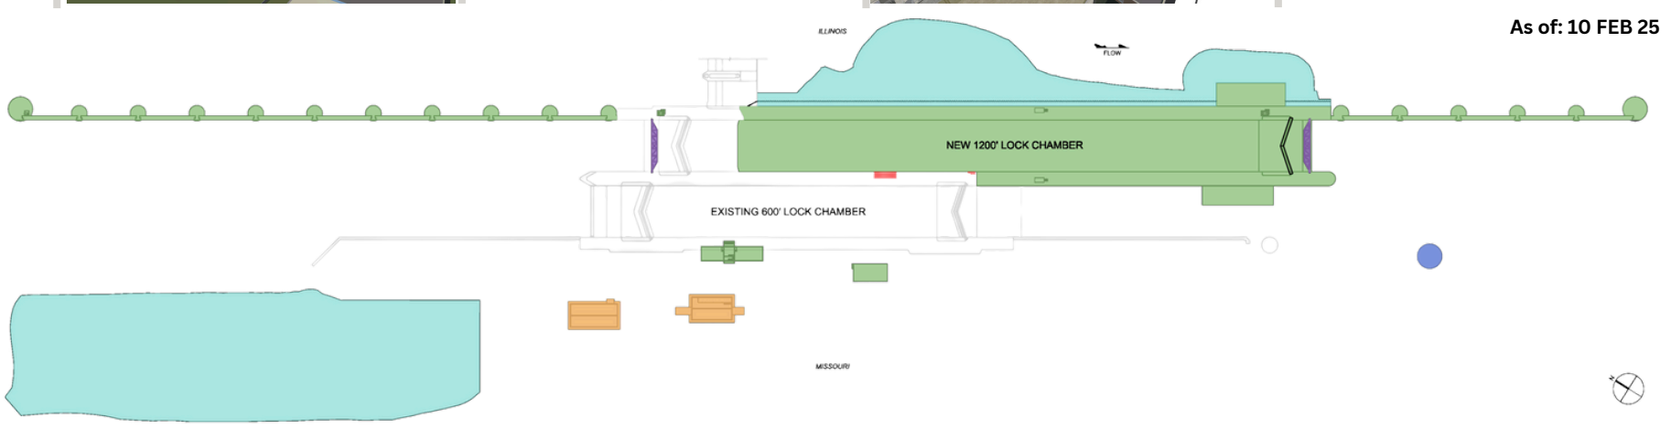

- Lockwall Construction Phase 1
- Bulkheads Phase 2A
- Downstream Cell Phase 2B
- Construction Operations Facilities Phase 2C
- Lock Foundation & Site Preparation Phase 2D
- Main Lock Phase 2
