



US Army  
Corps of Engineers  
St. Louis District

# ***FUSRAP***



Gateway to Excellence

## St. Louis Oversight Committee Meeting *Corps Update*

09 APR 99



April 1999

1

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Capability**
- **Taskers**
- **Questions**

April 1999

2

## Notes

---

---

---

---

---

---

---




US Army  
Corps of Engineers  
St. Louis District

## Mississippi Valley Division



Gateway to Excellence

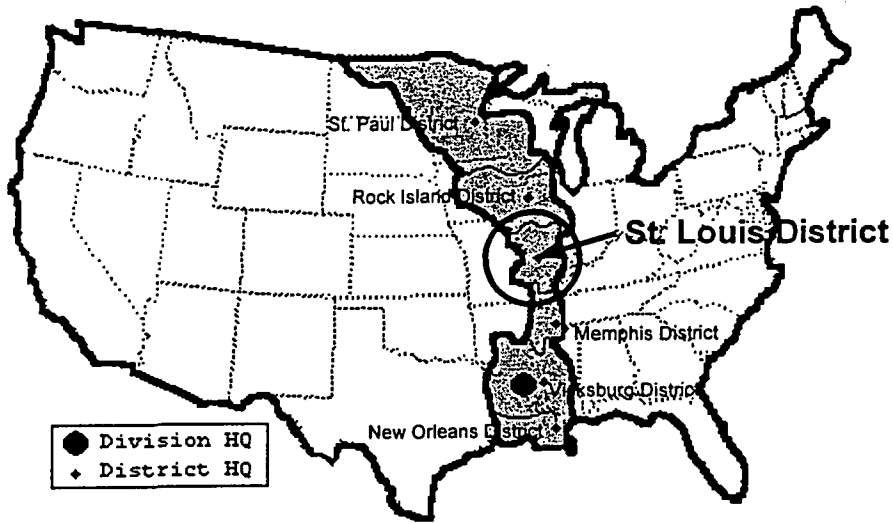

3

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **EE/CA Action Memo/Responsiveness Summary - Distributed**
- **North Ditch / Sedimentation Basin Construction ongoing**
  - Little progress from last meeting due to weather
  - North Ditch (including Sediment Trap) - 16,148 cyds - 63%
  - Sedimentation Basin - 13,978 cyds - 95%
    - Began placing liner week of 22 March
    - Treated and released 900,000 gallons of water - S Ditch
    - Released 2.5 million gallons - N Ditch, S Ditch & East End
- **SLAPS East End Construction ongoing**
  - 8,588 cy by PRAC (Radian) -100%
    - Prepared 800 cyds of asbestos for shipment
  - 20,000 cy by TERC (Stone & Webster) starting 1 JUN 99
    - Negotiating Task Order - RA - partially complete (APR 99)
- **Rail Shipments off SLAPS and Eva**
  - 468 gondola railcars shipped to date (33,228 cyds)

April 1999

4

## Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue



Gateway to Excellence

- **Railspur construction complete**
  - Substantially completed 29 March.
    - Excavation generated two additional covered piles (3,000 & 2,000 cubic yards) on site
  - BNI demobilized from the site
  - SLAPS RA Contractor working on Siding Agreement
- **HISS and Eastern Pile Removal (40,000 cy total).**
  - Finalizing Plans and Specifications for HISS piles
  - RFP to contractor April 30th for Eastern Piles
  - Estimated FY99 removal is 4,000 cy (constrained by funds)
  - Initial start date is July 99

April 1999

5

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report SLAPS Vicinity Properties



Gateway to Excellence

- **Negotiating Laboratory lease and Right-of-Way with several Vicinity Property owners.**
  - SUPERVALU property is being investigated
- **No remediation currently scheduled this fiscal year**
- **Developing remediation strategy**
  - Risk based priorities list by end of FY99.
- **Finalizing release letter for remediated properties.**
  - VP56 (Pershall Road) and St. Denis Bridge
    - Will coincide with PRAR (Post Remedial Action Report)
  - Provided DoE information (ORISE Report, etc..) for VP21(Frost Avenue) to facilitate sale of property.

April 1999

6

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **IT Corp. continues Planning & Design activities**
  - Plant 1 Remedial Design - underway
- **IT Corp remediation efforts**
  - Remediation of City Properties is approximately 98% complete - backfill ongoing. (4,500 cy)
  - Plant 2 began on 6 JAN with slab break up. Subsurface excavation ongoing (8,500) - 20% complete.
- **Partnering Meeting scheduled for 22 APR**
- **Ninety-six gondola cars shipped to date. (6,816 cy)**

April 1999

7

### Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ROD & ARARs**
  - First pass of ARAR's completed - comments from HTRW-CX received
  - PCOC Assessment Memo under internal review
  - ECO risk sampling ongoing - awaiting meeting with USEPA
  - Land use designation under CoE review
  - Definition of operable units
  - Definition of inaccessible soils (Through sampling)
- **COE/DOE Memorandum of Understanding**
  - Finalized on 17 March
- **Nationwide Disposal Contract**
  - Award in May

April 1999

8

## Notes

---

---

---

---

---

---

---





US Army  
Corps of Engineers  
St. Louis District

## Community Interactions



Gateway to Excellence

- **Recent Events**

- KMOV Channel 4 Allman Report visits SLAPS
  - Based on concerns of Kay Drey. An individual within the site took pictures and forwarded them to Kay who called Channel 4. Pictures showed nothing out of the ordinary.
  - Follow up letter to MDNR, from Kay Drey, was received 7 APR
- Hazelwood High School Physics Class Presentation
- USACE Technical Conference Presentations
  - Community Relations (w/ Mr. Cavanagh), Lessons Learned, Data Management, Risk Assessment, Precision Excavation, Three Dimensional Geospatial Modelling, Field Screening and Synergistic Transportation & Disposal
  - Conference was opened to contractors, regulators at last minute

- **Upcoming Events**

- FUSRAP Model on Display at Clay School (15 Apr-19 May)
- Real Life Adventures in Science Day at St. Louis District

April 1999

9

## Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Taskers



Gateway to Excellence

- **Old Taskers**

- Information on DoE/CoE MOU to Mr. Cavanagh (Complete)
  - MOU signed 17 March
- Funding Letter to Chairman Packard via Mr. Cavanagh and Mr. Horgan (Complete)
- Research SUPERVALU ground for laboratory location per Mr. Manning (Complete)
- List of Nationwide Disposal Contract Bidders (Not Complete - bidders names not releasable until award - will furnish names upon award)
- Participation at Air & Waste Management Conference - Mr. Binz lead (No further action)

- **New Taskers**

April 1999

10

## Notes

---

---

---

---

---

---

---



US Army  
Corps of Engineers  
St. Louis District

## Questions



Gateway to Excellence

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

8-Apr-99 April 1999

11

## Notes

---

---

---

---

---

---

---
