

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, MO 63105

314.615.1635

Ric_Cavanagh@Stlouisco.com

MEMORANDUM

TO: Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh, CHE
Chairperson

RE: Next Meeting

The next meeting of the St. Louis FUSRAP Oversight Committee will be held on Friday, March 8, 2002, 11:30 am, in the trailers on Latty Ave.

Committee members who cannot attend should contact the Chairperson at the above numbers to be excused.

Thank you.

:RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 111 So. Meramec

Clayton, MO 63105

314.615.1635

Ric_Cavanagh@Stlouisco.com

Meeting Summary

February 8, 2002

Committee Members Present: Jon Langerak, Tom Manning, Jim Grant, Ric Cavanagh, Jan Titus, Tom Binz, and Sally Price

Committee Members Excused: Bill Brandes

Other Interested Parties: Jack Frauenhoffer, Jim McCord, Elaine Seele, Eric Gilstrap, Larry Erickson, Mike Zlatic, Lou Dell'Orco, Sharon Cotner

The following is a summary of information provided in addition to the handouts provided by USACE.

Page 4 - The project is approaching a point in a few months where work will be on hold until the ROD is approved.

Page 6 - USACE is working through internal channels to determine how to handle properties whose owners have indicated by letter that they do not want their properties remediated. (There is a need to be consistent in handling these cases throughout the country). SLDS Remedial Design is on hold due to lack of funds. Given the dollars available, the project will soon be down to only one crew at SLDS.

Page 7 - Long Term Stewardship (LTS) committee has discussed the use of Overlay Districts to address the issue of documenting that certain properties have not been cleaned up to unrestricted use criteria. This process could be handled by local municipalities or counties and would work within the regular zoning laws. It would not require changes in ordinances nor formal deed restrictions on properties.

Page 11 - SOR stands for sum of ratios

Page 16 - Sharon clarified that ERC contractor does not do final status survey.

Discussion of Clean Up criteria: Staff do not feel that USACE's legal interpretation of clean up standards is consistent with previous NRC standards. The conflict with the Center of Excellence (CX) continues. CX and legal want to use the Linde site criteria, which would not meet the expectations of the Task Force Report. Larry Erickson of MDNR indicated that several other sites disagree with using these criteria. Unfortunately, both USACE Headquarters and CX counsel disagree with St. Louis' view.

The EPA has a great deal of influence, ultimately, in determining what standards are used and are prone to support the desires of the local site. However, resolution of this disagreement could take as long as two years, severely restricting clean up in North County for that time period.

Next Meeting

Friday, March 8, 2002

11:30 am

Trailers on Latty Ave.



US Army
Corps of Engineers
St. Louis District

FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting Corps Update

8 MARCH 02



March 2002

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Excavation to Backfill Process**
- **Taskers**
- **Questions**

March 2002

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

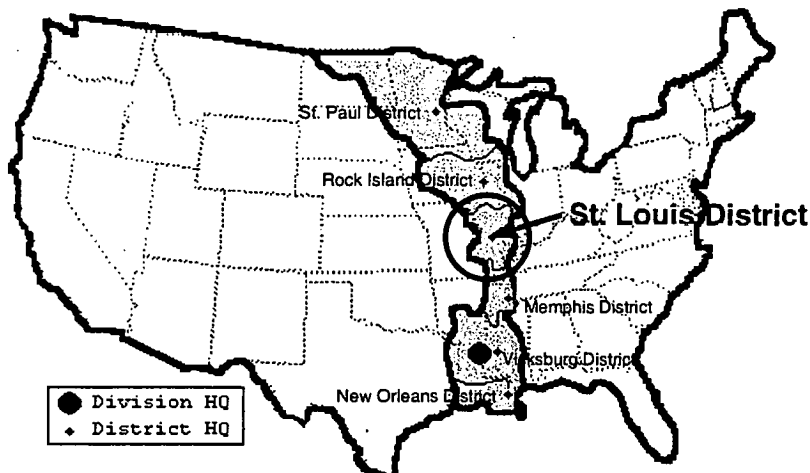

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Investigation**
 - Walkover of Airport Authority property S of Banshee Road pending
- **Remedial Design**
 - **Work Description for Phases 4 / 5** - 60% under internal MVS review, hold at 90%
 - Addendum 1 for the portion of Coldwater Creek adjacent to 4/5 is pending.
 - **Work Description for Phase 6** - 60% due in APR, hold at 90% this FY.
- **Removal Actions**
 - **Began Phase I (IA5) excavation 10 DEC** - 43,000 cyds expected
 - 14,334 cyds removed to date. Phase 1 has been removed to 1' above the water table.
 - 1,000 cyds have been removed from SU 14 - 50% complete, SU 22 is next.
 - Need to relocate site support trailers to east end before further removals can take place.
 - **Status of water treatment system** - Bench test was completed - did not meet standard.
 - Contractor was defaulted. Working on next course of action.
 - **MVS and MDNR FFS met with MDNR Water Pollution Control 17 DEC**
 - Received approval for removal of Outfall 3 from SLAPS permit equivalent and reduced sampling on Outfall 2 due to remediation completed to date.
 - **Rail Shipments off SLAPS**
 - 32,467 cyds shipped to date / 50,000 planned.

March 2002

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - Meeting with MDNR Water Pollution Control on sampling at HISS today.
 - **GIFREHC Roof Replacement**
 - MVS support of the GIFREHC roofing contractor will resume @ 18 MAR.
 - 8 of 63 areas removed to date. 4,000 cyds are expected. 300 removed to date
 - **Rail Shipments off HISS**
 - 3301 cyds shipped to date / 5,000 cyds planned
- **SLAPS VP's**
 - **Data Evaluation**
 - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
 - **Designs are on hold and expected to be completed in FY03**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Supporting Pershall Utility / I-170 MoDoT work**
 - No contamination above criteria was identified:
 - In Pershall east of the Hazelwood / Pershall intersection for the I-170 MoDoT work.
 - In the shoulders of Pershall west of the Hazelwood / Pershall intersection in support of the Missouri American Water Line Utility support.
 - **Supporting proposed property improvements at VP 24 and 56/57.**

March 2002 Sample results show some contamination at 24, MVS is currently bounding.

- 56/57 cleared for installation of a fire suppression system.

5



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **No remediation letters** - Working issue within the Corps. Meeting with Thomas and Proetz next week.
- **Remedial Investigation** - USACE assembling data for Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - Internal USACE draft is under review.
- **Remedial Design**
 - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Christiana, Star Bedding, Collins, Cotto Waxo and Thomas / Proetz Lumber are currently on hold
 - **Work Descriptions - REV 1's may be issued after PDI re-evaluation**
 - PSC Metals, Heintz Steel, Thomas and Proetz and McKinley Bridge deep soils evaluation working. Also working additional PDI issues at McKinley Bridge.
- **Remedial Action**
 - **Plant 1 continues (@3,750 cyds) - 3,724 cyds remediated to date**
 - Remediation is complete. Authorization to backfill is pending on area 7/8w.
 - **Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 13,304 cyds remediated to date**
 - Excavation and backfill of Phase I Survey Units continues. Completion date is DEC 02.
 - **VP's - Midwest Waste (4,500 cyds) - 4,322 cyds removed to date, spot excavation is ongoing. Expect completion in MAY 02.**
 - **ADM (DT-1) - Final Status Survey is under internal review.**
 - **Rail Shipments off SLDS**
 - 8,784 cyds shipped / 15,000 planned

March 2002

6



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - USACE comments, including OC in the HTRW-CX, have been received and the responses are being finalized. Issues exist with the CX OC comments - MVS working response
 - CX issue resolution and FS/PP regulator review are the next steps.
- **Long Term Stewardship - Next meeting is 21 MAR**
 - Meeting was held 24 JAN. LTS document development is ongoing
 - DoE may be coming to view site next week - pending scheduling issues
- **DoE Program POC's interactions -**
 - None during this timeframe
- **The Army Audit Agency continues their audits**
 - Audit 1 - Final copy has been released at the HQ level, expect receipt next week at the site
 - Audit 2 - Draft for internal USACE comment expected in MAR 02.
- **Met with MDNR on out years funding 4 MAR**
- **Possible strike averted at MI on 1 MAR**
- **MVS SLDS TERC (IT Corp) -** Company is in the process of being purchased, most likely by the Shaw Group. Site operations have not been affected to date.

March 2002

7




US Army
Corps of Engineers
St. Louis District

FY 02 Volume Shipped Using Environmental Documents



Gateway to Excellence

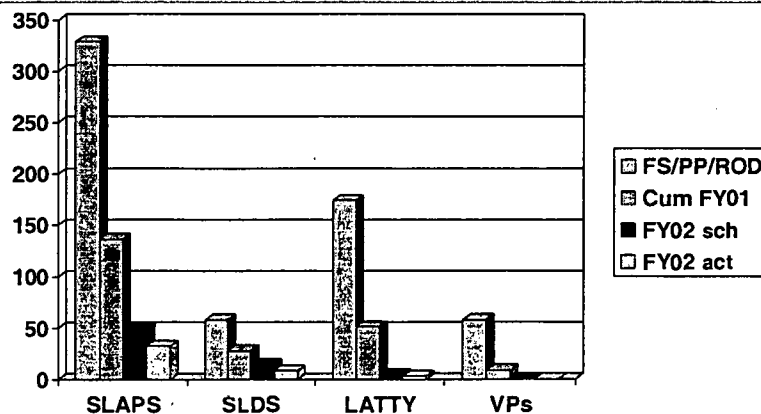

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are EXSITU. EXSITU volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include inaccessible

March 2002

8



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**
 - Newsletter Published - FEB 02
 - Briefed at Incarnate Word Science Olympiad - 28 FEB
- **Upcoming Events**
 - None at this time.

March 2002

9



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**
 - Put the updated maps of the Phases of SLAPS and properties at SLDS in the next newsletter (Complete)
 - The Oversight Committee will meet to discuss how to increase public awareness on clean up standards and LTS (Ongoing - Meeting held)
 - Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)
- **New Taskers**

March 2002

10



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

Questions?

March 2002

11

FUSRAP Document Management System

Year ID
00 3084

Further Info?
☐

Operating Unit
St. Louis Sites

Site

Area

MARKS Number
FN:1110-1-8100g

Primary Document Type
Public Affairs/Community Relation

Secondary Document Type
Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Meeting Minutes from February 8, 2002 Meeting

Author/Originator
Richard Cavanagh

Company
St. Louis County DOH

Date
3/1/2002

Recipient(s)
Distribution

Company (-ies)

Version
Final

Original's Location
Central Files

Document Format
Paper

Confidential File?
☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

- ☒ North County
- ☐ Madison
- ☐ Downtown
- ☐ Iowa

ETL
8.10

Filed in Volume
8

