

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

c/o 8945 Latty Ave.

Berkley, MO 63134

314.260.3924

Jacqueline.Mattingly@mvs02.usace.army.mil

October 4, 2002

MEMORANDUM

TO: Oversight Committee Members
Other Interested Parties

FROM: Richard R. Cavanagh
Chairperson

RE: Next Meeting

The next meeting of the FUSRAP Oversight Committee will be held on Friday, October 11, 2002, in the trailers on Latty Ave, at 11:30 am.

Committee members who cannot attend should contact the Chairperson at the above numbers or at his office (314-918-8222) to be excused. Please note the change in mailing address, phone number, and e-mail address for the Committee.

Thank you.

.RRC

ST. LOUIS FUSRAP OVERSIGHT COMMITTEE

**c/o 8945 Latty Ave.
Berkeley, MO 63134
314.260.3924**

Jacqueline.Mattingly@mvs02.usace.army.mil

**Summary of Meeting
September 13, 2002**

Committee Members Present: Jim Grant, Ric Cavanagh, Sally Price, Tom Manning, Jan Titus, Jon Langerak

Other Interested Parties: Jack Fraenhoffer, Mike Zlatic, Eric Gilstrap, Joan Reading, Sharon Cotner, Bob Marchant

The following comments are in addition to the information in the handouts provided by USACE at the meeting.

Page 4 – We will likely exceed the 55,000cyd expectation this year. Water treatment is the key issue. USACE met with DNR on 8/29 regarding permitting for water treatment. DNR will respond within 30 days.

Page 5 – DOE remediation assessment is a low priority. VP 22 – the Corps approved replacement of the concrete pad (copy of letter distributed to Committee).

Page 6 – Remedial design on hold due to funding restrictions. Corps has met with Mallinckrodt regarding de-commissioning.

Page 7 – North County ROD: apparently the decision on clean up criteria will be made by Division office in Vicksburg. They will need to be educated about St. Louis community needs and expectations. In a related matter, New Jersey has established very restrictive clean up standards. This may set a good precedent for our project.

**NEXT MEETING
Friday, October 11, 2002
11:30am**

Mattingly, Jacqueline MVS

From: Mattingly, Jacqueline MVS

Sent: Thursday, October 10, 2002 7:32 AM

To: Brandes, Bill; Cavanagh, Richard; Cotner, Sharon; DellOrco, Lou; ensowest@pacbell.net; Erickson, Larry; Fitzgerald, Bill; Frauenhoffer, Jack; Geller, Bob; Gilstrap, Eric; Grant, Jim; Groboski, Jill; Manning, Tom; Marchant, Robert; Meeks, Jacquelynn; Mitas, Jim; Price, Sally; Seele, Elaine; Slaten, Neal; Titus, Jan; Wall, Dan; Wolf, Rick; Zlatic, Michael

Subject: Oversight Committee Meeting Minutes

Good morning!

The subject meeting minutes are attached. The next meeting is scheduled for this Friday, October 11, 2002, at the FUSRAP Project Offices at 8945 Latty Avenue.

See you soon!

For to

Redacted - Privacy Act

John Langerak

Ⓢ 524-0243

Redacted - Privacy Act

Anna Linsburg

Ⓢ 622-4398


Redacted - Privacy Act

Tom Bing

Ⓢ 892-6132

~~Karen Burke?~~

10/10/2002



U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134

FROM: *Jacque Mattingly*

Phone: *260-3924*

Fax: *260-3941*

TO: *Anna Ginsburg*


Phone: *Redacted - Privacy Act*

Fax: *~~622-4398~~ 613-3120*

Date: *10/10/02*

No. Pages Including Cover Sheet: *3*

REMARKS:



U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134

FROM: *Jacque Mattingly*

Phone: 260-3924

Fax: 260-3941

TO: *John Langerak*


Phone: Redacted - Privacy Act

Fax: 524-0243

Date: *October 10, 2002*

No. Pages Including Cover Sheet: *3*

REMARKS:



U. S. Army Corps of Engineers
St. Louis District - FUSRAP Project Office
8945 Latty Avenue
Berkeley, Missouri 63134

FROM: *Jacque Mattingly*

Phone: *260-3924*

Fax: *260-3941*

TO: *Tom Bing*

Redacted - Privacy Act

Phone:

Fax: *892-6132*

Date: *10/10/02*

No. Pages Including Cover Sheet: *3*

REMARKS:

1



US Army
Corps of Engineers
St. Louis District


FUSRAP



Gateway to Excellence

St. Louis Oversight Committee Meeting *Corps Update*

13 SEPTEMBER 02

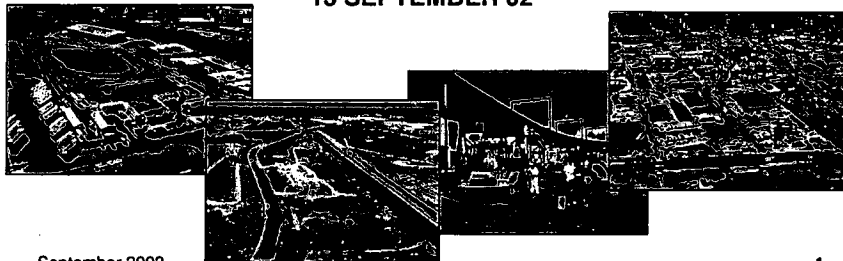

September 2002

1



US Army
Corps of Engineers
St. Louis District

Agenda



Gateway to Excellence

- **Mississippi Valley Division**
- **Progress Report**
- **Community Interactions**
- **Taskers**
- **Questions**

September 2002

2




US Army
Corps of Engineers
St. Louis District

Mississippi Valley Division



Gateway to Excellence

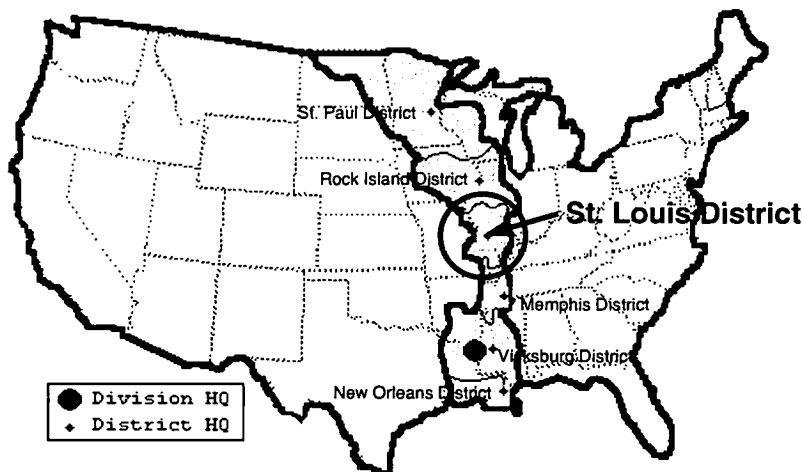

3



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Airport Site (SLAPS)



Gateway to Excellence

- **Remedial Design**
 - **Work Descriptions for Phases 4 / 5 and Phase 6** - Next step is regulator review for Phase 4/5 (after North County ROD) and USACE 90% review for Phase 6. Phase 6 is currently being coordinated with the railroad.
- **Removal Actions**
 - **Began Phase I (IA5) excavation 10 DEC 01** - 55,000 cyds expected
 - 51,179 cyds removed to date. Phase 1 removal continues.
 - 2 of the 5 Survey Units have been cleared, 1 is under Final Status Survey
 - Removal of the Radium Pits sump area (Survey Unit 21A) is next.
 - **Status of water treatment system** - Pilot test and Bench test status
 - Pilot scale test (15,000 gallons) for water treatment - Ongoing for batch 5 of 7. Se levels met MSD discharge limits for the first 4 tests. Test 5 is ongoing.
 - Large scale pilot test (130,000 gallons) began 9 SEP to see if we can treat a large volume of water in a small amount of time.
 - Bench tests - results @ 30 SEP (This will provide a determination if we can (1) reduce the need to haul sludge for each test or (2) if a two stage process is more effective for the treatment of Se.
 - Continuing to use Best Management Practices at the site for water management
 - Resubmitted the USACE proposed discharge limit for Se to the MDNR for further consideration.
 - Met with the MDNR on 29 August, expect a response within the next month.
 - **Rail Shipments off SLAPS**
September 2002 70,177 cyds shipped to date / 50,000 planned.

4



US Army
Corps of Engineers
St. Louis District

Progress Report Hazelwood Interim Storage Site (HISS)/Latty Avenue / SLAPS VPS



Gateway to Excellence

- **HISS / Latty Avenue**
 - **Requesting removal of NPDES permit at HISS.**
 - Letter sent to MDNR, no response to date. MDNR is looking at our request (29 August meeting).
 - **GIFREHC Roof Replacement**
 - MVS support of the GIFREHC roofing contractor resumed 18 MAR.
 - 60% complete. 2,100 cyds removed to date. Expected to be complete by Christmas
 - **Rail Shipments off HISS**
 - 5,030 cyds shipped to date / 5,000 cyds planned
- **SLAPS VP's**
 - **Data Evaluation**
 - Assessment of the 30 DoE remediated properties. Finalizing response to comments.
 - **Designs are on hold and expected to be completed in FY03**
 - 56/57/58/59/1C & Pershall & I-270 ROW + 9/10/11/12 & Ballfield hotspots
 - **Working with VP22 on a proposed concrete pad replacement**
 - The area for the pad was cleared by USACE, report is pending
 - **Provided radiological support recently to a VP 37 chemical spill**
 - **Rail Shipments from VP's**

September 2002 - 0 planned, 120 cyds complete

5



US Army
Corps of Engineers
St. Louis District

Progress Report St. Louis Downtown Site (SLDS)



Gateway to Excellence

- **No remediation areas** - Working path forward within the Corps.
- **Remedial Investigation** - USACE completed internal draft for the Groundwater Remedial Action Alternatives Assessment due to high levels of U in well at Plant 6W - It is currently under internal review.
- **Remedial Design**
 - **Pre Design Investigation** - Mallinckrodt West, Plant 7N/7S, Heintz Steel, Gunther Salt, Christiana Ct, Star Bedding, Collins, and Cotto Waxo are currently on hold
 - **Work Descriptions - REV 1's may be issued after PDI re-evaluation**
 - Thomas and Proetz deep soils evaluation results are under review.
 - MVS is completing its PDI at McKinley Bridge / City of Venice property, PSC Metals is next.
- **Remedial Action**
 - **Plant 1 - 3,724 cyds remediated**
 - Post Remedial Action Report - data from additional sampling being evaluated.
 - **Plant 6E / 6E1/2 (27,000 cyds) began 3 DEC 00 - 15,376 cyds remediated to date**
 - Backfill of Phase I ongoing, continuing Phase 3 remediation. Completion date is MAR 03.
 - **VP's - Midwest Waste (4,750 cyds)** - 4,557 cyds removed to date, Final status survey and spot excavation is ongoing. 2 of 6 Survey Units cleared for backfill to date. Expect completion in DEC 02.
 - **Rail Shipments off SLDS**
 - 10,992 cyds shipped / 15,000 planned.
- **IT Corporation is relocating its on site offices from Plant 7 to Midwest Waste**

September 2002

6



US Army
Corps of Engineers
St. Louis District

Progress Report Other Issues



Gateway to Excellence

- **North County Feasibility Study/ Proposed Plan**
 - One remaining major issue exists with the CX OC comments - MVS continues to work on finalizing our position paper
 - CX issue resolution and public review are the next steps.
- **Long Term Stewardship -**
 - Next meeting will be scheduled in the NOV / DEC timeframe
- **DoE Program POC's interactions -**
 - None at this time
- **The Army Audit Agency - Awaiting final audit**
 - Audit 2 FUSRAP Disposal Actions - USACE comments were furnished to AAA in MAY 02.
- **FUSRAP Program Review**
 - The next USACE program Review is 15-17 OCT

September 2002

7




US Army
Corps of Engineers
St. Louis District

FY 02 Volume Shipped Using Environmental Documents



Gateway to Excellence

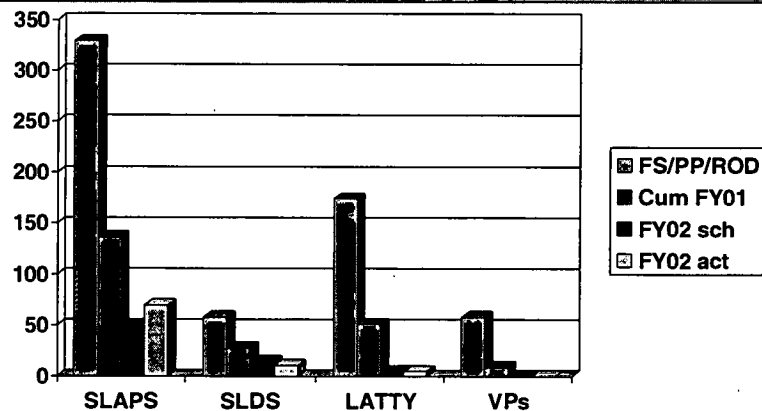

Note 1. North County volumes are based on the North County FS/PP

Note 2. All volumes are exsitu. Exsitu volume = Insitu volume plus 20% for excavation and 25% for swell prior to Transportation and Disposal

Note 3. SLDS volumes do not include Inaccessibles

September 2002

8



US Army
Corps of Engineers
St. Louis District

Community Interactions



Gateway to Excellence

- **Recent Events**

- Workshop for North County FS/PP - 13 and 20 August
 - Held at the Hazelwood Civic Center located at 8969 Dunn Road in Hazelwood. (314) 839-5575
 - 6 - 9 pm each evening
- Brief at Small Business Training Conference on 28 AUG.

- **Upcoming Events**

- Attend North Broadway Business Association Meeting in SEP

September 2002

9



US Army
Corps of Engineers
St. Louis District

Taskers



Gateway to Excellence

- **Old Taskers**

- The Oversight Committee will meet to discuss how to increase public awareness on clean up standards and LTS (Complete - Workshops held)
- Provide the Oversight Committee a briefing on the FS/PP when appropriate (Working)

- **New Taskers**

September 2002

10



US Army
Corps of Engineers
St. Louis District

Questions



Gateway to Excellence

Questions? **Questions?** **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**
Questions? **Questions?**

September 2002

11

FUSRAP Document Management System

Year ID

00 3398

Further Info?

☐

Operating Unit

St. Louis Sites

Site

Area

MARKS Number

FN:1110-1-8100g

Primary Document Type

Public Affairs/Community Relation

Secondary Document Type

Public Meeting Minutes/Transcripts

Subject or Title

St. Louis Oversight Committee Briefing and Meeting Minutes from the 9/13/02 meeting

Author/Originator

Richard Cavanagh

Company

Oversight Committee

Date

10/4/2002

Recipient(s)

Distribution

Company (-ies)

Version

Final

Original's Location

Central Files

Document Format

Paper

Confidential File?

☐

Comments

SAIC number

Bechtel ID

Include in which AR(s)?

☒ North County

☐ Madison

☐ Downtown

☐ Iowa

ETL

8.10

Filed in Volume

8

